

WEEKLY PROJECT REPORT-031



Picture Taken : 18 Apr 2012

AS ON 18 APR 2012

PROJECT SUMMARY AS ON: 18 APR 2012

- Program is 63 days delayed from master program as on 18th Apr 2012. Still delay time is increasing and 5 days more lag in 7th floor roof slab casting. But it should be controlled.
- Still no signature by MEP in Work Inspection Request (WIR) before slab casting.
- Manpower is same as before.
- Tool Box Meeting (Safety Meeting) with picture and Visitor Safety Instruction are attached.

WEEKLY CHECK-LIST FOR **PROGRAM** AS ON: 18-04-12



Name of Sub-Contractor:	Sohel Enterprise
--------------------------------	------------------

WBS					
Task Name	8th floor Roof beam & slab casting				
Schedule Finish	10/02/2012	Actual Finish:	13/04/2012	Time Lag:	63
Causes of Delay					

WBS					
Task Name	8th floor Roof beam and Slab shuttering complete				
Actual Start		Actual Finish:	12/04/2012	Time Lag:	
Causes of Delay					

WBS					
Task Name					
Actual Start		Actual Finish:	24/02/2012	Time Lead/Lag:	
Causes of Delay					

WBS					
Task Name					
Actual Start		Actual Finish:		Time Lead/Lag:	
Causes of Delay					

WBS					
Task Name					
Actual Start		Actual Finish:		Time Lead/Lag:	
Causes of Delay					

Remarks: (Penalty/ Award) to be filled by Project Incharge

Suggestion/ Advice:

Slab is delayed 63 days from master program as on 18th April 2012. which is much 5 days more than previous slab casting. See attached graph.

 Consultant


 Chief Engineer

Project Incharge

Chief Engineer

Director

Delay of Roof Slab Casting

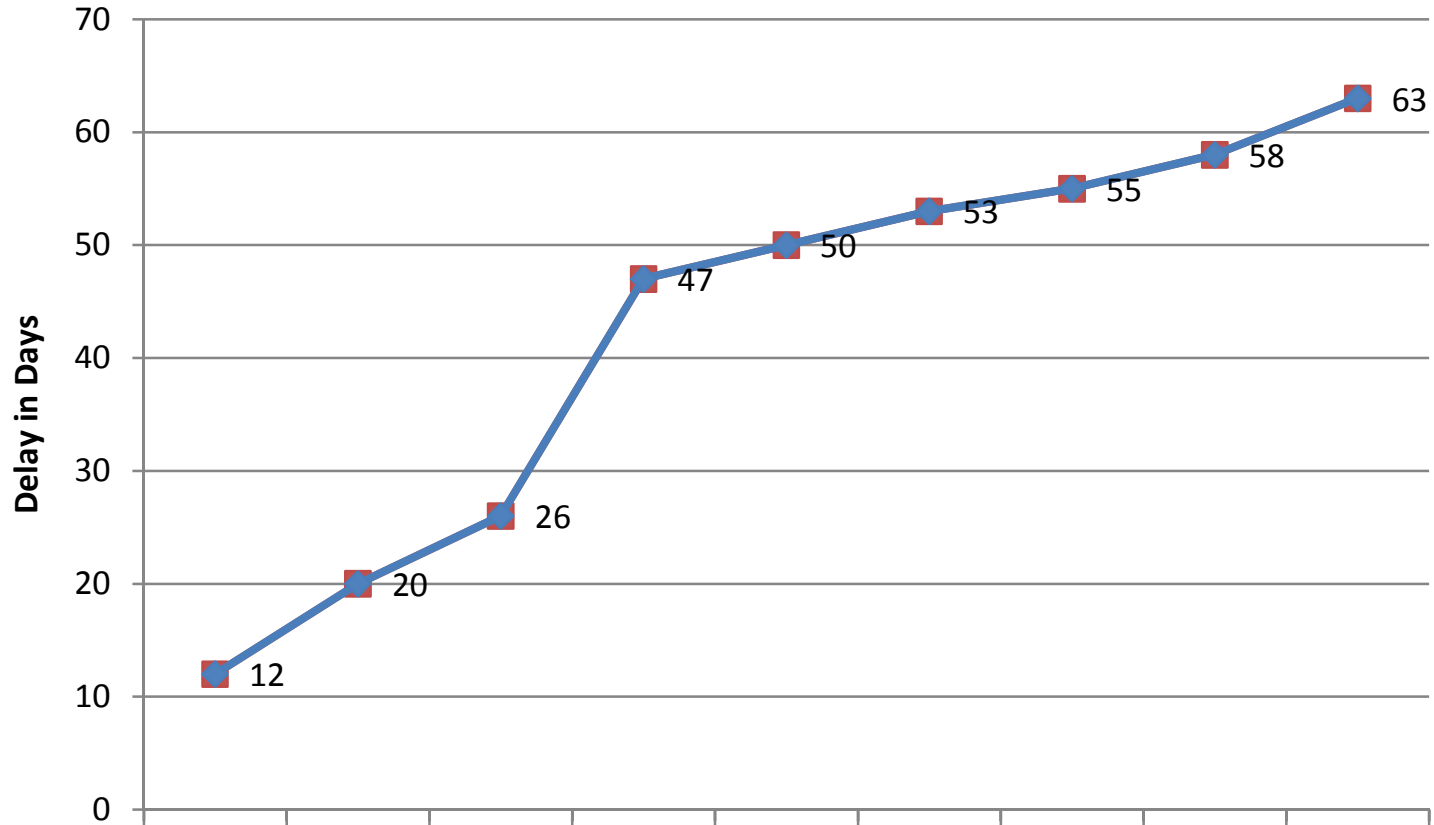

Actual Finish	29/08/11	02/10/11	28/10/11	09/12/11	07/01/12	31/01/12	24/02/12	18/03/12	13/04/12
Schedule Finish	17/8/11	12/9/11	2/10/11	23/10/11	18/11/11	9/12/11	31/12/11	20/1/12	10/2/12
	Ground Floor	1st Floor	2nd Floor	3rd Floor	4th Floor	5th Floor	6th Floor	7th Floor	8th Floor

Ekushey Bhaban-Superstructure-Progress

Sl.	Task Name	Duration	Start	Finish	Actual Finish	% Compl	Jan '12				Feb '12				Mar '12				Apr '12							
							01/01	08/01	15/01	22/01	29/01	05/02	12/02	19/02	26/02	04/03	11/03	18/03	25/03	01/04	08/04	15/04	22/04			
1	Ekushey Bhaban	442 d	28/07/11	18/11/12	NA	5%	18/04/12																			
1.1	Superstructure	300 d	28/07/11	14/06/12	NA	63%																				
1.1.1	Ground Floor	20 d	28/07/11	17/08/11	29/08/11	100%																				
1.1.2	1st Floor	20 d	18/08/11	12/09/11	02/10/11	100%																				
1.1.3	2nd Floor	20 d	13/09/11	02/10/11	28/10/11	100%																				
1.1.4	3rd Floor	20 d	03/10/11	23/10/11	09/12/11	100%																				
1.1.5	4th Floor	20 d	24/10/11	18/11/11	07/01/12	100%																				
1.1.6	5th Floor	20 d	19/11/11	09/12/11	31/01/12	100%																				
1.1.7	6th Floor	20 d	10/12/11	31/12/11	24/02/12	100%																				
1.1.8	7th Floor	20 d	01/01/12	20/01/12	18/03/12	100%																				
1.1.9	8th Floor	20 d	21/01/12	10/02/12	18/04/12	100%																				
1.1.9.1	Layout Work	1 d	21/01/12	21/01/12	NA	100%																				
1.1.9.2	Column (17 nos): Lift-1	4 d	22/01/12	25/01/12	NA	100%																				
1.1.9.3	Column (17 nos): Lift-2	4 d	26/01/12	29/01/12	NA	100%																				
1.1.9.4	Lift Core: Lift-1	5 d	22/01/12	26/01/12	NA	100%																				
1.1.9.5	Lift Core: Lift-2	4 d	27/01/12	30/01/12	NA	100%																				
1.1.9.6	Stair Case (2 nos)-Flight-1	8 d	23/01/12	30/01/12	NA	100%																				
1.1.9.7	Stair Case (2 nos)-Flight-2	8 d	02/02/12	10/02/12	NA	100%																				
1.1.9.8	Roof Slab	10 d	31/01/12	10/02/12	18/04/12	100%																				
1.1.9.8.1	Formwork	5 d	31/01/12	04/02/12	NA	100%																				
1.1.9.8.2	Re-bar	3 d	05/02/12	08/02/12	NA	100%																				
1.1.9.8.3	MEP Work	2 d	08/02/12	09/02/12	NA	100%																				
1.1.9.8.4	Inspection	1 d	09/02/12	09/02/12	NA	100%																				
1.1.9.8.5	Concrete	1 d	10/02/12	10/02/12	18/04/12	100%																				
1.1.10	9th Floor	20 d	11/02/12	02/03/12	NA	22%																				
1.1.10.1	Layout Work	1 d	11/02/12	11/02/12	NA	100%																				
1.1.10.2	Column (17 nos): Lift-1	4 d	12/02/12	15/02/12	NA	100%																				
1.1.10.3	Column (17 nos): Lift-2	4 d	16/02/12	19/02/12	NA	0%																				
1.1.10.3.1	Re-bar	1 d	16/02/12	16/02/12	NA	0%																				
1.1.10.3.2	Formwork	2 d	17/02/12	18/02/12	NA	0%																				
1.1.10.3.3	Concrete	1 d	19/02/12	19/02/12	NA	0%																				
1.1.10.4	Lift Core: Lift-1	5 d	12/02/12	16/02/12	NA	100%																				
1.1.10.4.1	Re-bar	2 d	12/02/12	13/02/12	NA	100%																				
1.1.10.4.2	Formwork	2 d	14/02/12	15/02/12	NA	100%																				
1.1.10.4.3	Concrete	1 d	16/02/12	16/02/12	NA	100%																				
1.1.10.5	Lift Core: Lift-2	4 d	17/02/12	20/02/12	NA	0%																				
1.1.10.5.1	Re-bar	1 d	17/02/12	17/02/12	NA	0%																				
1.1.10.5.2	Formwork	2 d	18/02/12	19/02/12	NA	0%																				
1.1.10.5.3	Concrete	1 d	20/02/12	20/02/12	NA	0%																				
1.1.10.6	Stair Case (2 nos)-Flight-1	8 d	13/02/12	20/02/12	NA	0%																				

Project: Ekushey Bhaban - Superstruc Date: 01/08/12	Task		Summary		Rolled Up Progress	
	Critical Task		Rolled Up Task		Project Summary	
	Progress		Rolled Up Critical Task		Group By Summary	
