

WEEKLY PROJECT REPORT-035



Picture Taken : 16 May 2012

AS ON 16 MAY 2012

PROJECT SUMMARY AS ON: 16 MAY 2012

- Program is 70 days delayed from master program as on 16th May 2012. Still delay time is increasing and 7 days more lag in 8th floor roof slab casting. But it should be controlled.
- Still no signature by MEP in Work Inspection Request (WIR) before slab casting.
- Manpower is slightly increased as before.
- Tool Box Meeting (Safety Meeting) with picture, Safety Award picture and Safety violation notice are attached.

WEEKLY CHECK-LIST FOR **PROGRAM** AS ON: 16-05-2012



Name of Sub-Contractor:	Sohel Enterprise
--------------------------------	------------------

WBS					
Task Name	9th floor roof slab casting				
Schedule Finish	02/03/2012	Actual Finish:	11/05/2012	Time Lag:	70
Causes of Delay					

WBS					
Task Name	9th floor roof slab and beam shuttering complete				
Actual Start		Actual Finish:	10/05/2012	Time Lag:	
Causes of Delay					

WBS					
Task Name					
Actual Start		Actual Finish:		Time Lead/Lag:	
Causes of Delay					

WBS					
Task Name					
Actual Start		Actual Finish:		Time Lead/Lag:	
Causes of Delay					

WBS					
Task Name					
Actual Start		Actual Finish:		Time Lead/Lag:	
Causes of Delay					

Remarks: (Penalty/ Award) to be filled by Project Incharge

Suuggestion/ Advice:

9th floor roof slab casting is 70 days delayed from master program which is 7 days more delay than previous slab.

 Consultant


 Chief Engineer

Project Incharge

Chief Engineer

Director

Delay of Roof Slab Casting

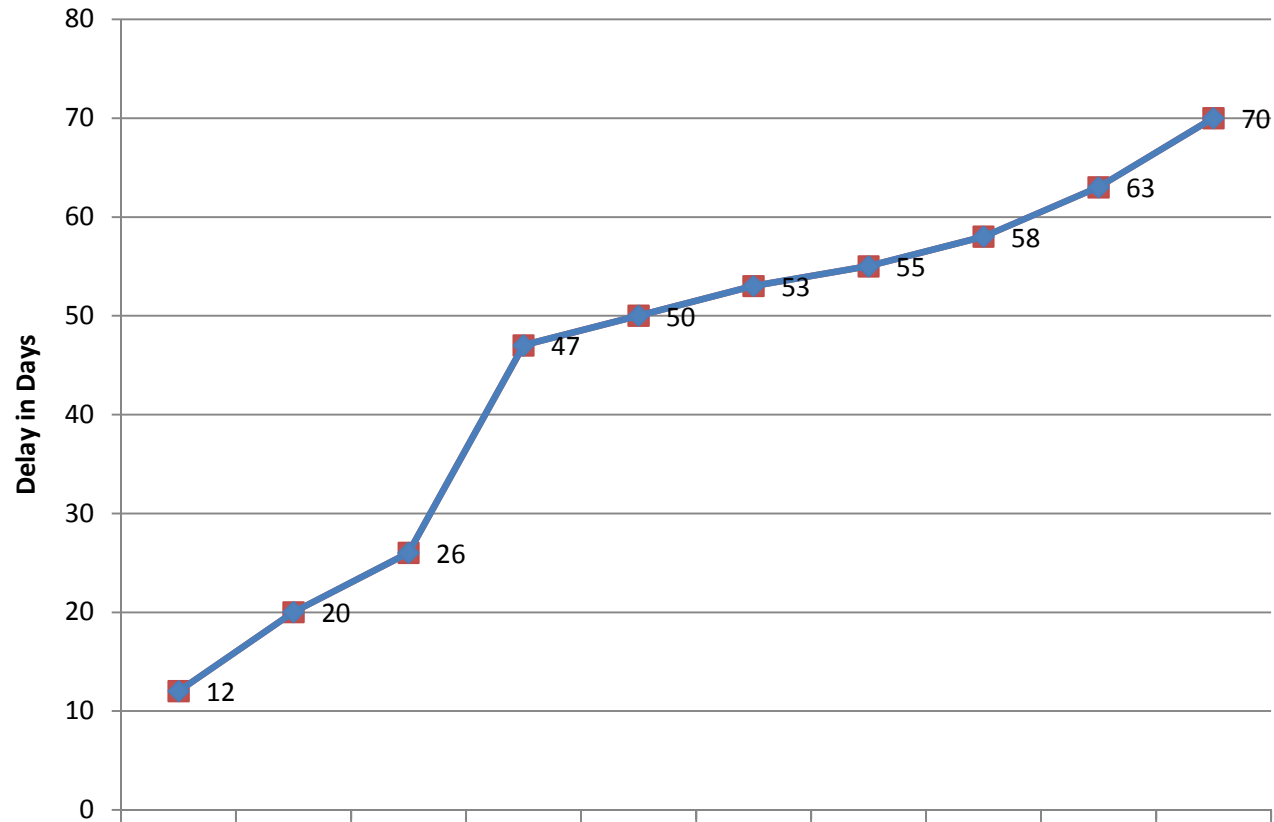

Actual Finish

Schedule Finish

29/08/11	02/10/11	28/10/11	09/12/11	07/01/12	31/01/12	24/02/12	18/03/12	13/04/12	11/05/12
17/8/11	12/9/11	2/10/11	23/10/11	18/11/11	9/12/11	31/12/11	20/1/12	10/2/12	2/3/12
Ground Floor	1st Floor	2nd Floor	3rd Floor	4th Floor	5th Floor	6th Floor	7th Floor	8th Floor	9th Floor

Ekushey Bhaban-Superstructure-Progress

Sl.	Task Name	Duration	Start	Finish	Actual Finish	% Compl	Mar '12					Apr '12				May '12									
							12/02	19/02	26/02	04/03	11/03	18/03	25/03	01/04	08/04	15/04	22/04	29/04	06/05	13/05	20/05				
1	Ekushey Bhaban	442 d	28/07/11	18/11/12	NA	5%	16/05/12																		
1.1	Superstructure	300 d	28/07/11	14/06/12	NA	70%																			
1.1.1	Ground Floor	20 d	28/07/11	17/08/11	29/08/11	100%																			
1.1.2	1st Floor	20 d	18/08/11	12/09/11	02/10/11	100%																			
1.1.3	2nd Floor	20 d	13/09/11	02/10/11	28/10/11	100%																			
1.1.4	3rd Floor	20 d	03/10/11	23/10/11	09/12/11	100%																			
1.1.5	4th Floor	20 d	24/10/11	18/11/11	07/01/12	100%																			
1.1.6	5th Floor	20 d	19/11/11	09/12/11	31/01/12	100%																			
1.1.7	6th Floor	20 d	10/12/11	31/12/11	24/02/12	100%																			
1.1.8	7th Floor	20 d	01/01/12	20/01/12	18/03/12	100%																			
1.1.9	8th Floor	20 d	21/01/12	10/02/12	18/04/12	100%																			
1.1.10	9th Floor	20 d	11/02/12	02/03/12	11/05/12	100%																			
1.1.10.1	Layout Work	1 d	11/02/12	11/02/12	NA	100%																			
1.1.10.2	Column (17 nos): Lift-1	4 d	12/02/12	15/02/12	NA	100%																			
1.1.10.3	Column (17 nos): Lift-2	4 d	16/02/12	19/02/12	NA	100%																			
1.1.10.4	Lift Core: Lift-1	5 d	12/02/12	16/02/12	NA	100%																			
1.1.10.5	Lift Core: Lift-2	4 d	17/02/12	20/02/12	NA	100%																			
1.1.10.6	Stair Case (2 nos)-Flight-1	8 d	13/02/12	20/02/12	NA	100%																			
1.1.10.7	Stair Case (2 nos)-Flight-2	8 d	24/02/12	02/03/12	NA	100%																			
1.1.10.8	Roof Slab	10 d	22/02/12	02/03/12	11/05/12	100%																			
1.1.10.8.1	Formwork	5 d	22/02/12	26/02/12	NA	100%																			
1.1.10.8.2	Re-bar	3 d	27/02/12	29/02/12	NA	100%																			
1.1.10.8.3	MEP Work	2 d	29/02/12	01/03/12	NA	100%																			
1.1.10.8.4	Inspection	1 d	01/03/12	01/03/12	NA	100%																			
1.1.10.8.5	Concrete	1 d	02/03/12	02/03/12	11/05/12	100%																			
1.1.11	10th Floor	20 d	03/03/12	23/03/12	NA	18%																			
1.1.11.1	Layout Work	1 d	03/03/12	03/03/12	NA	100%																			
1.1.11.2	Column (17 nos): Lift-1	4 d	04/03/12	07/03/12	NA	100%																			
1.1.11.2.1	Re-bar	1 d	04/03/12	04/03/12	NA	100%																			
1.1.11.2.2	Formwork	2 d	05/03/12	06/03/12	NA	100%																			
1.1.11.2.3	Concrete	1 d	07/03/12	07/03/12	NA	100%																			
1.1.11.3	Column (17 nos): Lift-2	4 d	08/03/12	11/03/12	NA	0%																			
1.1.11.3.1	Re-bar	1 d	08/03/12	08/03/12	NA	0%																			
1.1.11.3.2	Formwork	2 d	09/03/12	10/03/12	NA	0%																			
1.1.11.3.3	Concrete	1 d	11/03/12	11/03/12	NA	0%																			
1.1.11.4	Lift Core: Lift-1	5 d	04/03/12	08/03/12	NA	70%																			
1.1.11.4.1	Re-bar	2 d	04/03/12	05/03/12	NA	100%																			
1.1.11.4.2	Formwork	2 d	06/03/12	07/03/12	NA	50%																			
1.1.11.4.3	Concrete	1 d	08/03/12	08/03/12	NA	50%																			
1.1.11.5	Lift Core: Lift-2	4 d	09/03/12	12/03/12	NA	0%																			

Project: Ekushey Bhaban - Superstruc Date: 02/08/12	Task Critical Task Progress	Summary Rolled Up Task Rolled Up Critical Task	Rolled Up Progress Project Summary Group By Summary	Rolled Up Progress Project Summary Group By Summary
--	-----------------------------------	--	---	---
