

WEEKLY PROJECT REPORT-039



Picture Taken : 13 Jun 2012

AS ON 13 JUN 2012

PROJECT SUMMARY AS ON: 13 JUN 2012

- Program is 80 days delayed from master program as on 13th Jun 2012. Still delay time is increasing and 10 days more lag in 9th floor roof slab casting. But it should be controlled.
- Still no signature by MEP in Work Inspection Request (WIR) before slab casting.
- Manpower is slightly decreased as before.
- Safety Induction Program with picture is attached.

WEEKLY CHECK-LIST FOR **PROGRAM** AS ON: 13-06-12



Name of Sub-Contractor:	Sohel Enterprise
--------------------------------	------------------

WBS					
Task Name	10th floor roof beam & slab casting				
Schedule Finish	23/03/2012	Actual Finish:	11/06/2012	Time Lag:	80
Causes of Delay					

WBS					
Task Name	10th floor beam and Slab shuttering complete				
Actual Start		Actual Finish:	10/06/2012	Time Lag:	
Causes of Delay					

WBS					
Task Name					
Actual Start		Actual Finish:	24/02/2012	Time Lead/Lag:	
Causes of Delay					

WBS					
Task Name					
Actual Start		Actual Finish:		Time Lead/Lag:	
Causes of Delay					

WBS					
Task Name					
Actual Start		Actual Finish:		Time Lead/Lag:	
Causes of Delay					

Remarks: (Penalty/ Award) to be filled by Project Incharge

Suuggestion/ Advice:

Floor casting is 80 days delayed from Master program and 10 days more delay than previous slab.

 Consultant


 Chief Engineer

Project Incharge

Chief Engineer

Director

Delay of Roof Slab Casting

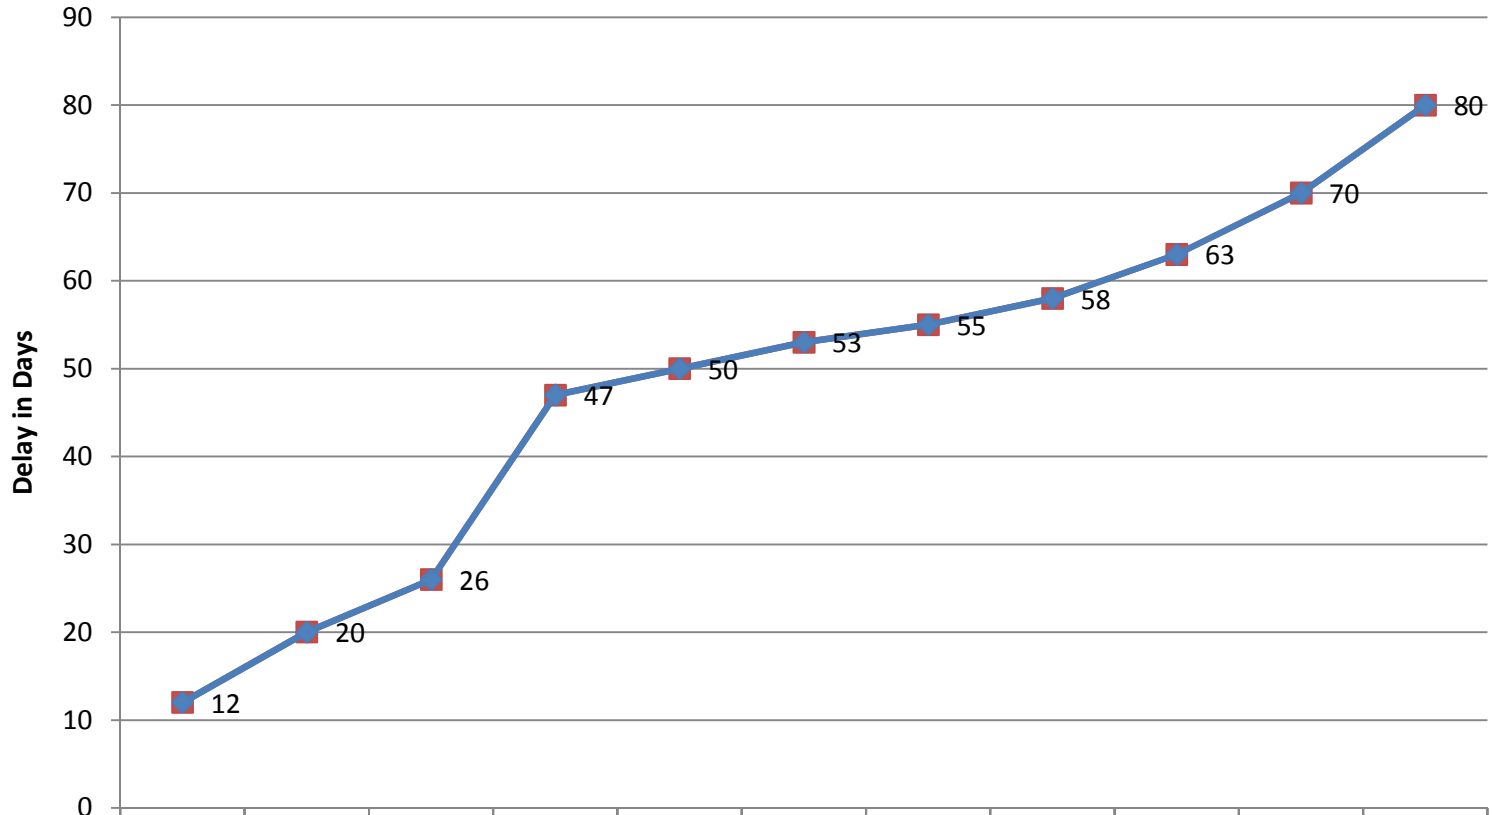

Actual Finish	29/08/11	02/10/11	28/10/11	09/12/11	07/01/12	31/01/12	24/02/12	18/03/12	13/04/12	11/05/12	11/06/12
Schedule Finish	17/8/11	12/9/11	2/10/11	23/10/11	18/11/11	9/12/11	31/12/11	20/1/12	10/2/12	2/3/12	23/3/12
	Ground Floor	1st Floor	2nd Floor	3rd Floor	4th Floor	5th Floor	6th Floor	7th Floor	8th Floor	9th Floor	10th Floor

Ekushey Bhaban-Superstructure-Progress

Sl.	Task Name	Duration	Start	Finish	Actual Finish	% Compl	Timeline											
							'12	Apr '12	May '12	Jun '12	Jul '12	Aug '12	Sep '12	Oct '12	Nov '12			
1	Ekushey Bhaban	442 d	28/07/11	18/11/12	NA	5%												
1.1	Superstructure	300 d	28/07/11	14/06/12	NA	75%												
1.1.1	Ground Floor	20 d	28/07/11	17/08/11	29/08/11	100%												
1.1.2	1st Floor	20 d	18/08/11	12/09/11	02/10/11	100%												
1.1.3	2nd Floor	20 d	13/09/11	02/10/11	28/10/11	100%												
1.1.4	3rd Floor	20 d	03/10/11	23/10/11	09/12/11	100%												
1.1.5	4th Floor	20 d	24/10/11	18/11/11	07/01/12	100%												
1.1.6	5th Floor	20 d	19/11/11	09/12/11	31/01/12	100%												
1.1.7	6th Floor	20 d	10/12/11	31/12/11	24/02/12	100%												
1.1.8	7th Floor	20 d	01/01/12	20/01/12	18/03/12	100%												
1.1.9	8th Floor	20 d	21/01/12	10/02/12	18/04/12	100%												
1.1.10	9th Floor	20 d	11/02/12	02/03/12	11/05/12	100%												
1.1.11	10th Floor	20 d	03/03/12	23/03/12	11/06/12	100%												
1.1.11.1	Layout Work	1 d	03/03/12	03/03/12	NA	100%												
1.1.11.2	Column (17 nos): Lift-1	4 d	04/03/12	07/03/12	NA	100%												
1.1.11.3	Column (17 nos): Lift-2	4 d	08/03/12	11/03/12	NA	100%												
1.1.11.4	Lift Core: Lift-1	5 d	04/03/12	08/03/12	NA	100%												
1.1.11.5	Lift Core: Lift-2	4 d	09/03/12	12/03/12	NA	100%												
1.1.11.6	Stair Case (2 nos)-Flight-1	8 d	05/03/12	12/03/12	NA	100%												
1.1.11.7	Stair Case (2 nos)-Flight-2	8 d	15/03/12	23/03/12	NA	100%												
1.1.11.8	Roof Slab	10 d	13/03/12	23/03/12	11/06/12	100%												
1.1.11.8.1	Formwork	5 d	13/03/12	18/03/12	10/06/12	100%												
1.1.11.8.2	Re-bar	3 d	19/03/12	21/03/12	NA	100%												
1.1.11.8.3	MEP Work	2 d	21/03/12	22/03/12	NA	100%												
1.1.11.8.4	Inspection	1 d	22/03/12	22/03/12	NA	100%												
1.1.11.8.5	Concrete	1 d	23/03/12	23/03/12	11/06/12	100%												
1.1.12	11th Floor	20 d	24/03/12	12/04/12	NA	2%												
1.1.12.1	Layout Work	1 d	24/03/12	24/03/12	NA	100%												
1.1.12.2	Column (17 nos): Lift-1	4 d	25/03/12	28/03/12	NA	0%												
1.1.12.2.1	Re-bar	1 d	25/03/12	25/03/12	NA	0%												
1.1.12.2.2	Formwork	2 d	26/03/12	27/03/12	NA	0%												
1.1.12.2.3	Concrete	1 d	28/03/12	28/03/12	NA	0%												
1.1.12.3	Column (17 nos): Lift-2	4 d	29/03/12	01/04/12	NA	0%												
1.1.12.3.1	Re-bar	1 d	29/03/12	29/03/12	NA	0%												
1.1.12.3.2	Formwork	2 d	30/03/12	31/03/12	NA	0%												
1.1.12.3.3	Concrete	1 d	01/04/12	01/04/12	NA	0%												
1.1.12.4	Lift Core: Lift-1	5 d	25/03/12	29/03/12	NA	0%												
1.1.12.4.1	Re-bar	2 d	25/03/12	26/03/12	NA	0%												
1.1.12.4.2	Formwork	2 d	27/03/12	28/03/12	NA	0%												
1.1.12.4.3	Concrete	1 d	29/03/12	29/03/12	NA	0%												

Project: Ekushey Bhaban - Superstruc Date: 02/08/12	Task		Summary		Rolled Up Progress	
	Critical Task		Rolled Up Task		Project Summary	
	Progress		Rolled Up Critical Task		Group By Summary	
