

# WEEKLY PROJECT REPORT-055



AS ON 03 OCT 2012

## PROJECT SUMMARY AS ON: 03 OCT 2012

- Program is 126 days delayed from master program as on 03<sup>rd</sup> Oct 2012. Delay time is too much more from previous i.e. 32 days more lag in 12<sup>th</sup> floor roof slab casting. This is due to Eid Vacation. So Proper measure should be taken in next Eid Vacation.
- Still no signature by MEP in Work Inspection Request (WIR) before slab casting.
- Safety Tool Box Meeting Notice, Picture and Hazards (in draft form) are attached.
- Manpower is slightly increased.

WEEKLY CHECK-LIST FOR **PROGRAM** AS ON: 03-10-2012



<b>Name of Sub-Contractor:</b>	Sohel Enterprise
--------------------------------	------------------

WBS	1.1.14.8.5				
Task Name	13 th floor roof slab and beam casting Complete				
Schedule Finish	25/05/2012	Actual Finish:	28/09/2012	Time Lag:	126
Causes of Delay	Eid Vacation				

WBS	1.1.14.8.1				
Task Name	13 th Floor roof slab & Beam Shuttering complete				
Actual Start		Actual Finish:	28/09/2012	Time Lag:	
Causes of Delay					

WBS					
Task Name					
Actual Start		Actual Finish:		Time Lead/Lag:	
Causes of Delay					

WBS					
Task Name					
Actual Start		Actual Finish:		Time Lead/Lag:	
Causes of Delay					

WBS					
Task Name					
Actual Start		Actual Finish:		Time Lead/Lag:	
Causes of Delay					

**Remarks: (Penalty/ Award) to be filled by Project Incharge**

**Suuggestion/ Advice:**

Total 126 days delay from master program which is 32 days more delay than previous slab. This is due to Eid Vacation.

\_\_\_\_\_  
 Consultant


\_\_\_\_\_  
 Chief Engineer

\_\_\_\_\_  
Project Incharge

\_\_\_\_\_  
Chief Engineer

\_\_\_\_\_  
Director

# Delay of Roof Slab Casting

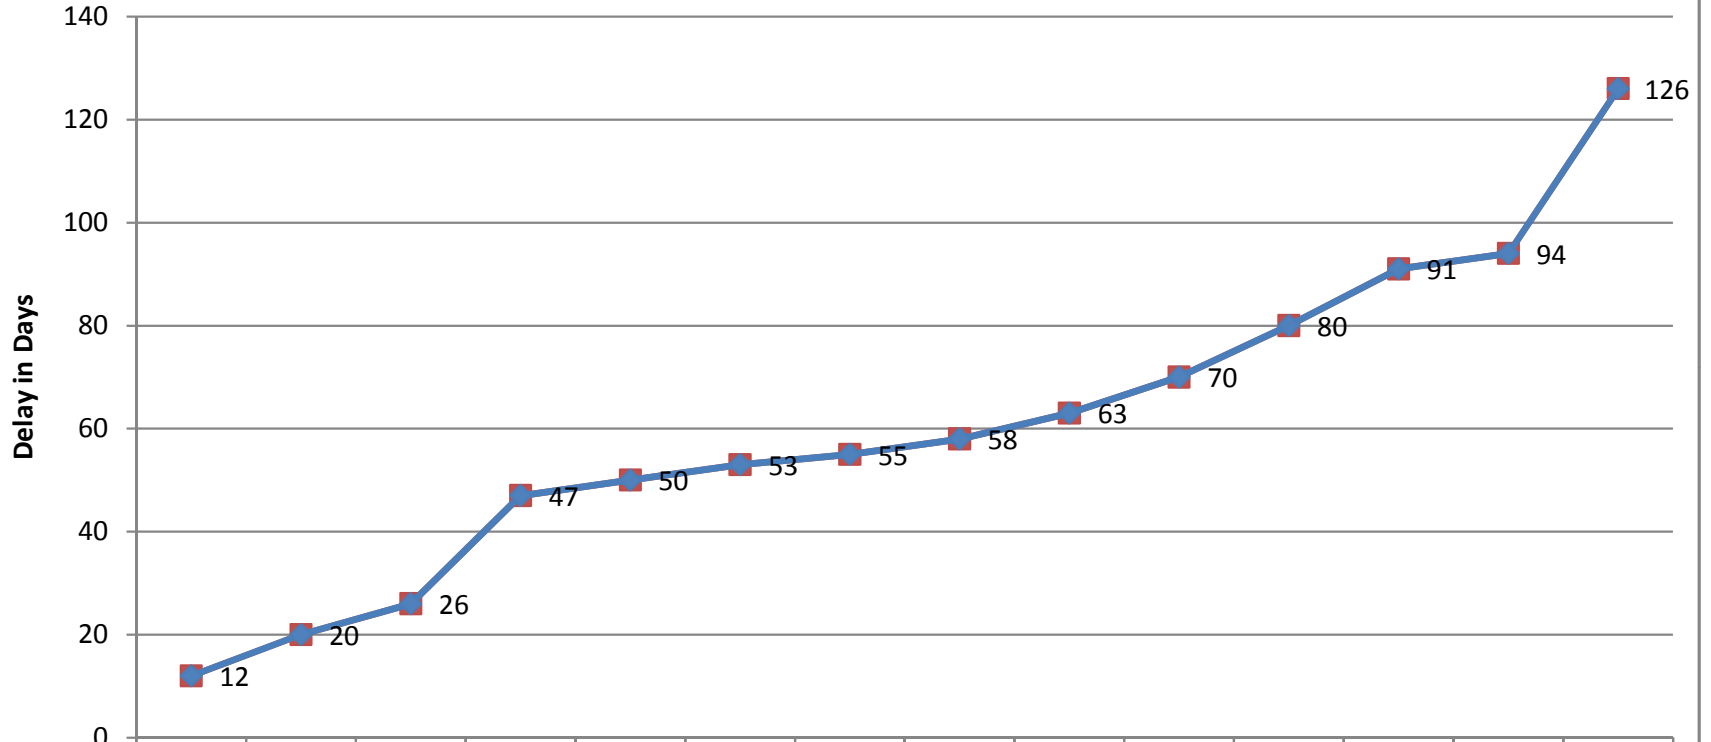

Actual Finish

Schedule Finish

29/08/11	02/10/11	28/10/11	09/12/11	07/01/12	31/01/12	24/02/12	18/03/12	13/04/12	11/05/12	11/06/12	12/07/12	06/08/12	28/09/12
17/8/11	12/9/11	2/10/11	23/10/11	18/11/11	9/12/11	31/12/11	20/1/12	10/2/12	2/3/12	23/3/12	12/4/12	4/5/12	25/5/12

### Ekushey Bhaban-Superstructure-Progress

Sl.	Task Name	Duration	Start	Finish	Actual Finish	% Compl	'12	Apr '12	May '12	Jun '12	Jul '12	Aug '12	Sep '12	Oct '12	Nov '12				
							1/08/05/01	08/05/02	09/06/03	00/07/03	00/07/04	01/08/05/02	09/05/02	09/06/02	09/06/03	00/07/14	11/18/14	11/18/15	
1	<b>Ekushey Bhaban</b>	442 d	28/07/11	18/11/12	NA	7%													
1.1	<b>Superstructure</b>	300 d	28/07/11	14/06/12	NA	97%													
1.1.1	Ground Floor	20 d	28/07/11	17/08/11	29/08/11	100%													
1.1.2	1st Floor	20 d	18/08/11	12/09/11	02/10/11	100%													
1.1.3	2nd Floor	20 d	13/09/11	02/10/11	28/10/11	100%													
1.1.4	3rd Floor	20 d	03/10/11	23/10/11	09/12/11	100%													
1.1.5	4th Floor	20 d	24/10/11	18/11/11	07/01/12	100%													
1.1.6	5th Floor	20 d	19/11/11	09/12/11	31/01/12	100%													
1.1.7	6th Floor	20 d	10/12/11	31/12/11	24/02/12	100%													
1.1.8	7th Floor	20 d	01/01/12	20/01/12	18/03/12	100%													
1.1.9	8th Floor	20 d	21/01/12	10/02/12	18/04/12	100%													
1.1.10	9th Floor	20 d	11/02/12	02/03/12	11/05/12	100%													
1.1.11	10th Floor	20 d	03/03/12	23/03/12	11/06/12	100%													
1.1.12	11th Floor	20 d	24/03/12	12/04/12	12/07/12	100%													
1.1.13	12th Floor	20 d	13/04/12	04/05/12	06/08/12	100%													
1.1.14	13th Floor	20 d	05/05/12	25/05/12	28/09/12	100%													
1.1.14.1	Layout Work	1 d	05/05/12	05/05/12	NA	100%													
1.1.14.2	Column (17 nos): Lift-1	4 d	06/05/12	09/05/12	NA	100%													
1.1.14.3	Column (17 nos): Lift-2	4 d	10/05/12	13/05/12	NA	100%													
1.1.14.4	Lift Core: Lift-1	5 d	06/05/12	10/05/12	NA	100%													
1.1.14.5	Lift Core: Lift-2	4 d	11/05/12	14/05/12	NA	100%													
1.1.14.6	Stair Case (2 nos)-Flight-1	8 d	07/05/12	14/05/12	NA	100%													
1.1.14.7	Stair Case (2 nos)-Flight-2	8 d	18/05/12	25/05/12	NA	100%													
1.1.14.8	Roof Slab	10 d	15/05/12	25/05/12	28/09/12	100%													
1.1.14.8.1	Formwork	5 d	15/05/12	20/05/12	NA	100%													
1.1.14.8.2	Re-bar	3 d	21/05/12	23/05/12	NA	100%													
1.1.14.8.3	MEP Work	2 d	23/05/12	24/05/12	NA	100%													
1.1.14.8.4	Inspection	1 d	24/05/12	24/05/12	NA	100%													
1.1.14.8.5	Concrete	1 d	25/05/12	25/05/12	28/09/12	100%													
1.1.15	<b>Top Floor</b>	20 d	26/05/12	14/06/12	NA	33%													
1.1.15.1	Layout Work	1 d	26/05/12	26/05/12	NA	100%													
1.1.15.2	Column (17 nos): Lift-1	4 d	27/05/12	30/05/12	NA	100%													
1.1.15.2.1	Re-bar	1 d	27/05/12	27/05/12	NA	100%													
1.1.15.2.2	Formwork	2 d	28/05/12	29/05/12	NA	100%													
1.1.15.2.3	Concrete	1 d	30/05/12	30/05/12	NA	100%													
1.1.15.3	Column (17 nos): Lift-2	4 d	31/05/12	03/06/12	NA	0%													
1.1.15.3.1	Re-bar	1 d	31/05/12	31/05/12	NA	0%													
1.1.15.3.2	Formwork	2 d	01/06/12	02/06/12	NA	0%													
1.1.15.3.3	Concrete	1 d	03/06/12	03/06/12	NA	0%													
1.1.15.4	Lift Core: Lift-1	5 d	27/05/12	31/05/12	NA	100%													

Project: Ekushey Bhaban - Superstruc Date: 07/10/12	Task		Summary		Rolled Up Progress	
	Critical Task		Rolled Up Task		Project Summary	
	Progress		Rolled Up Critical Task		Group By Summary	
