


WORK PLAN AND PROGRESS OF RIVER FRONT SATELLITE CITY

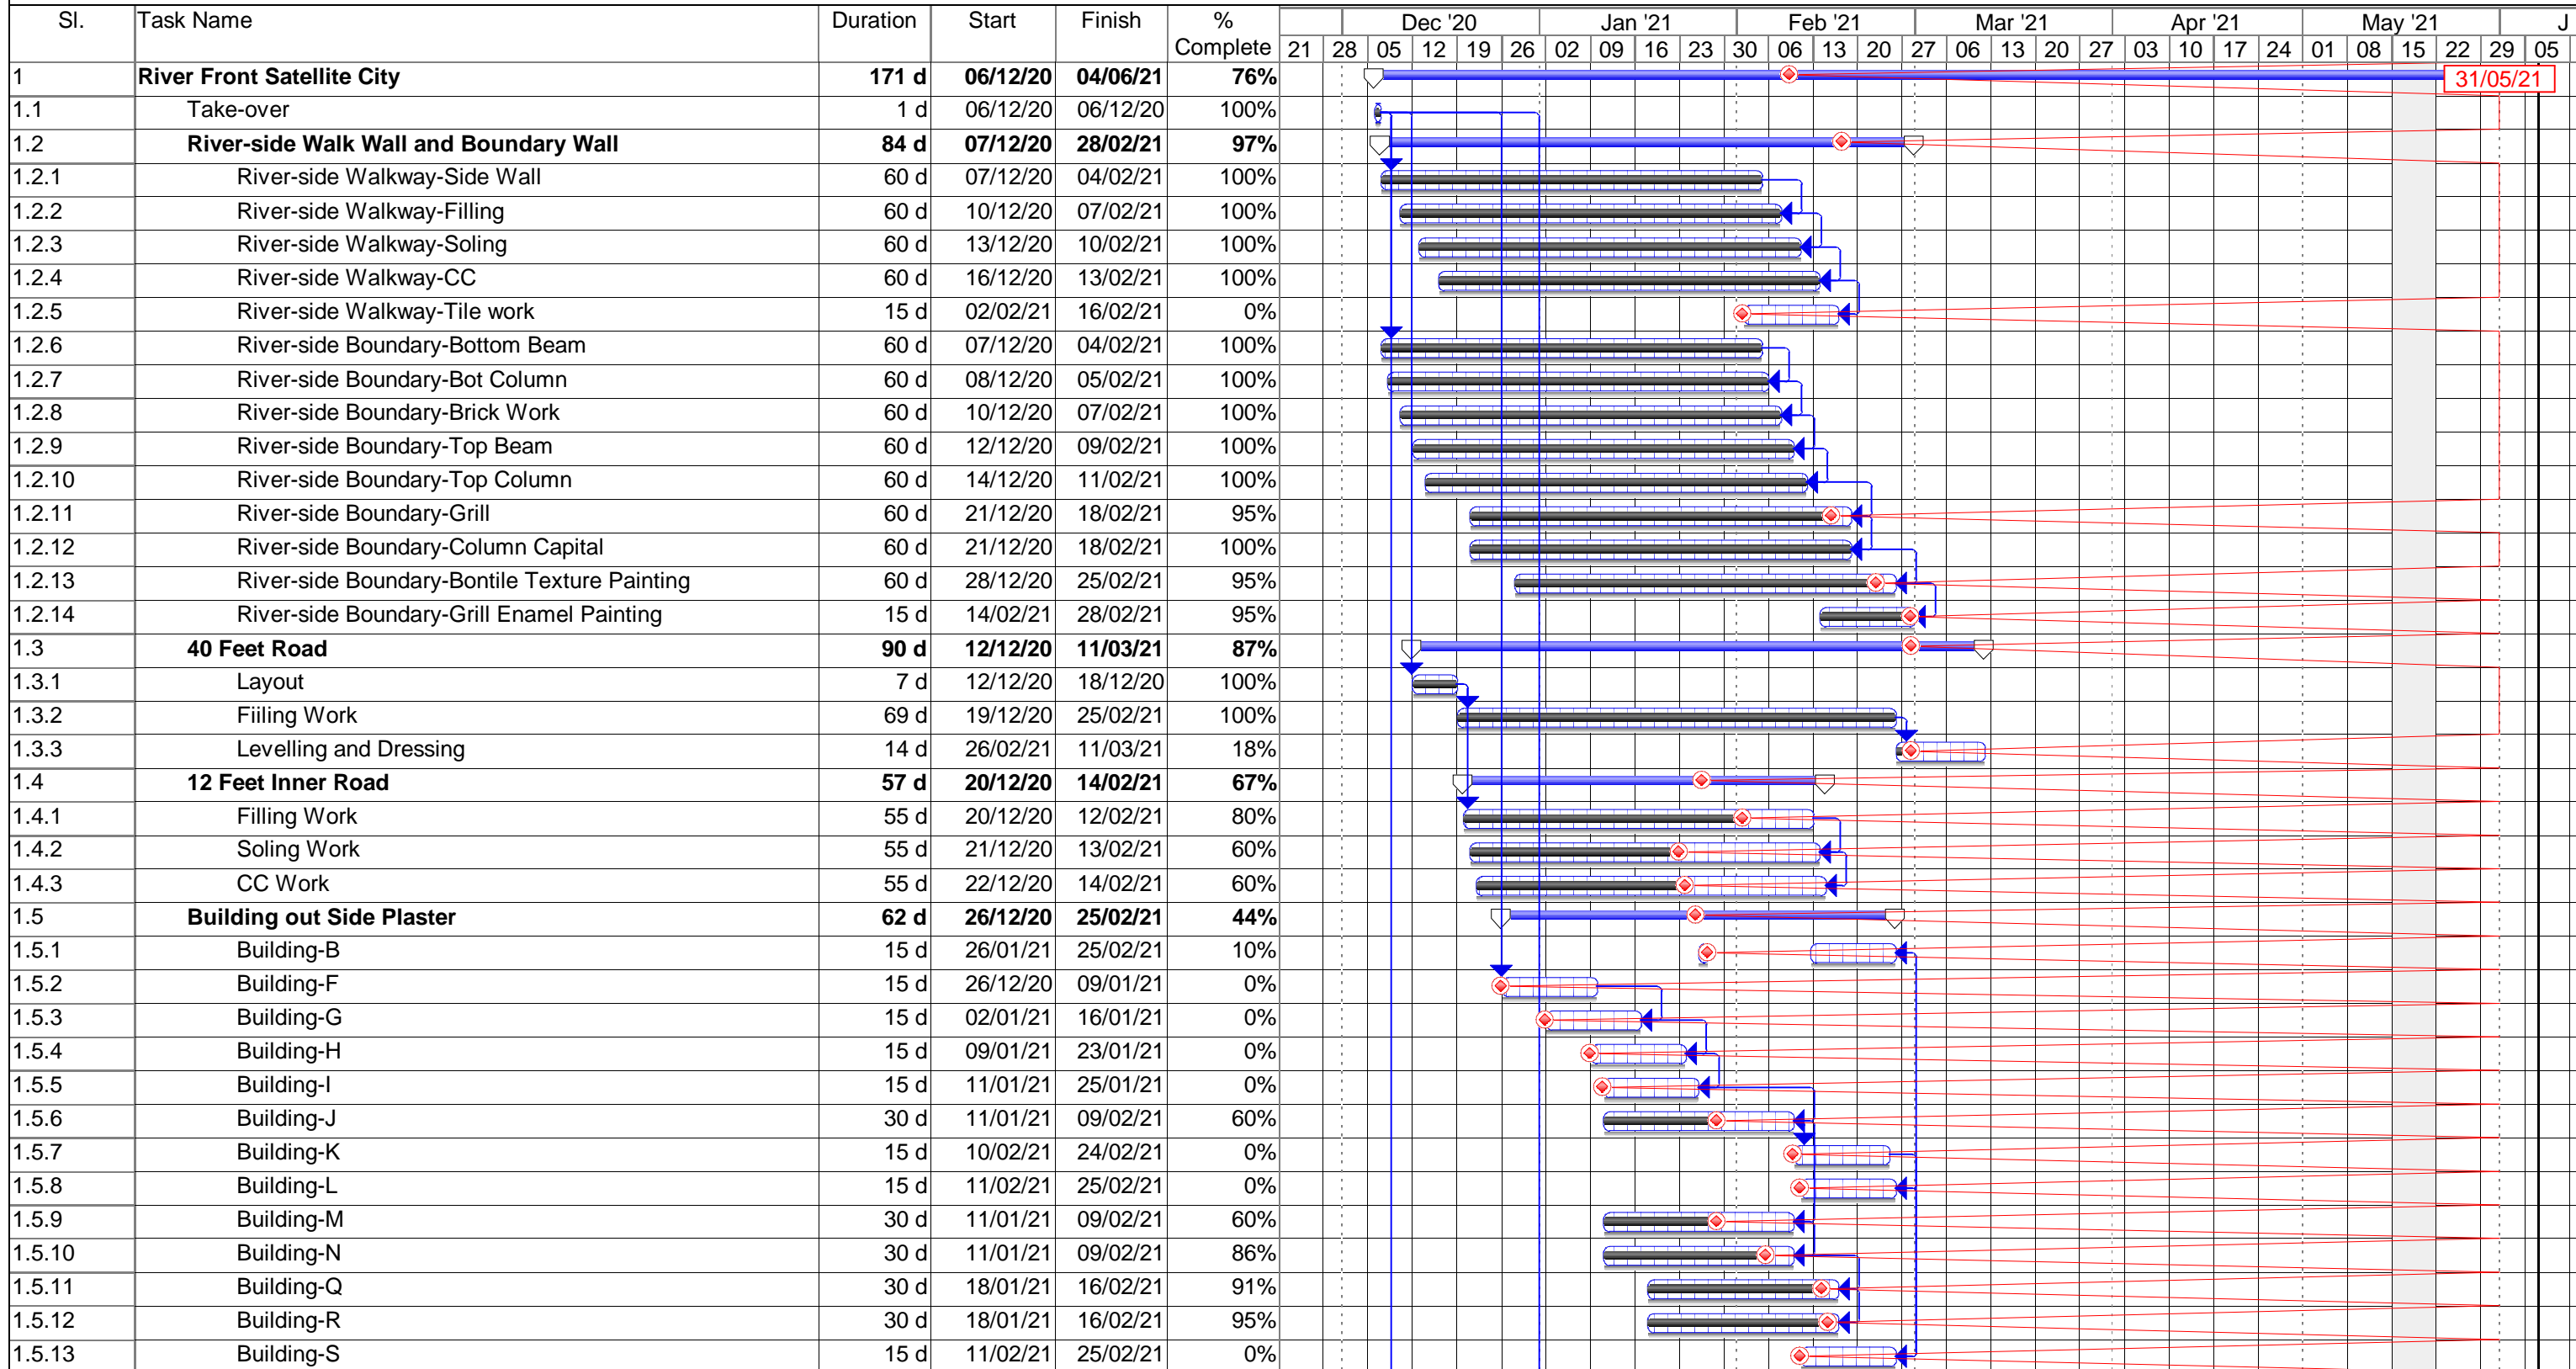

Date: 07/06/21 19:19
Sheet: 1 / 2

Task		Summary		Rolled Up Progress	
Critical Task		Rolled Up Task		Project Summary	
Progress		Rolled Up Critical Task		Group By Summary	

WORK PLAN AND PROGRESS OF RIVER FRONT SATELLITE CITY



Sl.	Task Name	Duration	Start	Finish	% Complete	Dec '20		Jan '21				Feb '21				Mar '21			Apr '21			May '21			J								
						21	28	05	12	19	26	02	09	16	23	30	06	13	20	27	06	13	20	27		03	10	17	24	01	08	15	22
1.6	Mock-up Flat	71 d	06/12/20	14/02/21	59%																												
1.6.1	Ground Floor	7 d	01/01/21	07/01/21	100%																												
1.6.1.1	Brick-Flat Soling	5 d	01/01/21	05/01/21	100%																												
1.6.1.2	CC	5 d	03/01/21	07/01/21	100%																												
1.6.2	Dismantling Work	21 d	01/01/21	21/01/21	100%																												
1.6.3	Construction Joint & Extension	5 d	27/01/21	31/01/21	100%																												
1.6.4	Masonry & Plaster	35 d	07/01/21	10/02/21	91%																												
1.6.4.1	Brick Work	15 d	17/01/21	31/01/21	100%																												
1.6.4.2	In-side Plaster Work	35 d	07/01/21	10/02/21	87%																												
1.6.5	Door Window	60 d	06/12/20	03/02/21	0%																												
1.6.6	Sanitary and Electrical	31 d	15/01/21	14/02/21	47%																												
1.6.6.1	Saniray Inside Pipe Fitting	14 d	01/02/21	14/02/21	0%																												
1.6.6.2	Electrical Conduit Cocealing Work	17 d	15/01/21	31/01/21	85%																												
1.7	New Mosque	160 d	07/12/20	25/05/21	65%																												
1.7.1	Pile Work	25 d	07/12/20	31/12/20	100%																												
1.7.2	Excavation and Pile Head Breaking	40 d	23/12/20	31/01/21	100%																												
1.7.3	Mat Concreting	20 d	20/01/21	08/02/21	100%																												
1.7.4	Basement	96 d	09/02/21	25/05/21	51%																												
1.7.4.1	Retaining wall, Column, Lift Core, Stair	29 d	09/02/21	09/03/21	100%																												
1.7.4.2	Ground Floor Slab	12 d	10/03/21	21/03/21	100%																												
1.7.4.3	Paster Work	30 d	10/04/21	09/05/21	5%																												
1.7.4.4	Tile Work	10 d	10/04/21	19/04/21	52%																												
1.7.4.5	Anciliary Works	30 d	16/04/21	25/05/21	30%																												
1.7.5	Ground Floor	55 d	22/03/21	25/05/21	66%																												
1.7.5.1	Column	12 d	22/03/21	02/04/21	100%																												
1.7.5.2	Roof Slab	7 d	03/04/21	09/04/21	100%																												
1.7.5.3	Stair-6 nos	25 d	22/03/21	15/04/21	83%																												
1.7.5.4	Anciliary Works	30 d	16/04/21	25/05/21	30%																												
1.7.6	20 ft Connectrion Road	14 d	01/04/21	14/04/21	5%																												
1.7.6.1	Sand Filling	14 d	01/04/21	14/04/21	5%																												
1.7.7	1st Floor	12 d	10/04/21	21/04/21	15%																												
1.7.7.1	Column	12 d	10/04/21	21/04/21	15%																												
1.8	Landing Station	14 d	22/05/21	04/06/21	5%																												
1.8.1	<i>Excavation</i>	<i>14 d</i>	<i>22/05/21</i>	<i>04/06/21</i>	<i>5%</i>																												

Date: 07/06/21 19:19
Sheet:2 /2

Task		Summary		Rolled Up Progress	
Critical Task		Rolled Up Task		Project Summary	
Progress		Rolled Up Critical Task		Group By Summary	
