

CONSTRUCTION OF NBL TWIN TOWER AT PANTHAPTH, DHAKA

PROGRESS REPORT



02 SEP 2021

Generated by: Cityscape International Limited

TABLE OF CONTENTS

- TOTAL PROGRESS
- TOTAL MANPOWER CHART
- CUMMULATIVE PROGRESS CHART
- SCHEDULE LEAD-LAG CHART
- LAST MONTH PROGRESS
- LAST MONTH MANPOWER HISTOGRAM
- LAST MONTH PROGRESS CHART
- DAILY PROGRESS REPORT
- WORK PLAN AND PROGRESS
- PROGRESS PHOTO



TOTAL PROGRESS REPORT

From 6-January-2021 to 2-September-2021

Project Code:	42	Name:	NBL Tower-Superstucure			
Client:	National Bank Limited	Contractor:				
Total Duration:	239	days	Total Working Days:	60	Total Manpower:	20318
Planning Progress =	100%	Actual Progress=	87.1%	SPI=	0.87	Behind Schedule

Total Progress

WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)	Not Yet
01	Ground Floor		100	11-11-20	12-12-20	12-12-20	12-12-20	0	
03	2nd Floor		100	18-12-20	06-01-21	06-01-21	06-01-21	0	
04.1.1	3rd Floor-South Tower-Column	14nos	100	02-01-21	08-01-21	06-01-21	06-01-21	2	
04.1.2	3rd Floor-South Tower-Lift Core	2nos	100	02-01-21	08-01-21	06-01-21	06-01-21	2	
04.1.3	3rd Floor-South Tower-Stair	2nos	100	09-01-21	13-01-21	11-01-21	11-01-21	2	
04.1.4	3rd Floor-South Tower-Roof Slab	958sqm	100	09-01-21	13-01-21	11-01-21	11-01-21	2	
04.2.1	3rd Floor-North Tower-Column	11nos	100	07-01-21	13-01-21	14-01-21	14-01-21	-1	
04.2.2	3rd Floor-North Tower-Lift Core	2nos	100	07-01-21	13-01-21	16-01-21	16-01-21	-3	
04.2.3	3rd Floor-North Tower-Stair	2nos	100	14-01-21	18-01-21	14-01-21	18-01-21	0	
04.2.4	3rd Floor-North Tower-Roof Slab	958sqm	100	14-01-21	18-01-21	14-01-21	18-01-21	0	
05.1.1	4th Floor-South Tower-Column	14nos	100	14-01-21	20-01-21	14-01-21	14-01-21	6	
05.1.2	4th Floor-South Tower-Lift Core	2nos	100	14-01-21	20-01-21	14-01-21	16-01-21	4	
05.1.3	4th Floor-South Tower-Stair	2nos	100	21-01-21	25-01-21	20-01-21	21-01-21	4	
05.1.4	4th Floor-South Tower-Roof Slab	960sqm	100	21-01-21	25-01-21	20-01-21	21-01-21	4	
05.2.1	4th Floor-North Tower-Column	11nos	100	19-01-21	25-01-21	19-01-21	19-01-21	6	


WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)	Not Yet
05.2.2	4th Floor-North Tower-Lift Core	2nos	100	19-01-21	25-01-21	20-01-21	22-01-21	3	
05.2.3	4th Floor-North Tower-Stair	2nos	100	26-01-21	30-01-21	27-01-21	27-01-21	3	
05.2.4	4th Floor-North Tower-Roof Slab	960sqm	100	26-01-21	30-01-21	27-01-21	27-01-21	3	
06.1.1	5th Floor-South Tower-Column	14nos	100	26-01-21	01-02-21	22-01-21	22-01-21	10	
06.1.2	5th Floor-South Tower-Lift Core	2nos	100	26-01-21	01-02-21	24-01-21	24-01-21	8	
06.1.3	5th Floor-South Tower-Stair	2nos	100	02-02-21	06-02-21	01-02-21	01-02-21	5	
06.1.4	5th Floor-South Tower-Roof Slab	840sqm	100	02-02-21	06-02-21	01-02-21	01-02-21	5	
06.2.1	5th Floor-North Tower-Column	11nos	100	31-01-21	06-02-21	29-01-21	29-01-21	8	
06.2.2	5th Floor-North Tower-Lift Core	2nos	100	31-01-21	06-02-21	30-01-21	02-02-21	4	
06.2.3	5th Floor-North Tower-Stair	2nos	100	07-02-21	11-02-21	06-02-21	06-02-21	5	
06.2.4	5th Floor-North Tower-Roof Slab	960sqm	100	07-02-21	11-02-21	06-02-21	06-02-21	5	
07.1.1	6th Floor-South Tower-Column	14nos	100	07-02-21	13-02-21	03-02-21	03-02-21	10	
07.1.2	6th Floor-South Tower-Lift Core	2nos	100	07-02-21	13-02-21	04-02-21	06-02-21	7	
07.1.3	6th Floor-South Tower-Stair	2nos	100	14-02-21	18-02-21	16-02-21	16-02-21	2	
07.1.4	6th Floor-South Tower-Roof Slab	963sqm	100	14-02-21	18-02-21	16-02-21	16-02-21	2	
07.2.1	6th Floor-North Tower-Column	11nos	100	12-02-21	18-02-21	08-02-21	08-02-21	10	
07.2.2	6th Floor-North Tower-Lift Core	2nos	100	12-02-21	18-02-21	15-02-21	18-02-21	0	
07.2.3	6th Floor-North Tower-Stair	2nos	100	19-02-21	23-02-21	22-02-21	23-02-21	0	
07.2.4	6th Floor-North Tower-Roof Slab	960sqm	100	19-02-21	23-02-21	22-02-21	23-02-21	0	

WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)	Not Yet
08.1.1	7th Floor-South Tower-Column	14nos	100	19-02-21	25-02-21	19-02-21	19-02-21	6	
08.1.2	7th Floor-South Tower-Lift Core	2nos	100	19-02-21	25-02-21	19-02-21	22-02-21	3	
08.1.3	7th Floor-South Tower-Stair Case	2nos	100	26-02-21	02-03-21	01-03-21	01-03-21	1	
08.1.4	7th Floor-South Tower-Roof Slab	950sqm	100	26-02-21	02-03-21	01-03-21	01-03-21	1	
08.2.1	7th Floor-North Tower-Column	11nos	100	24-02-21	02-03-21	25-02-21	25-02-21	5	
08.2.2	7th Floor-North Tower-Lift Core	2nos	100	24-02-21	02-03-21	26-02-21	02-03-21	0	
08.2.3	7th Floor-North Tower-Stair Case	2nos	100	03-03-21	07-03-21	08-03-21	08-03-21	-1	
08.2.4	7th Floor-North Tower-Slab	960m2	100	03-03-21	07-03-21	08-03-21	08-03-21	-1	
09.1.1	8th Floor-South Tower-Column	14nos	100	03-03-21	09-03-21	05-03-21	05-03-21	4	
09.1.2	8th Floor-South Tower-Lift Core	2nos	100	03-03-21	09-03-21	08-03-21	11-03-21	-2	
09.1.3	8th Floor-South Tower-Stair Case	2nos	100	10-03-21	14-03-21	17-03-21	17-03-21	-3	
09.1.4	8th Floor-South Tower-Roof Slab	963m2	100	10-03-21	14-03-21	17-03-21	17-03-21	-3	
09.2.1	8th Floor-North Tower-Column	11nos	100	08-03-21	14-03-21	12-03-21	12-03-21	2	
09.2.2	8th Floor-North Tower-Lift Core	2nos	100	08-03-21	14-03-21	14-03-21	20-03-21	-6	
09.2.3	8th Floor-North Tower-Stair Case	2nos	100	15-03-21	19-03-21	05-04-21	05-04-21	-17	
09.2.4	8th Floor-North Tower-Roof Slab	958m2	100	15-03-21	19-03-21	05-04-21	05-04-21	-17	
10.1.1	9th Floor-South Tower-Column	14nos	100	15-03-21	21-03-21	28-03-21	31-03-21	-10	
10.1.2	9th Floor-South Tower-Lift Core	2nos	100	15-03-21	21-03-21	28-03-21	06-04-21	-16	
10.1.3	9th Floor-South Tower-Stair	2nos	100	22-03-21	26-03-21	13-04-21	13-04-21	-18	


WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)	Not Yet
10.1.4	9th Floor-South Tower-Roof Slab	963m2	100	22-03-21	26-03-21	13-04-21	13-04-21	-18	
10.2.1	9th Floor-North Tower-Column	11nos	100	20-03-21	26-03-21	09-04-21	09-04-21	-14	
10.2.2	9th Floor-North Tower-Lift Core	2nos	100	20-03-21	26-03-21	12-04-21	16-04-21	-21	
10.2.3	9th Floor-North Tower-Stair	2nos	100	27-03-21	31-03-21	23-04-21	23-04-21	-23	
10.2.4	9th Floor-North Tower-Roof Slab	958m2	100	27-03-21	31-03-21	23-04-21	23-04-21	-23	
11.1.1	10th Floor-South Tower-Column	14nos	100	27-03-21	02-04-21	17-04-21	17-04-21	-15	
11.1.2	10th Floor-South Tower-Lift Core	2nos	100	27-03-21	02-04-21	17-04-21	21-04-21	-19	
11.1.3	10th Floor-South Tower-Stair	2nos	100	03-04-21	07-04-21	04-05-21	04-05-21	-27	
11.1.4	10th Floor-South Tower-Roof Slab	963m2	100	03-04-21	07-04-21	04-05-21	04-05-21	-27	
11.2.1	10th Floor-North Tower-Column	11nos	100	01-04-21	07-04-21	27-04-21	27-04-21	-20	
11.2.2	10th Floor-North Tower-Lift Core	2nos	100	01-04-21	07-04-21	29-04-21	02-05-21	-25	
11.2.3	10th Floor-North Tower-Stair	2nos	100	08-04-21	12-04-21	10-05-21	10-05-21	-28	
11.2.4	10th Floor-North Tower-Roof Slab	958m2	100	08-04-21	12-04-21	10-05-21	10-05-21	-28	
12.1.1	11th Floor-South Tower-Column	14nos	100	08-04-21	14-04-21	09-05-21	09-05-21	-25	
12.1.2	11th Floor-South Tower-Lift Core	2nos	100	08-04-21	14-04-21	09-05-21	12-06-21	-59	
12.1.3	11th Floor-South Tower-Stair	2nos	100	15-04-21	19-04-21	02-09-21	02-09-21	-136	
12.1.4	11th Floor-South Tower-Roof Slab	963m2	100	15-04-21	19-04-21	02-09-21	02-09-21	-136	
12.2.1	11th Floor-North Tower-Column	11nos	100	13-04-21	19-04-21	31-05-21	04-06-21	-46	
12.2.2	11th Floor-North Tower-Lift Core	2nos	50	13-04-21	19-04-21	15-06-21	15-06-21	-57	Completed

WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)	Not Yet
12.2.3	11th Floor-North Tower-Stair	2nos	0	20-04-21	24-04-21			0	Started
12.2.4	11th Floor-North Tower-Roof Slab	958m2	0	20-04-21	24-04-21			0	Started
13.1.1	12th Floor-South Tower-Column	13nos		20-04-21	26-04-21			0	Started
13.1.2	12th Floor-South Tower-Lift Core	2nos		20-04-21	26-04-21			0	Started
13.2.1	12th Floor-North Tower-Column	11nos		25-04-21	01-05-21			0	Started
13.2.2	12th Floor-North Tower-Lift Core	2nos		25-04-21	01-05-21			0	Started


DAILY MANPOWER

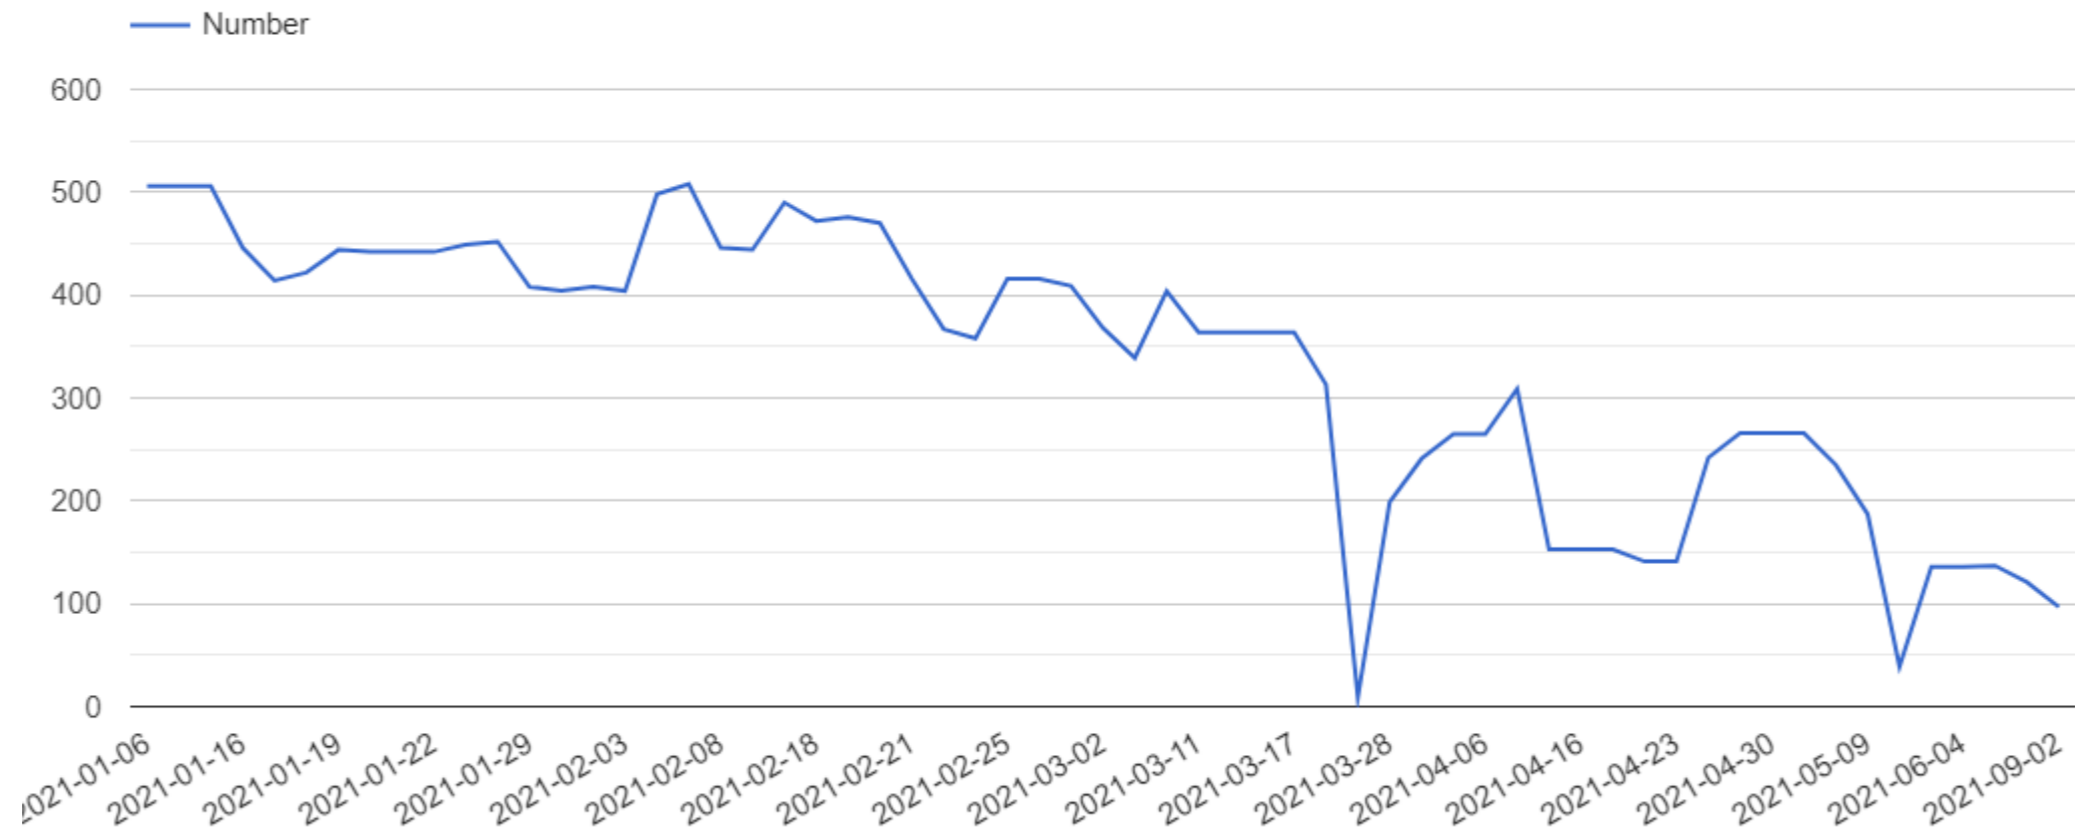


CUMMULATIVE ACTUAL WORK PROGRESS

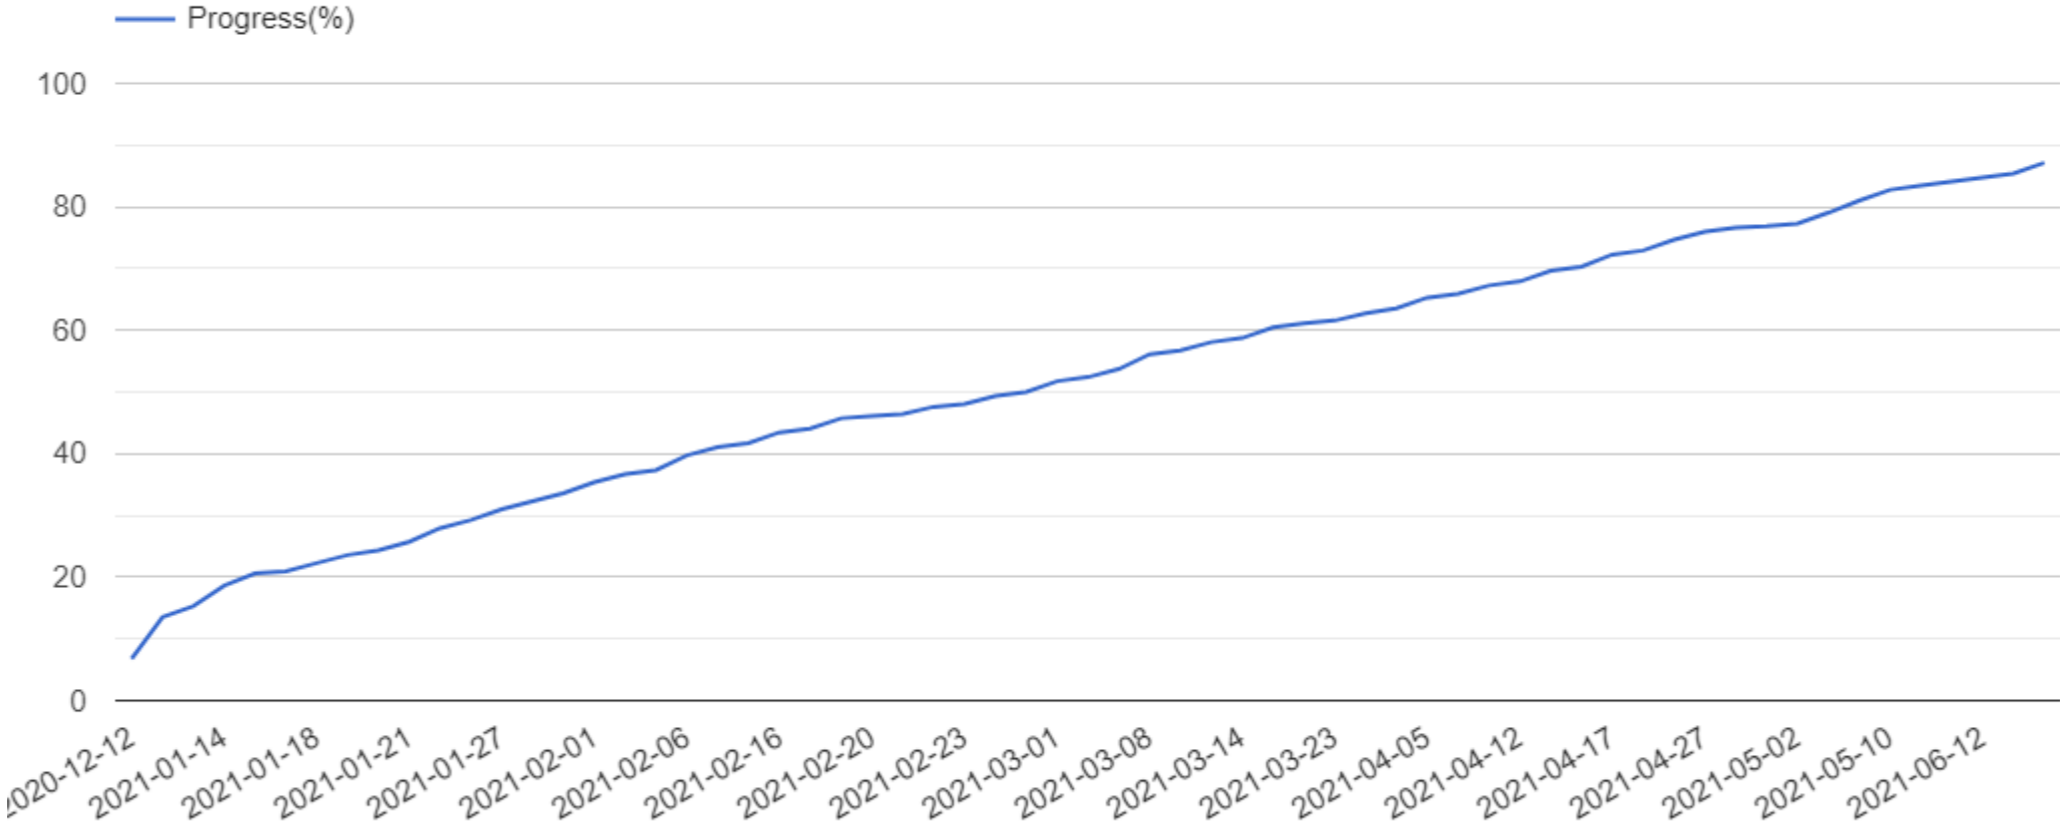


CUMMULATIVE PLAN WORK PROGRESS

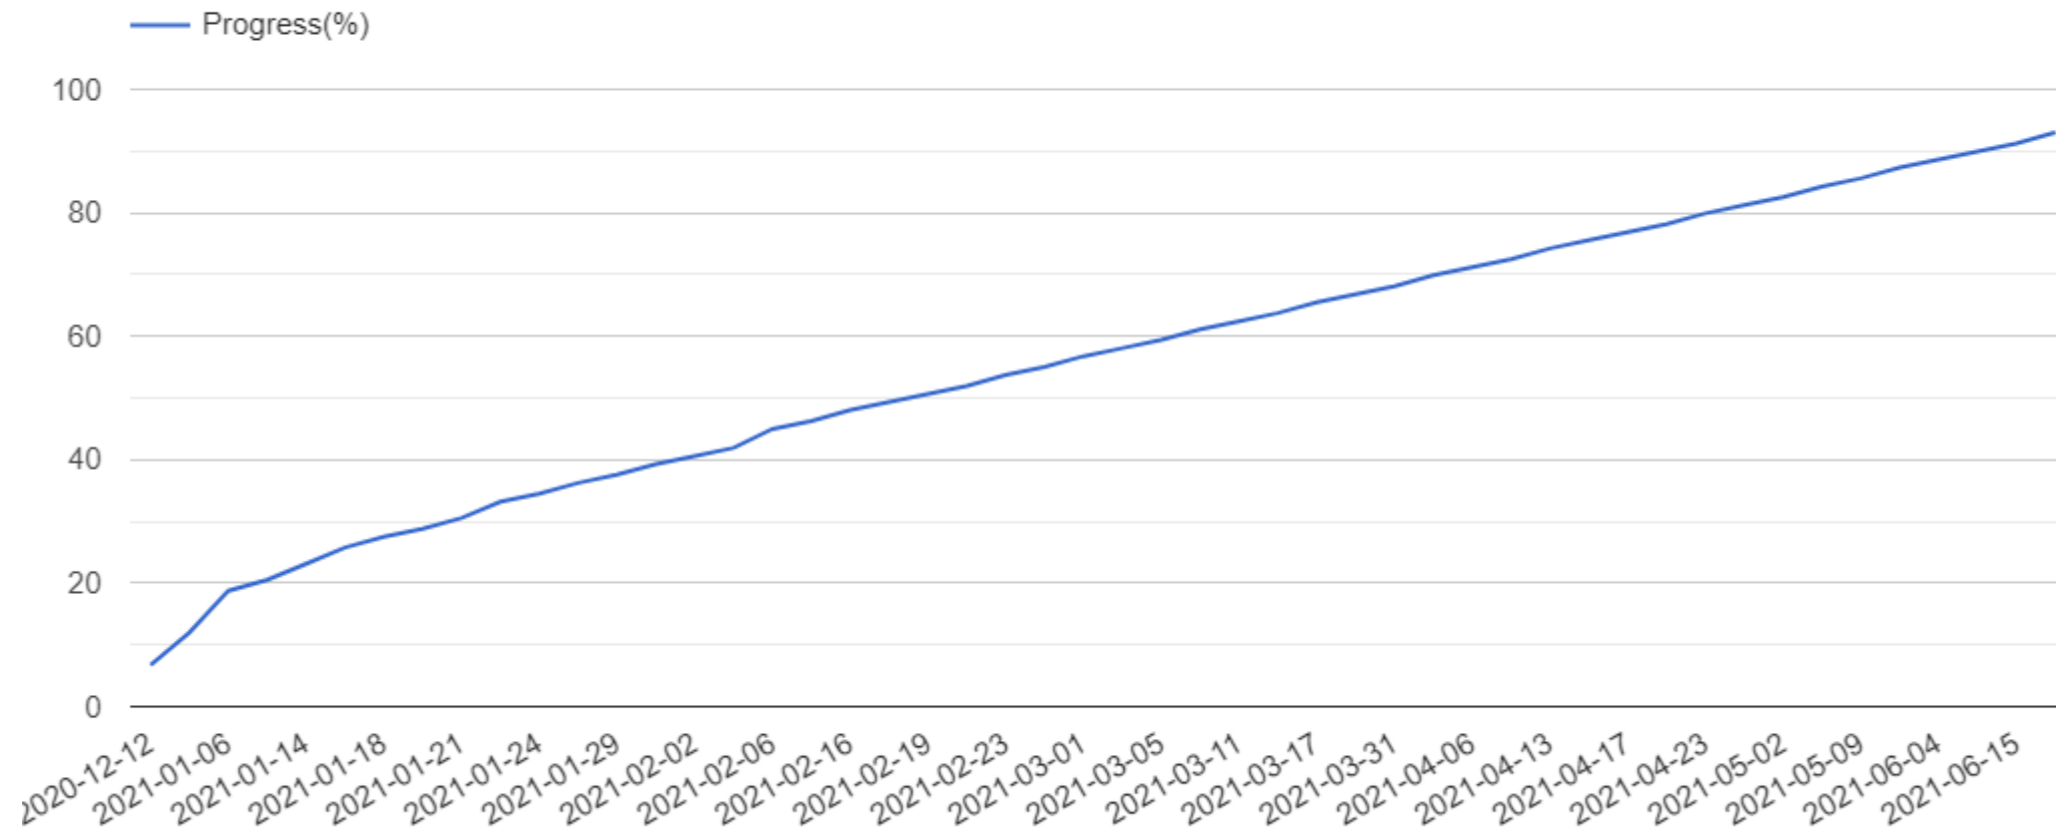

CUMMULATIVE WORK PROGRESS

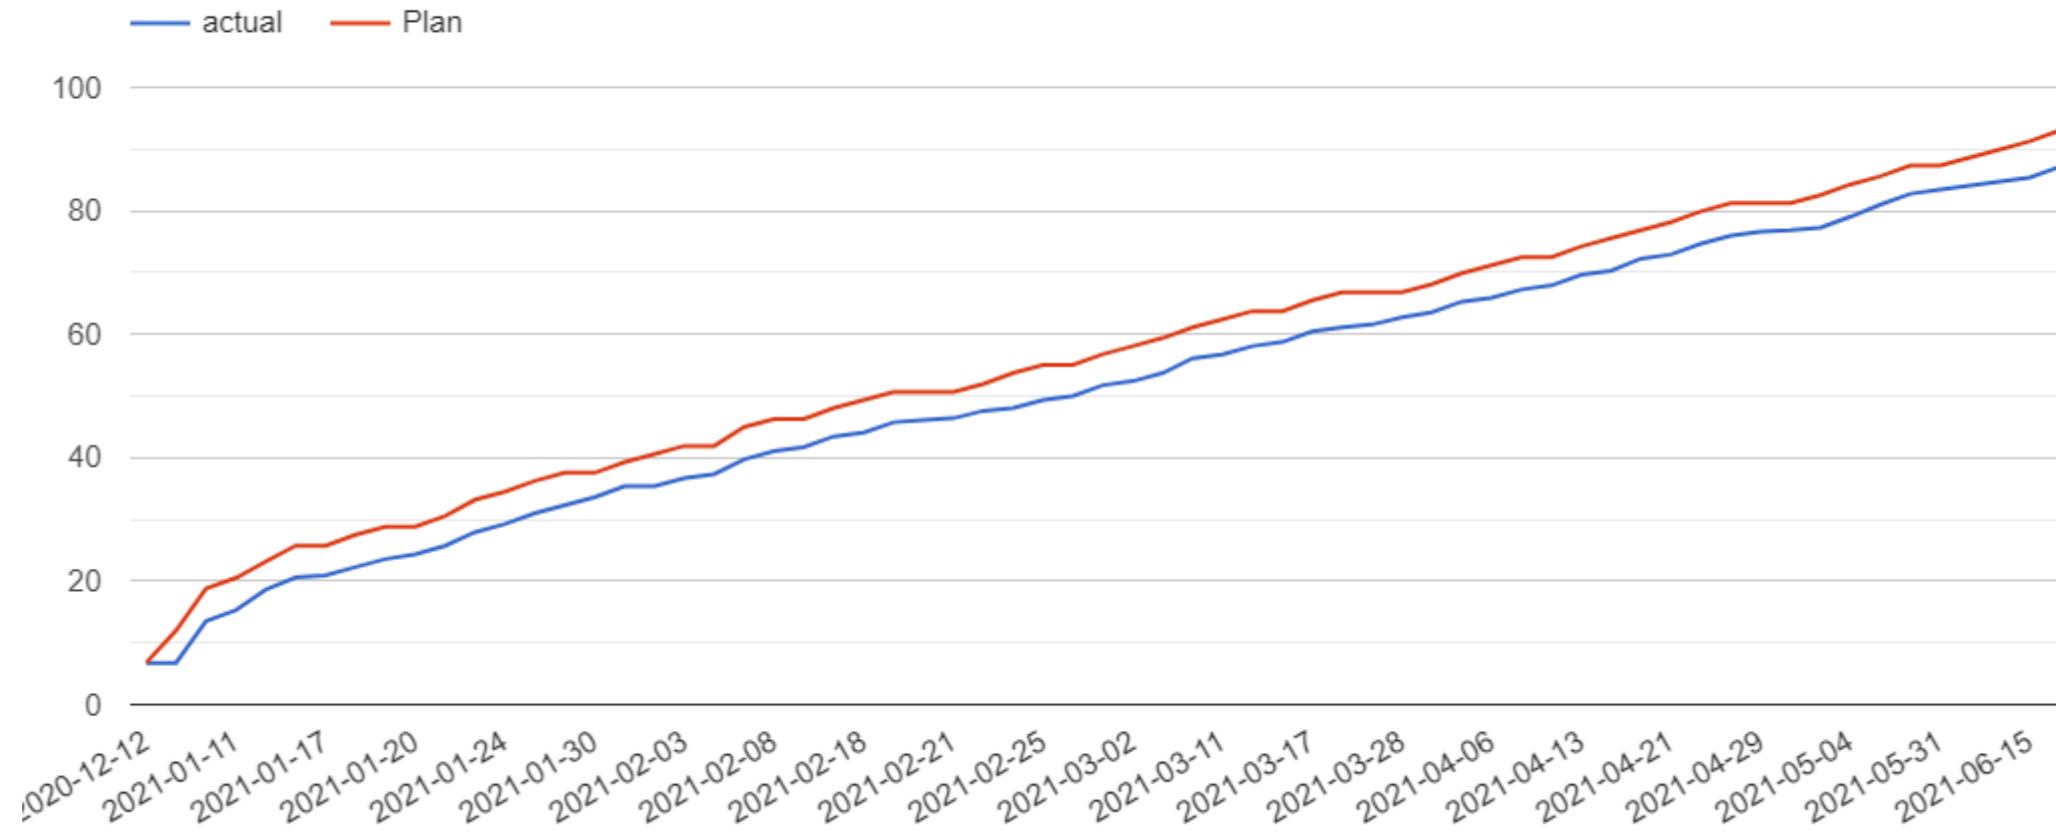

SCHEDULE AHEAD-BEHIND

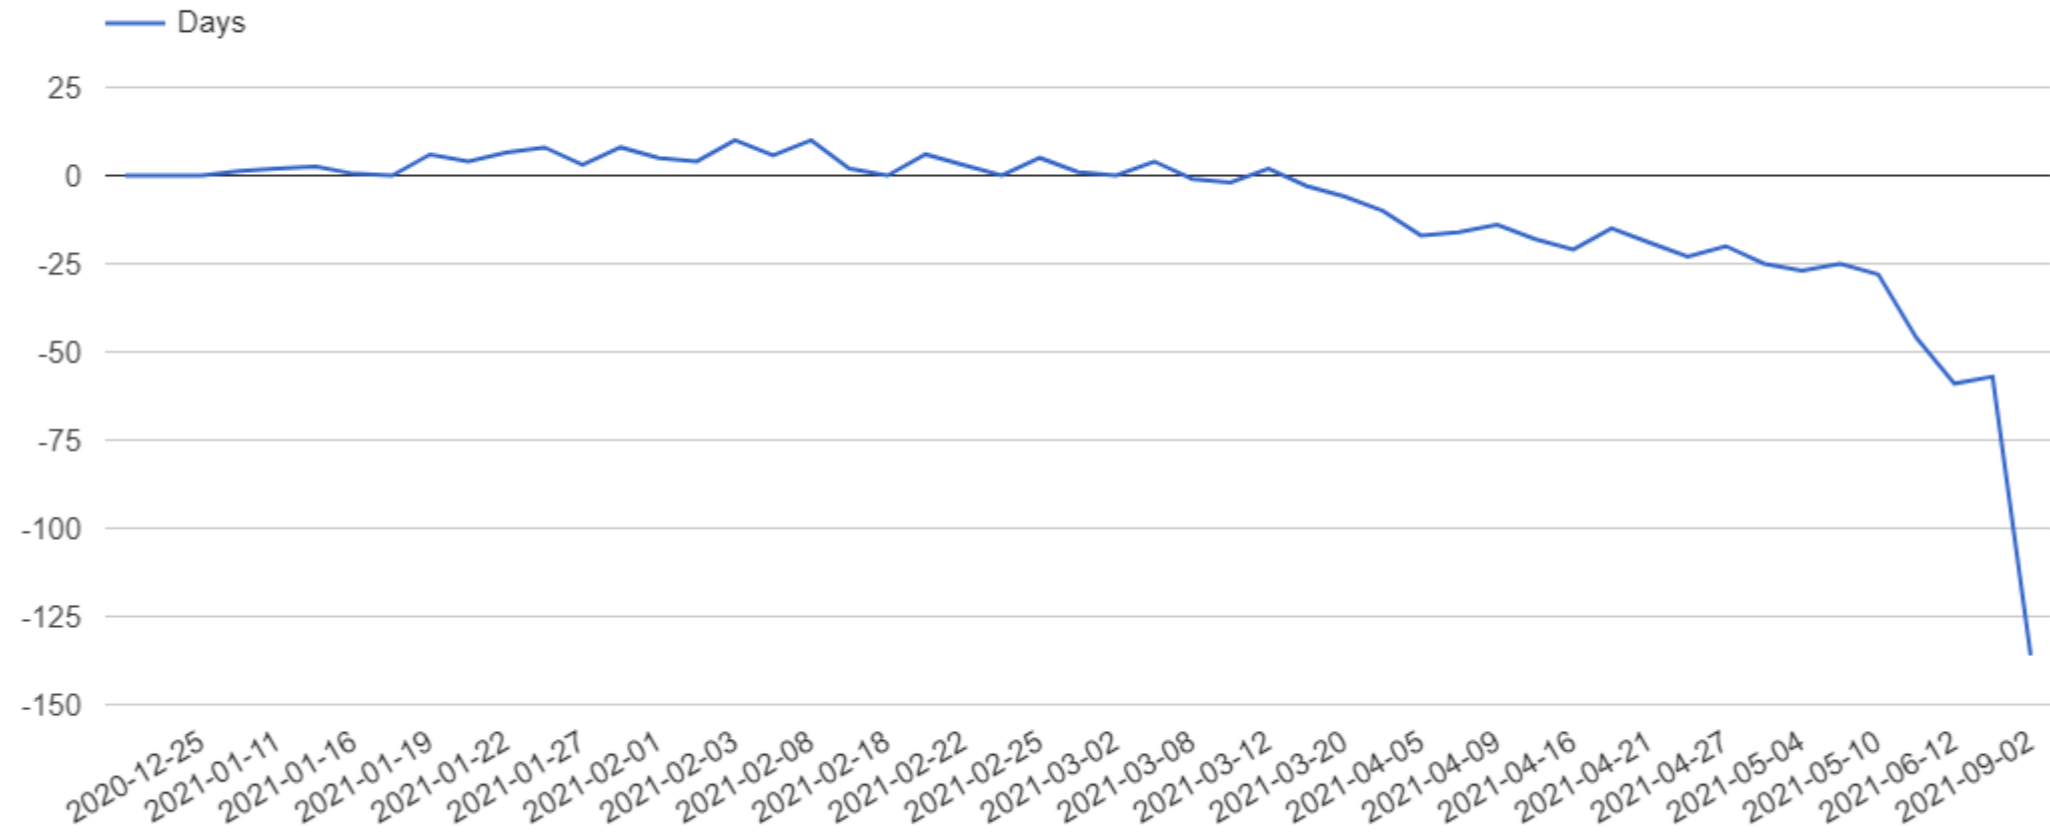

MONTHLY REPORT
DAILY REPORT



MONTHLY PROGRESS REPORT

From 1-September-2021 to 2-September-2021


Project Code:	42	Name:	NBL Tower-Superstucure
Client:	National Bank Limited	Contractor:	Cityscape International Ltd.

Monthly Progress


WBS	Task	Total Qty	Upto Last Month(%)	This Month(%)	Total Done(%)	Schedule Start	Schedule Finish	Actual Finish
12.1.3	11th Floor-South Tower-Stair	2nos	0	100	100	15-04-21	19-04-21	02-09-21
12.1.4	11th Floor-South Tower-Roof Slab	963m2	0	100	100	15-04-21	19-04-21	02-09-21

MANPOWER HISTOGRAM

Abu Sayed Cityscape Civil Worker Cityscape Staff-NBL
Elite Force Security-NBL

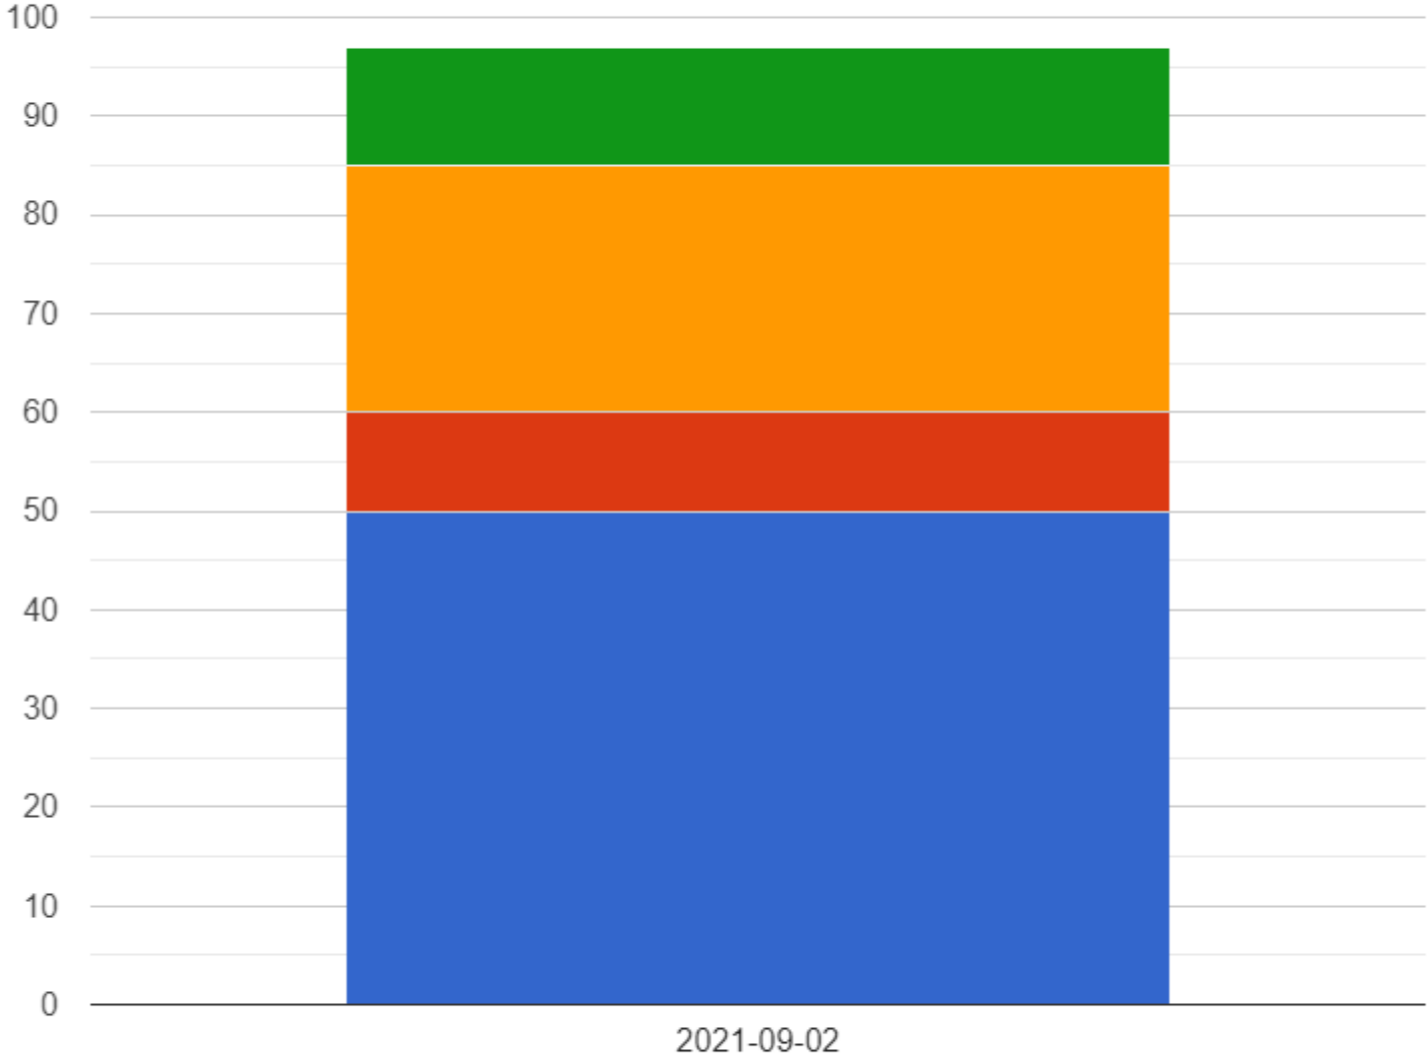

DAILY PROGRESS

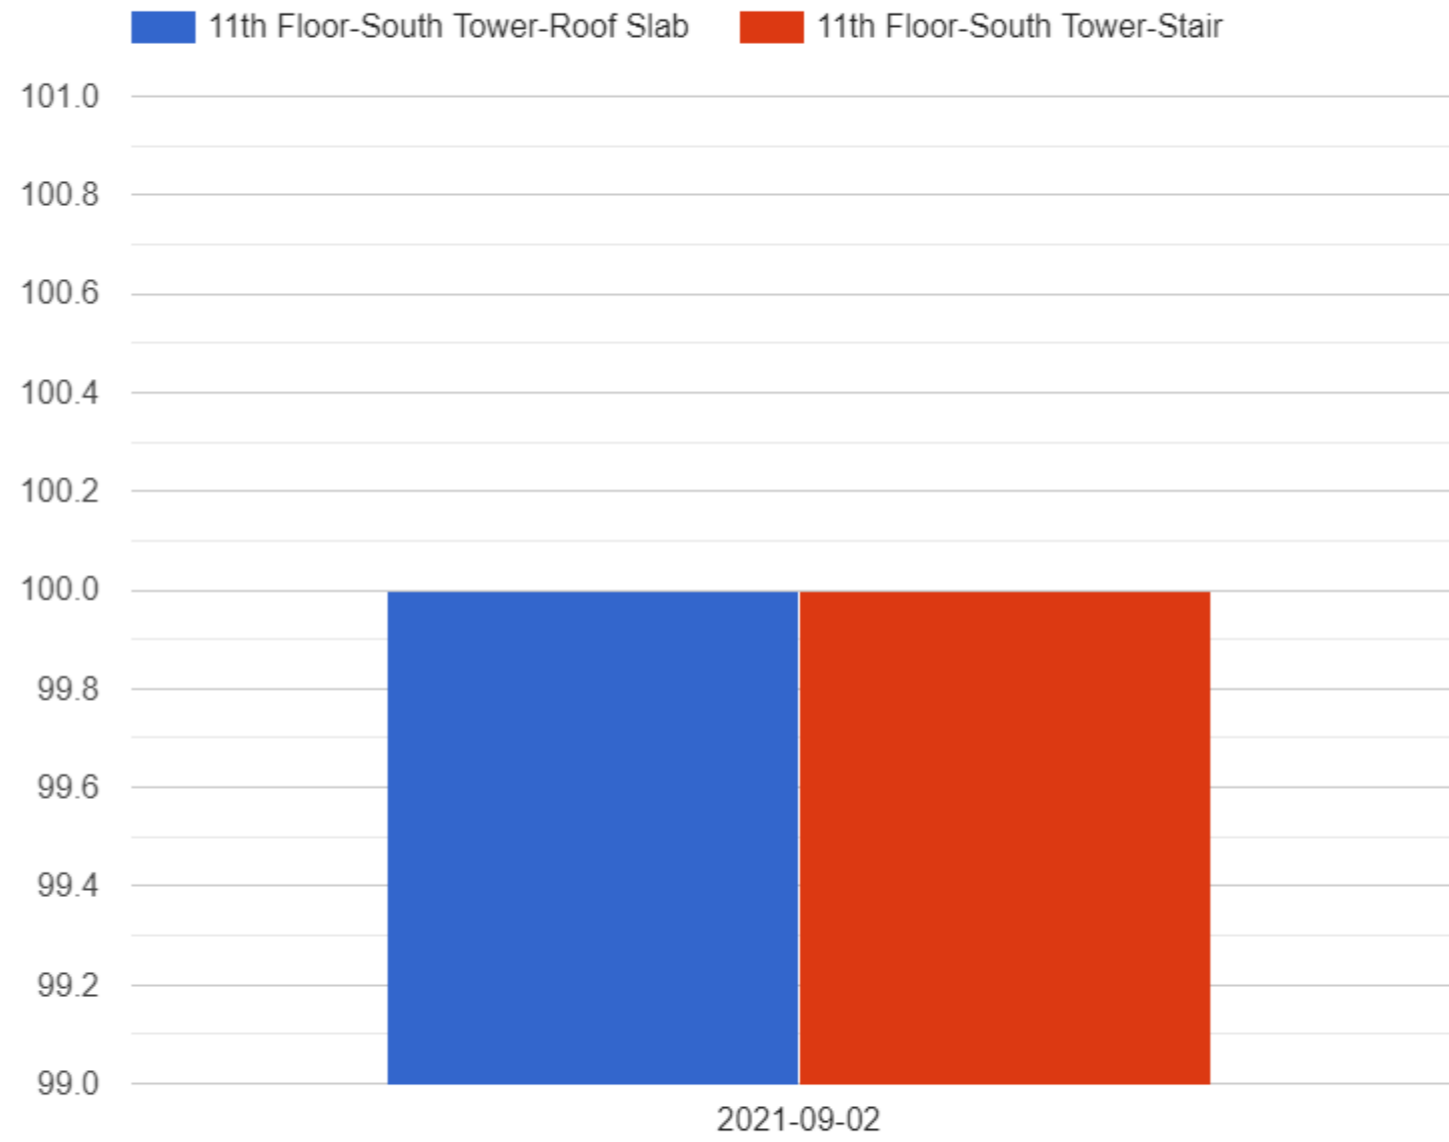

Project:	NBL Tower-Superstucure	Project Code:	42	Date:	2-September-2021
Client:	National Bank Limited	Report	061	Day	Thursday
Contractor:				Climate	Sunny
					28-34C

Manpower

SN	Description	Nos.
01	Cityscape Staff-NBL	25
02	Elite Force Security-NBL	12
03	Abu Sayed	50
04	Cityscape Civil Worker	10
TOTAL		97

Progress This Day

WBS	Task	Total Qty	Today Done(%)	Total Done(%)	Schedule Start	Schedule Finish
12.1.3	11th Floor-South Tower-Stair	2nos	100	100	15-04-21	19-04-21
12.1.4	11th Floor-South Tower-Roof Slab	963m2	100	100	15-04-21	19-04-21

Site Photographs



South Tower 11th Floor Slab Concreting

South Tower 11th Floor Slab Concreting

Site Description

Site Instruction

Entry by:


Generated by:

Planning Engineer


www.bel3c.com, Developed by: Engr. Md. Sanaul Haque

WORK PLAN AND PROGRESS

WORK PLAN AND PROGRESS FOR SUPER STRUCTURE OF NBL TWIN TOWER AT KARWANBAZAR, DHAKA

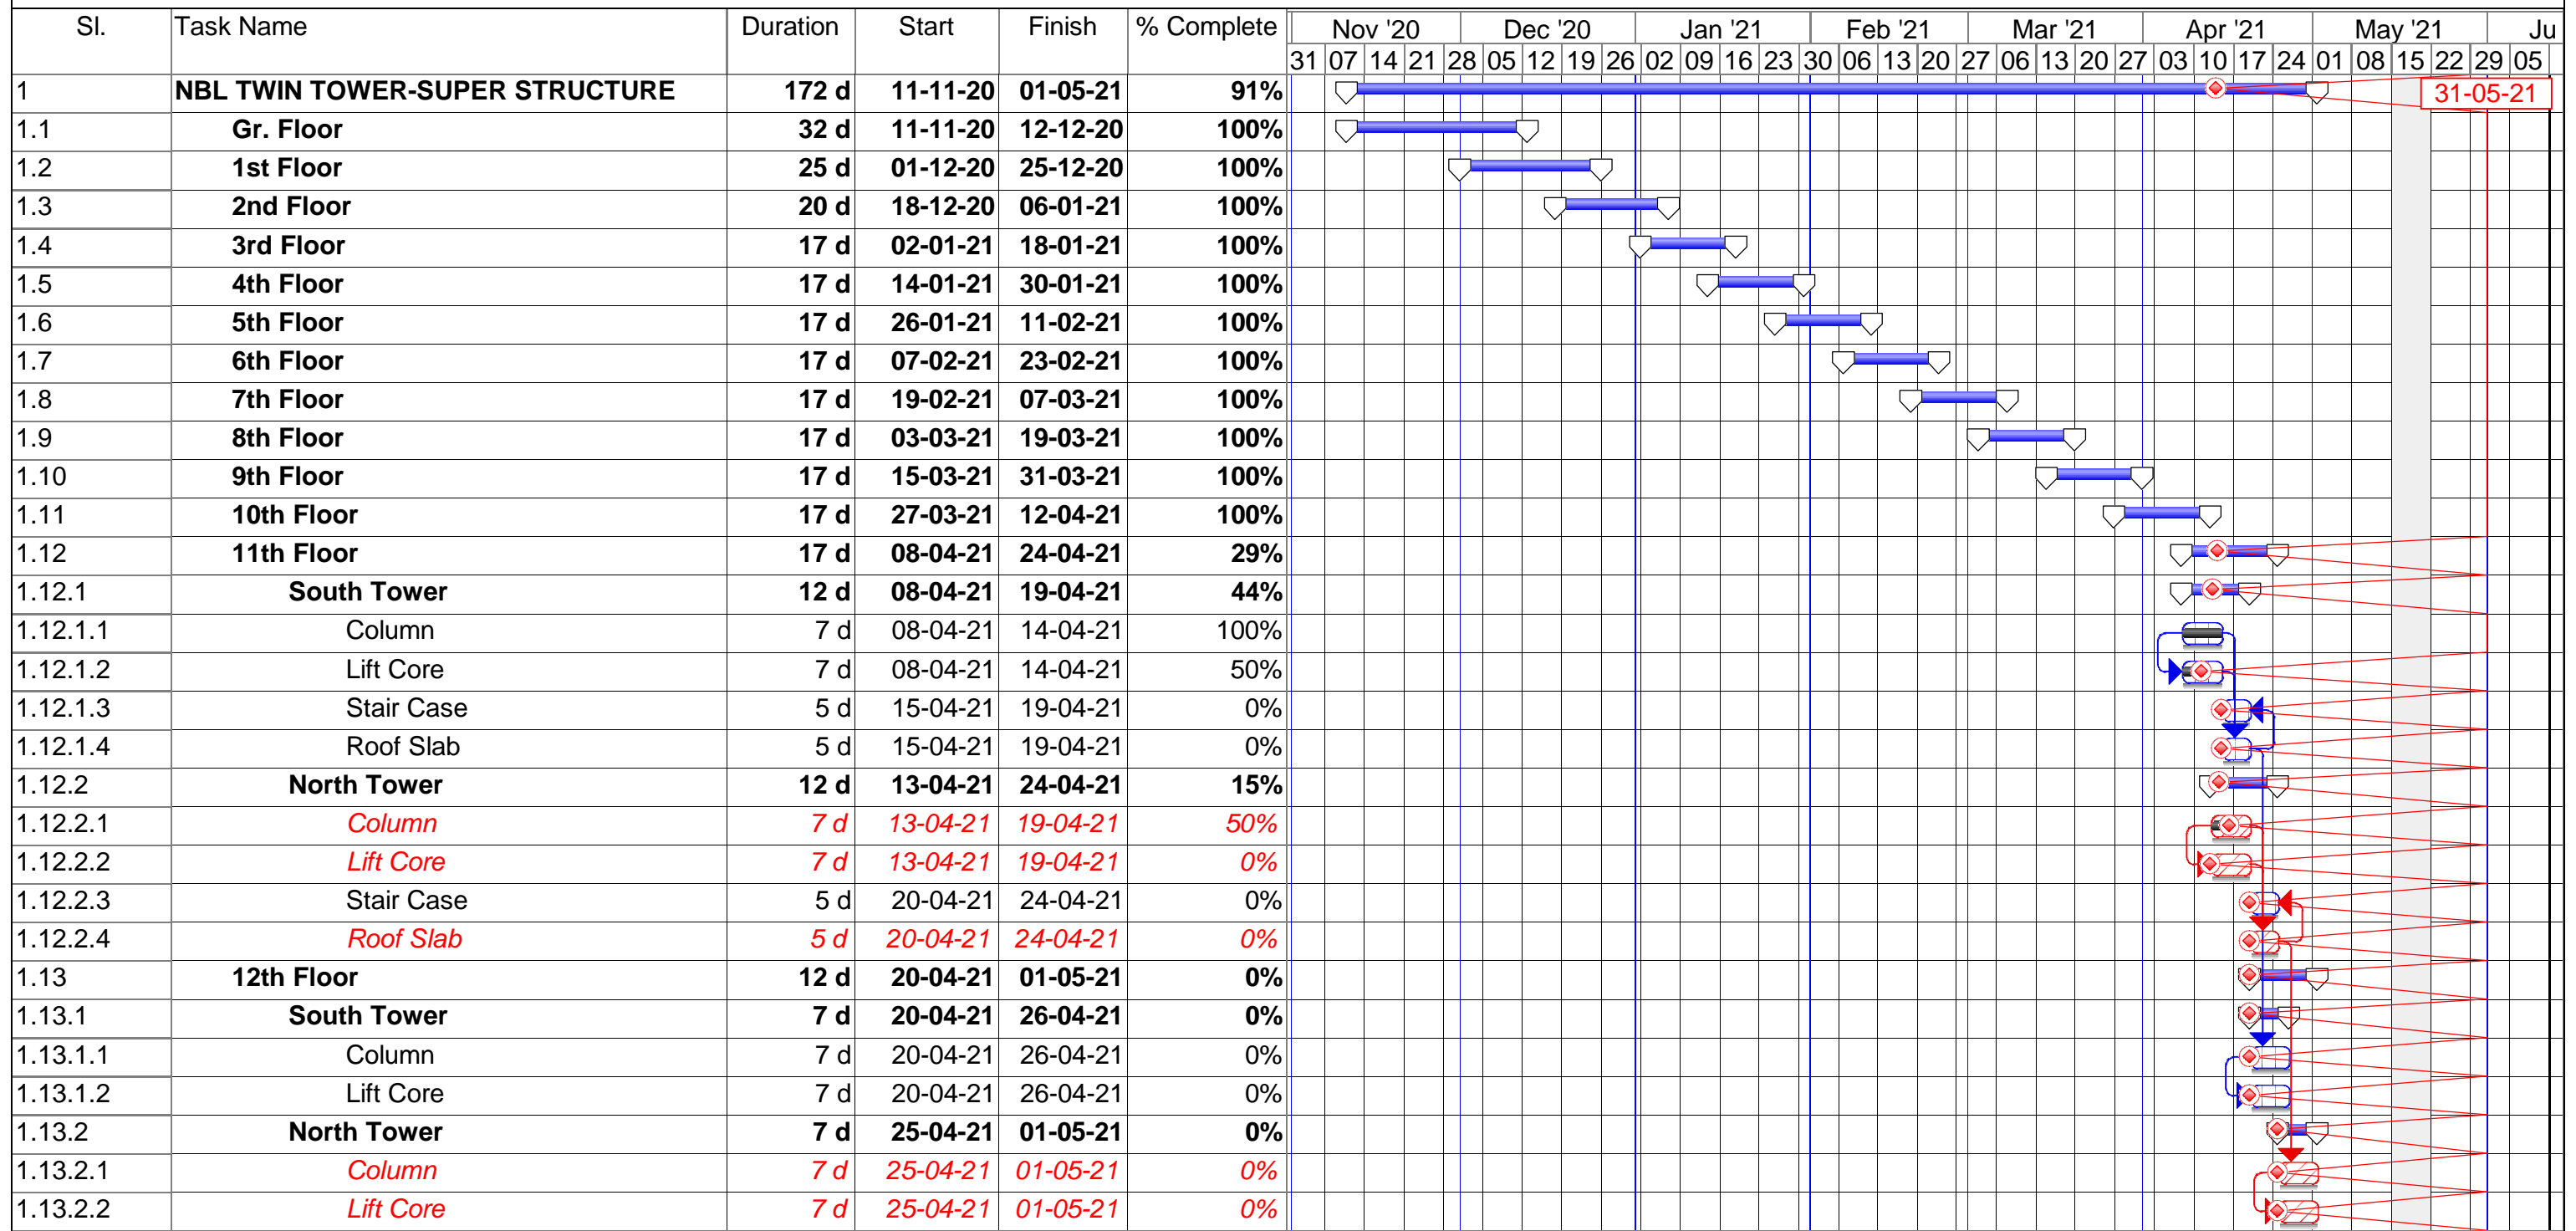

Date: 12-06-21 15.59
Sheet: 1 / 1



PROGRESS PHOTO

Site Photographs



3rd Floor South Tower-Column Complete on 06-01-21



3rd Floor South Tower Lift Core Complete on 06-01-21



3rd Floor South Tower Stair Complete on 11-01-21



3rd Floor South Tower Slab Complete on 11-01-21



Lift Core Wall Shoring on 14-01-21



Re-bar Lifting by Roof Hoist on 14-01-21




Night Shift Working on 16-01-21



Lift Core Wall Shuttering on 16-01-21



Lift Core Wall Shuttering on 17-01-21

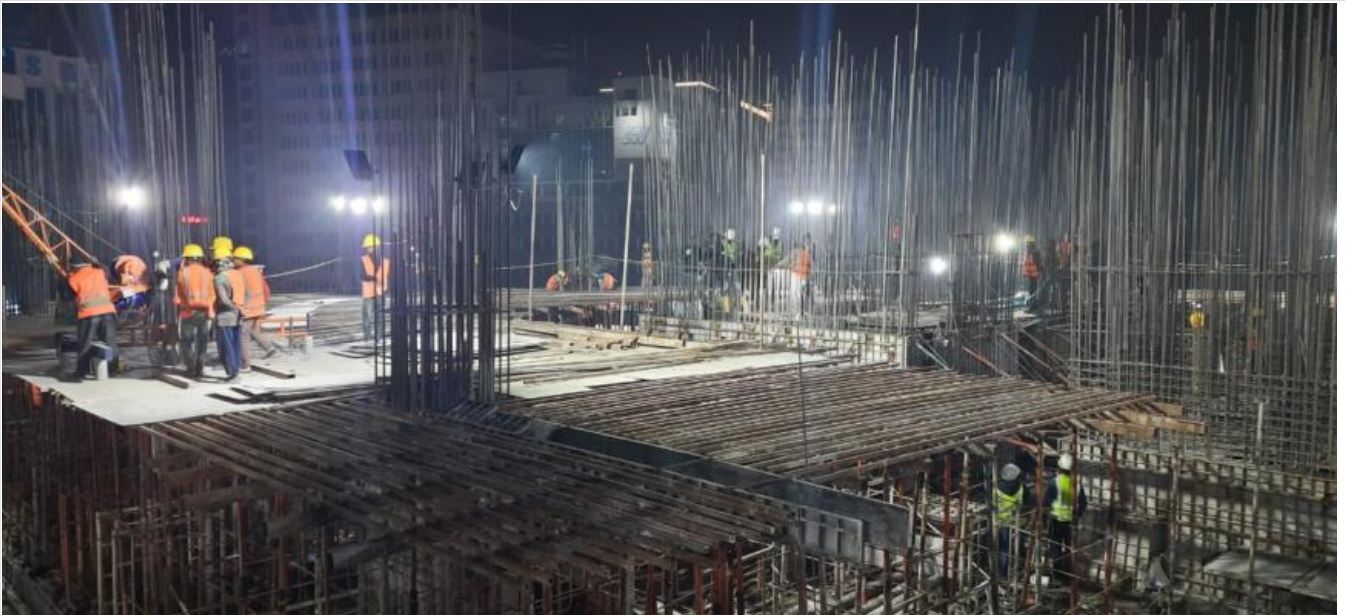

Re-bar Lifting by Roof Hoist on 17-01-21



Re-bar Work on 18-01-21



on 18-01-21



on 19-01-21



on 19-01-21



South Tower 4th Floor Roof Slab Running on 20-01-21



North Tower 4th Floor Lift Core Running on 20-01-21



South Tower 4th Floor Roof Slab Concreti on 21-01-21



Night Shift Working on 21-01-21



Curing after 4F South Tower Slab Concret on 22-01-21



Re-bar Work on 22-01-21



Project Picture on 24-01-21



Project Picture on 24-01-21



Slab Re-bar Work on 27-01-21



Slab Shuttering on 27-01-21



Project Picture on 29-01-21



Inside Building on 29-01-21



Slab Re-bar Work on 30-01-21



Work Inspection on 30-01-21



Roof Slab on 01-02-21




Inside on 01-02-21



Safety Railing on 03-02-21



Project Picture on 03-02-21

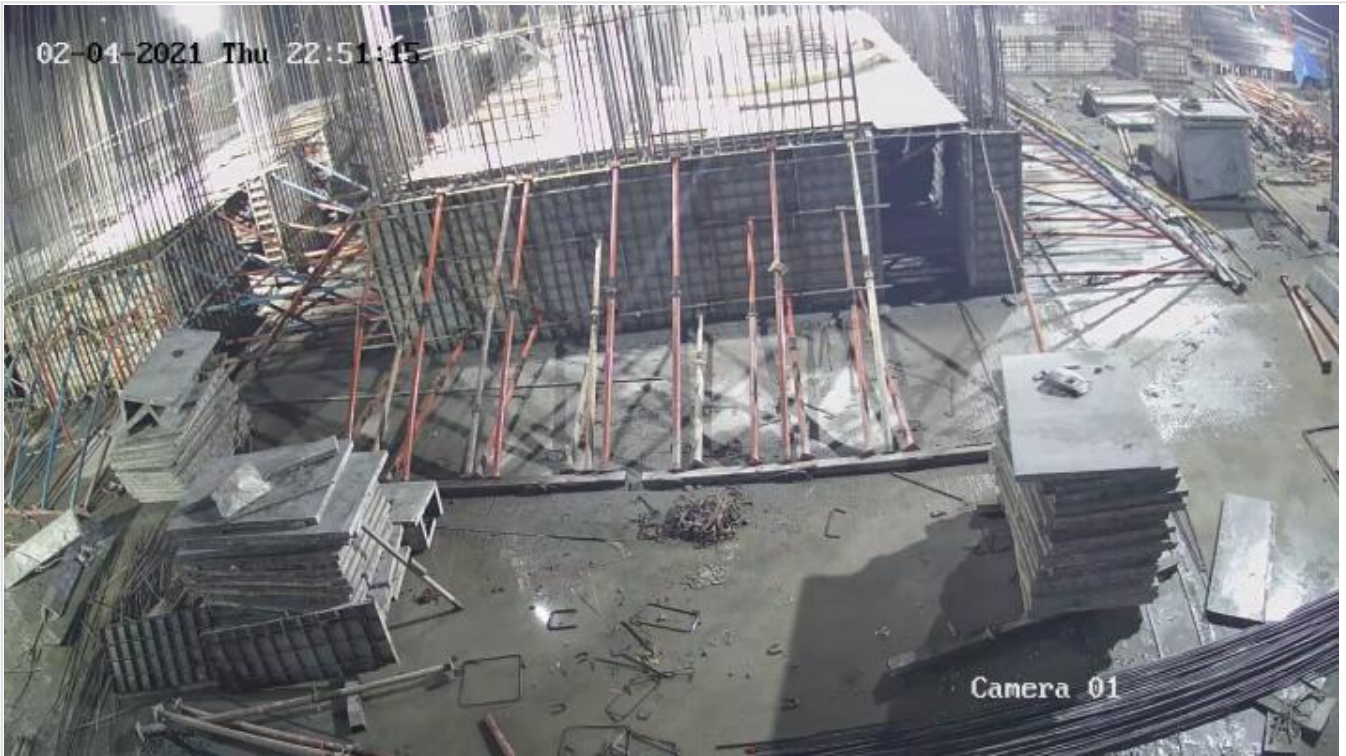

Night Shift Working on 04-02-21



Night Shift Working on 04-02-21



Project View from East Side on 06-02-21



Project View from West Side on 06-02-21



View from East Side on 08-02-21



View from West Side on 08-02-21



Project was closed 11-14 Feb 2021 due to on 15-02-21



on 15-02-21



on 16-02-21



on 16-02-21



on 18-02-21



on 18-02-21



on 19-02-21



on 19-02-21



on 20-02-21




on 20-02-21



on 21-02-21



on 21-02-21

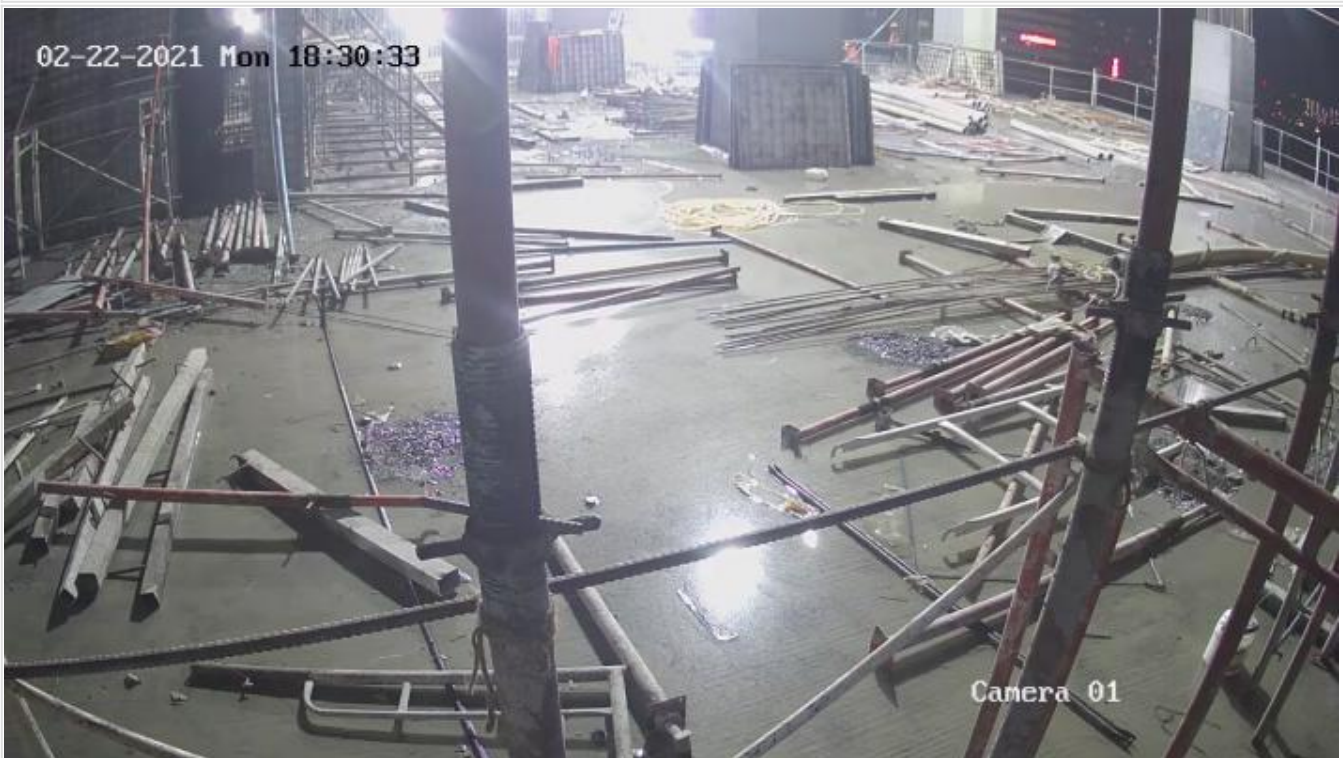

on 22-02-21



on 22-02-21



on 23-02-21



on 23-02-21



on 25-02-21



on 25-02-21



on 26-02-21



on 26-02-21



on 01-03-21



on 01-03-21



on 02-03-21




on 02-03-21



on 05-03-21



on 05-03-21

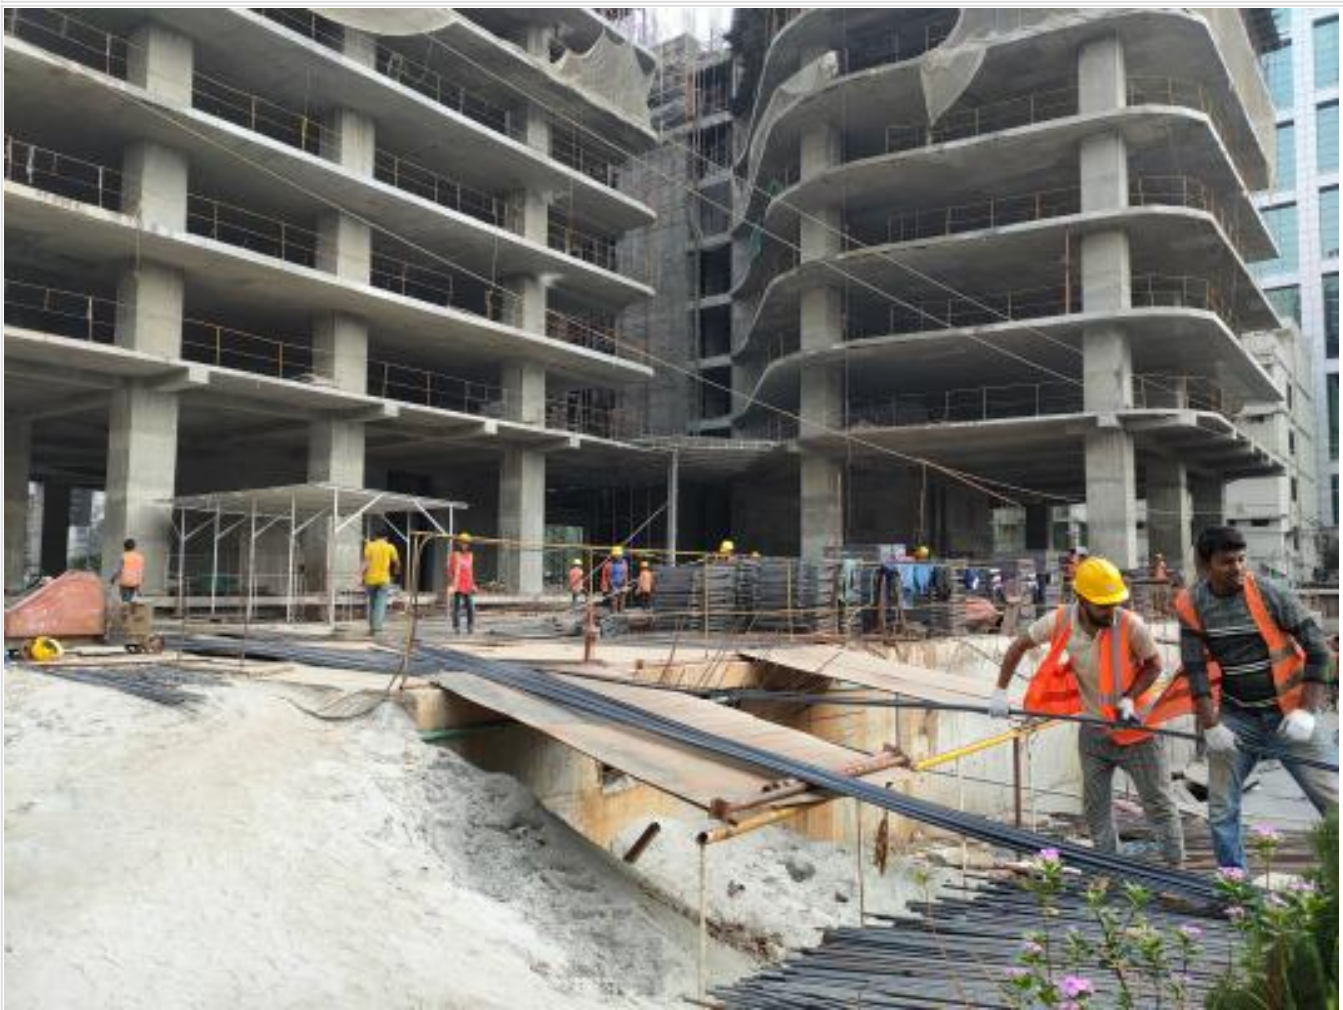



on 08-03-21



on 11-03-21



on 11-03-21



on 12-03-21



on 12-03-21



on 14-03-21



on 14-03-21



on 17-03-21



on 17-03-21



on 20-03-21



on 20-03-21



View from East Side on 28-03-21



View from East Side on 28-03-21




View from East Side on 31-03-21



Night Shift Working on 31-03-21



8th Floor North Tower Roof Slab Casting on 05-04-21

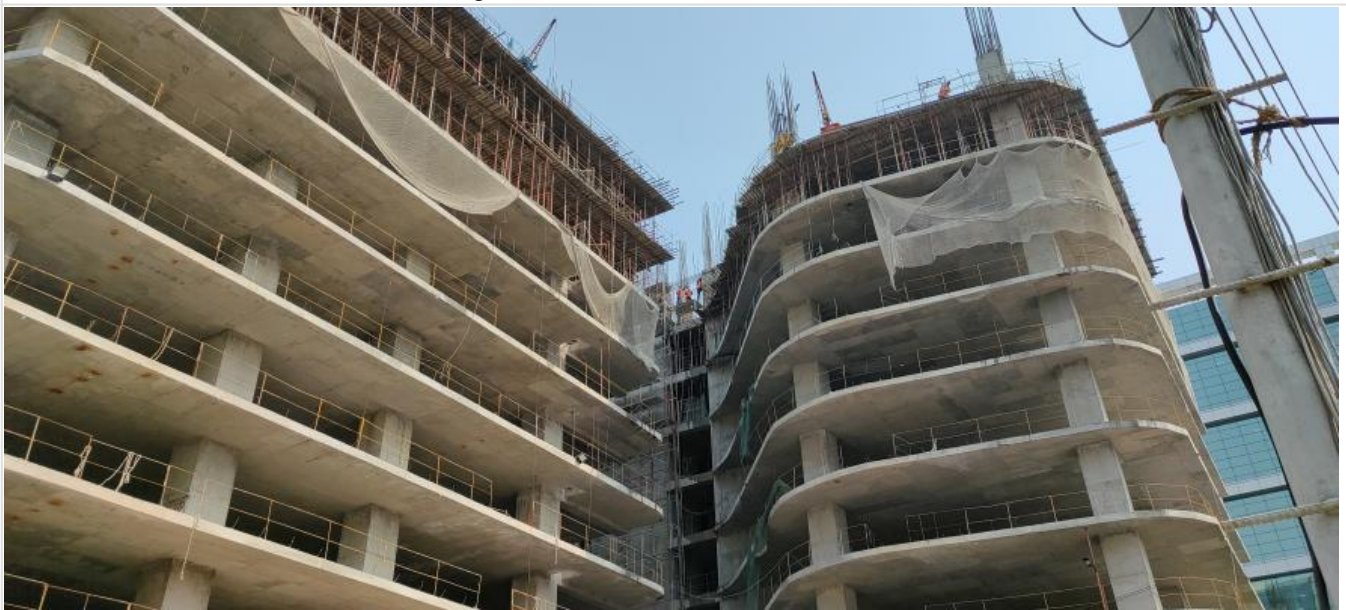

8th Floor North Tower Roof Slab Casting on 05-04-21



on 06-04-21



on 06-04-21



on 09-04-21



on 09-04-21



on 12-04-21



on 12-04-21



on 13-04-21



South Tower 10th Floor Slab Concreting on 13-04-21



on 16-04-21



on 16-04-21



on 17-04-21



on 17-04-21



on 21-04-21



on 21-04-21



on 23-04-21



on 23-04-21



on 27-04-21



on 27-04-21



on 29-04-21



on 29-04-21



on 30-04-21



on 30-04-21



on 02-05-21



on 02-05-21



on 09-05-21



on 09-05-21



on 10-05-21



on 10-05-21



on 31-05-21



on 31-05-21

Project Closed 11-22 May due to Eid-ul Fitre Vacation



on 04-06-21



on 04-06-21



on 12-06-21



on 12-06-21



on 15-06-21



on 15-06-21



South Tower 11th Floor Slab Concreting on 02-09-21



South Tower 11th Floor Slab Concreting on 02-09-21
