


**CONSTRUCTION OF CHANDAPAHAR RESORT, NILGIRI
AT
BANDARBAN, CHITTAGONG**

PROGRESS REPORT

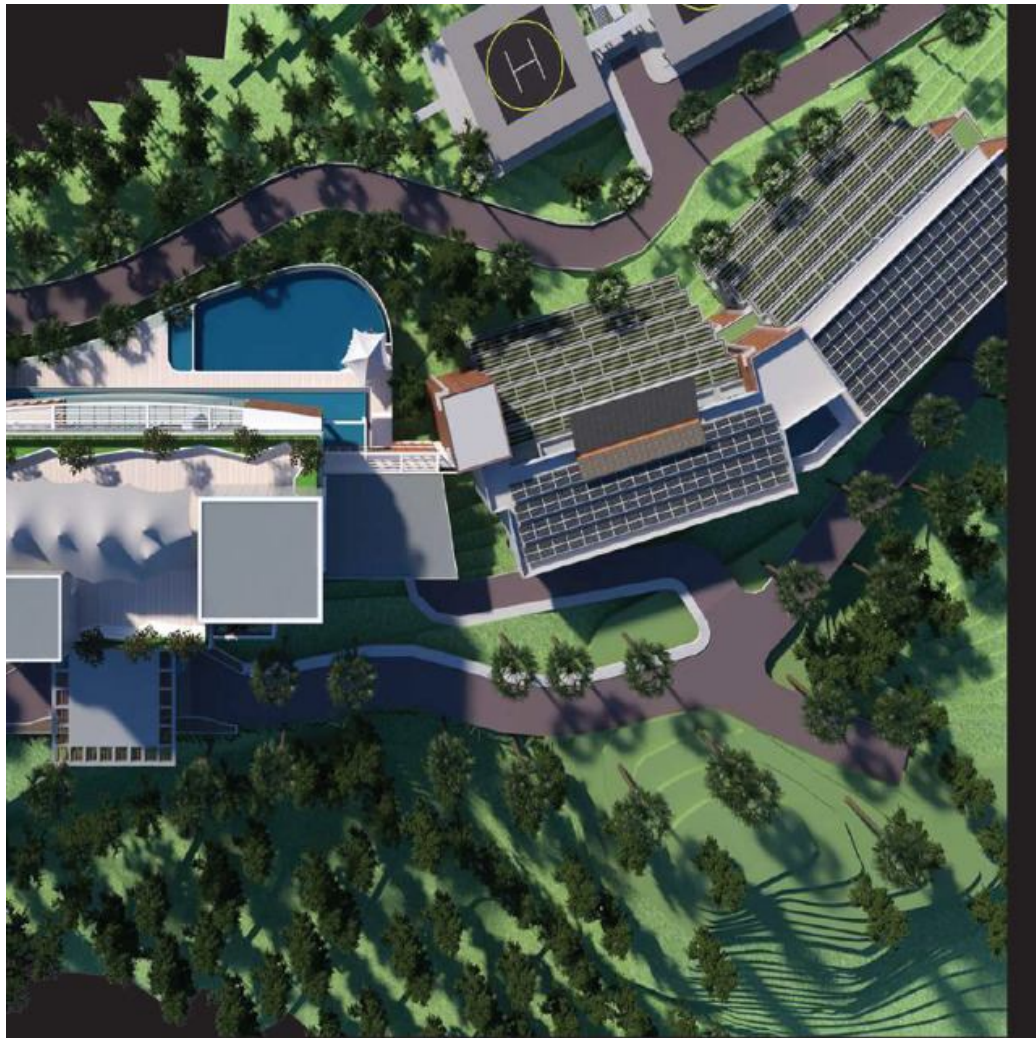

31 OCT 2020 – 21 JAN 2021

Generated by: Cityscape International Ltd

TABLE OF CONTENTS

- TOTAL PROGRESS
- TOTAL MANPOWER CHART
- CUMMULATIVE PROGRESS CHART
- SCHEDULE LEAD-LAG CHART
- LAST MONTH PROGRESS
- LAST MONTH MANPOWER HISTOGRAM
- LAST MONTH PROGRESS CHART
- DAILY PROGRESS REPORT
- WORK PLAN AND PROGRESS
- PROGRESS PHOTO



TOTAL PROGRESS REPORT

From 5-January-2021 to 21-January-2021


Project Code:	49	Name:	Marriot-Nilgiri at Bandarban			
Client:	Contractor:					
Total Duration:	16	days	Total Working Days:	14	Total Manpower:	381
Planning Progress =	28.2%	Actual Progress=	15.8%	SPI=	0.56	Behind Schedule

Total Progress


WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)	Not Yet
03.02	Mobilization-Material for Prelimina		5	08-12-20	05-02-21	13-01-21	13-01-21	23	
03.03.01	Soling n Plaster for PVC Water Tank		80	15-01-21	22-01-21	19-01-21	20-01-21	2	
03.06.02	Mobilization-Mechanics Shed-Frame W		100	15-01-21	22-01-21	12-01-21	20-01-21	2	
03.07	Mobilization-Grass Cutting-Roa		90	28-12-20	26-01-21	05-01-21	07-01-21	19	
03.08.01	Mobilization-Guest House-Layout	130sqm	100	06-01-21	06-01-21	06-01-21	06-01-21	0	
03.08.02	Mobilization-Guest House-Excavation	163cum	100	07-01-21	10-01-21	07-01-21	12-01-21	-2	
03.08.03	Mobilization-Guest House-Footi	16nos	100	08-01-21	12-01-21	12-01-21	15-01-21	-3	
03.08.04	Mobilization-Guest House-Pades	16nos	100	10-01-21	13-01-21	16-01-21	19-01-21	-6	
03.08.05	Mobilization-Guest House-Grade Beam	107m	65	12-01-21	17-01-21	19-01-21	21-01-21	-4	Completed
03.08.06	Mobilization-Guest House-Floor Work	130sqm	0	18-01-21	20-01-21			0	Started
03.08.07	Mobilization-Guest House-Column	16nos	0	21-01-21	24-01-21			0	
03.08.08	Mobilization-Guest House-Brick-work	268sqm	0	24-01-21	30-01-21			0	
03.08.09	Mobilization-Guest House-Tie Beam	107m	0	28-01-21	01-02-21			0	
03.08.10	Mobilization-Guest House-Truss	130sqm	0	26-01-21	31-01-21			0	

WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)	Not Yet
03.08.11	Mobilization-Guest House-San-ElePip	1item	0	31-01-21	01-02-21			0	
03.08.12	Mobilization-Guest House-Grill-DrFm	23nos	0	30-01-21	31-01-21			0	
03.08.13	Mobilization-Guest House-Plaster	536sqm	0	31-01-21	03-02-21			0	
03.08.14	Mobilization-Guest House-Roof Sheet	130sqm	0	01-02-21	03-02-21			0	
03.08.15	Mobilization-Guest House-Tile Work	130sqm	0	31-01-21	03-02-21			0	
03.08.16	Mobilization-Guest House-Painting	536sqm	0	02-02-21	05-02-21			0	
03.08.17	Mobilization-Guest House-Door-Windo	23nos	0	04-02-21	05-02-21			0	
03.08.18	Mobilization-Guest House-San-Ele-Fi	1item	0	03-02-21	05-02-21			0	


DAILY MANPOWER

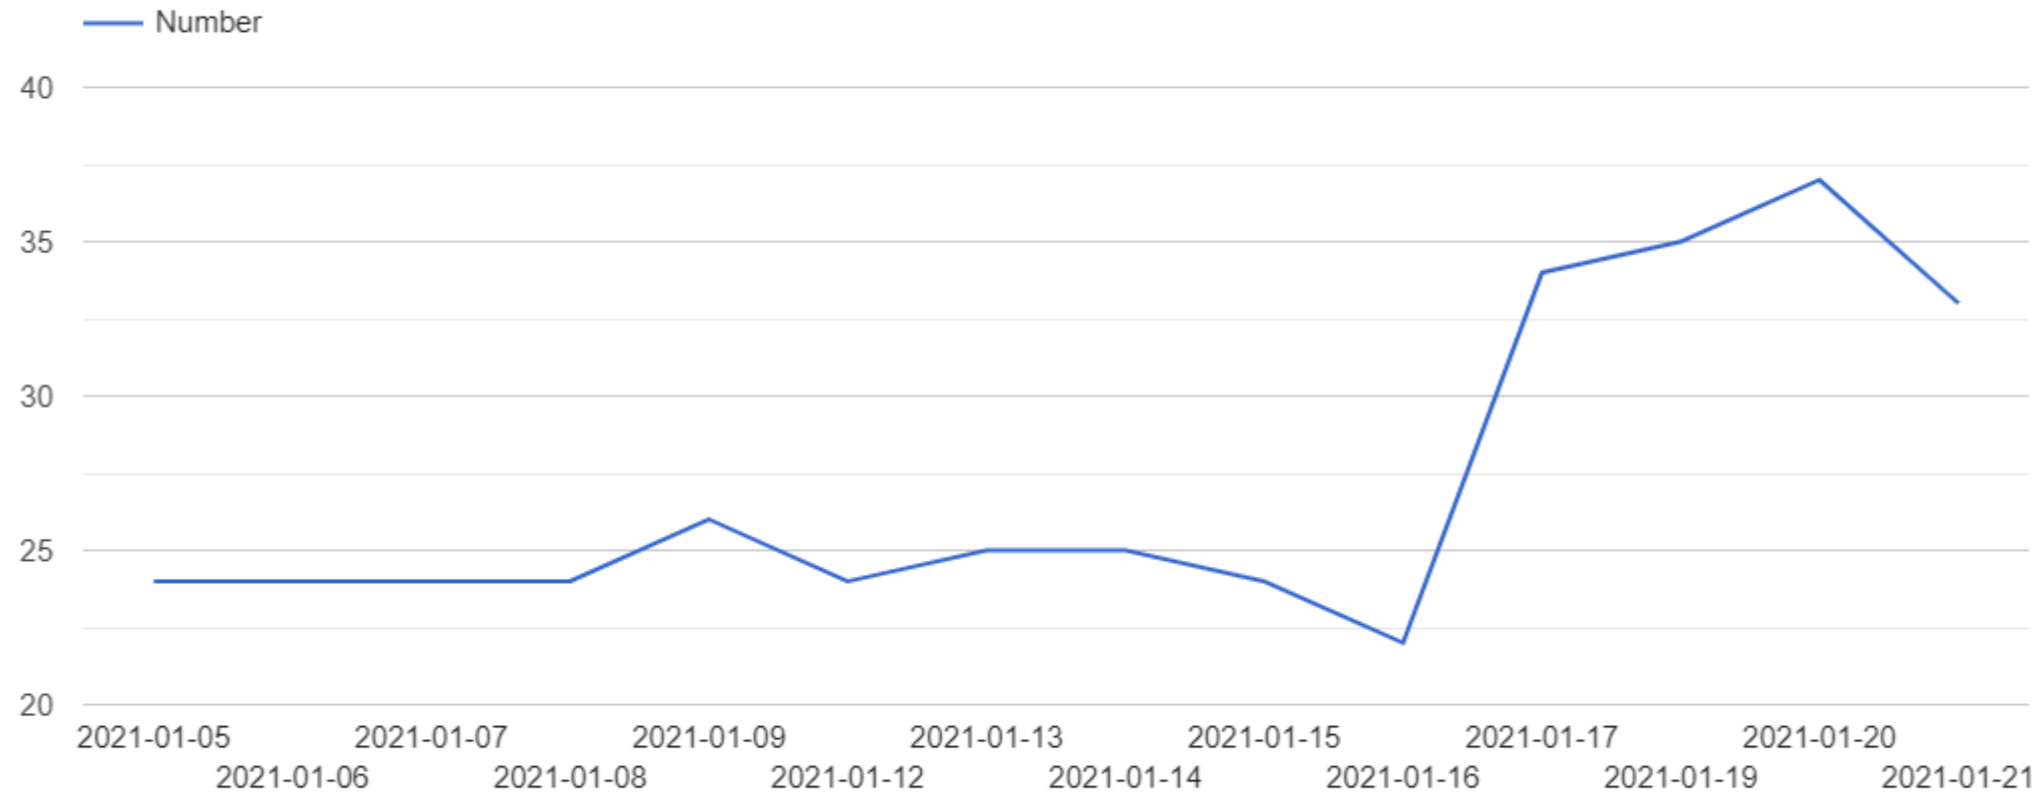


CUMMULATIVE ACTUAL WORK PROGRESS

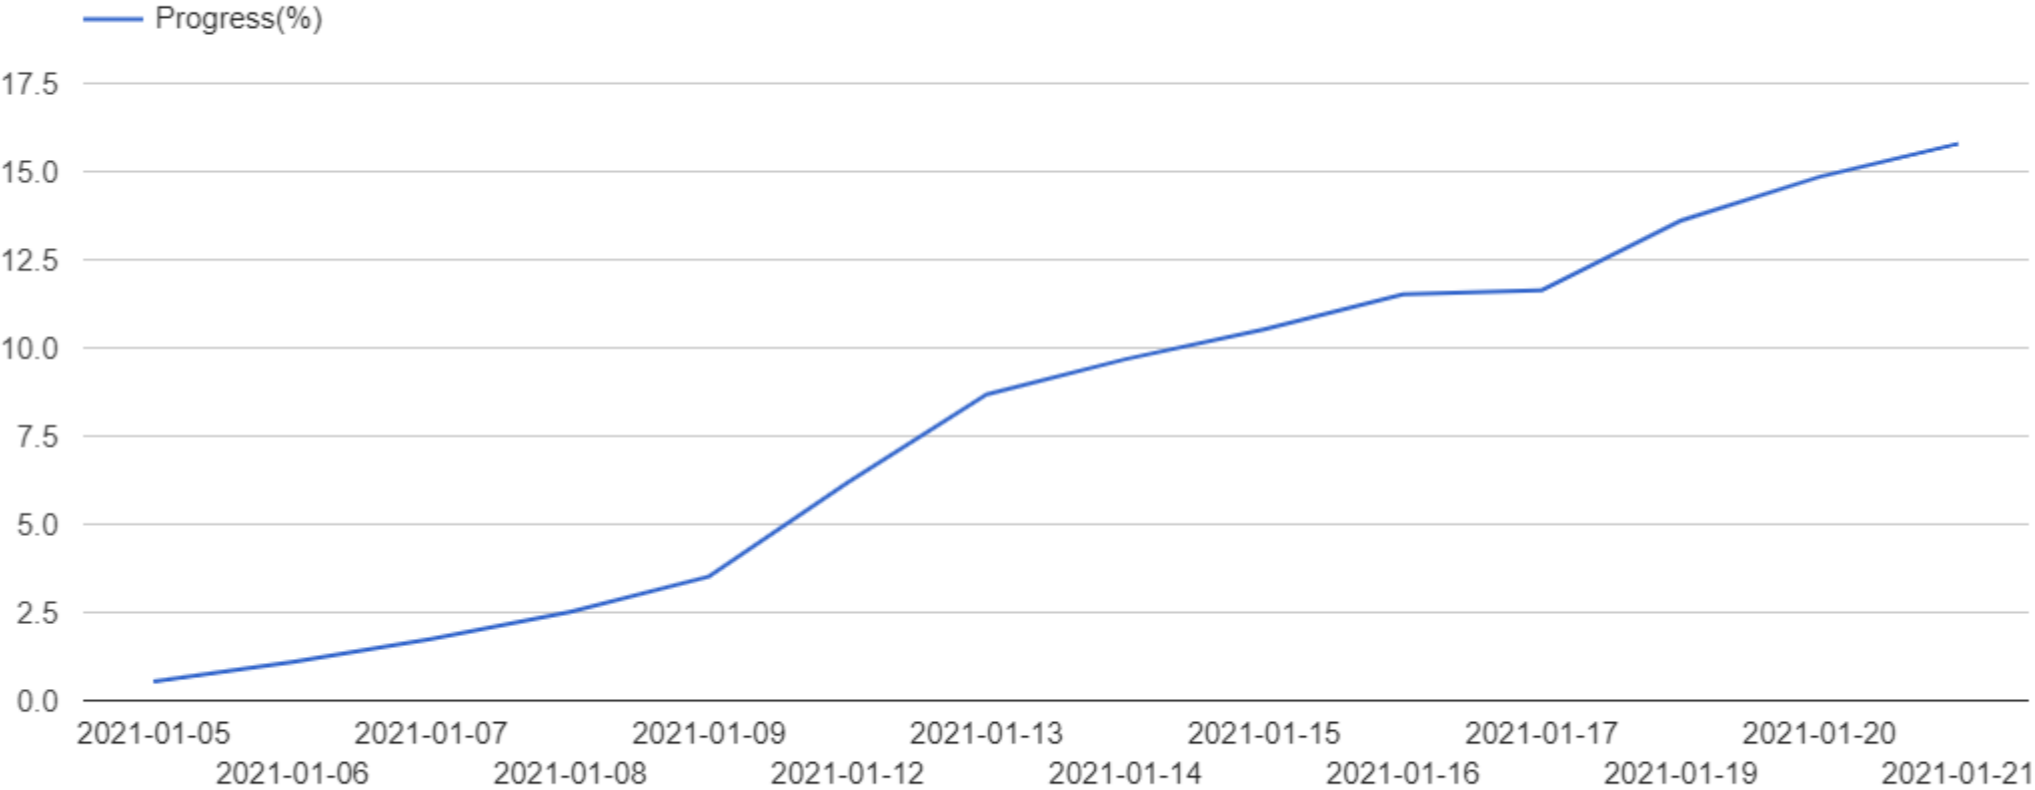


CUMMULATIVE PLAN WORK PROGRESS

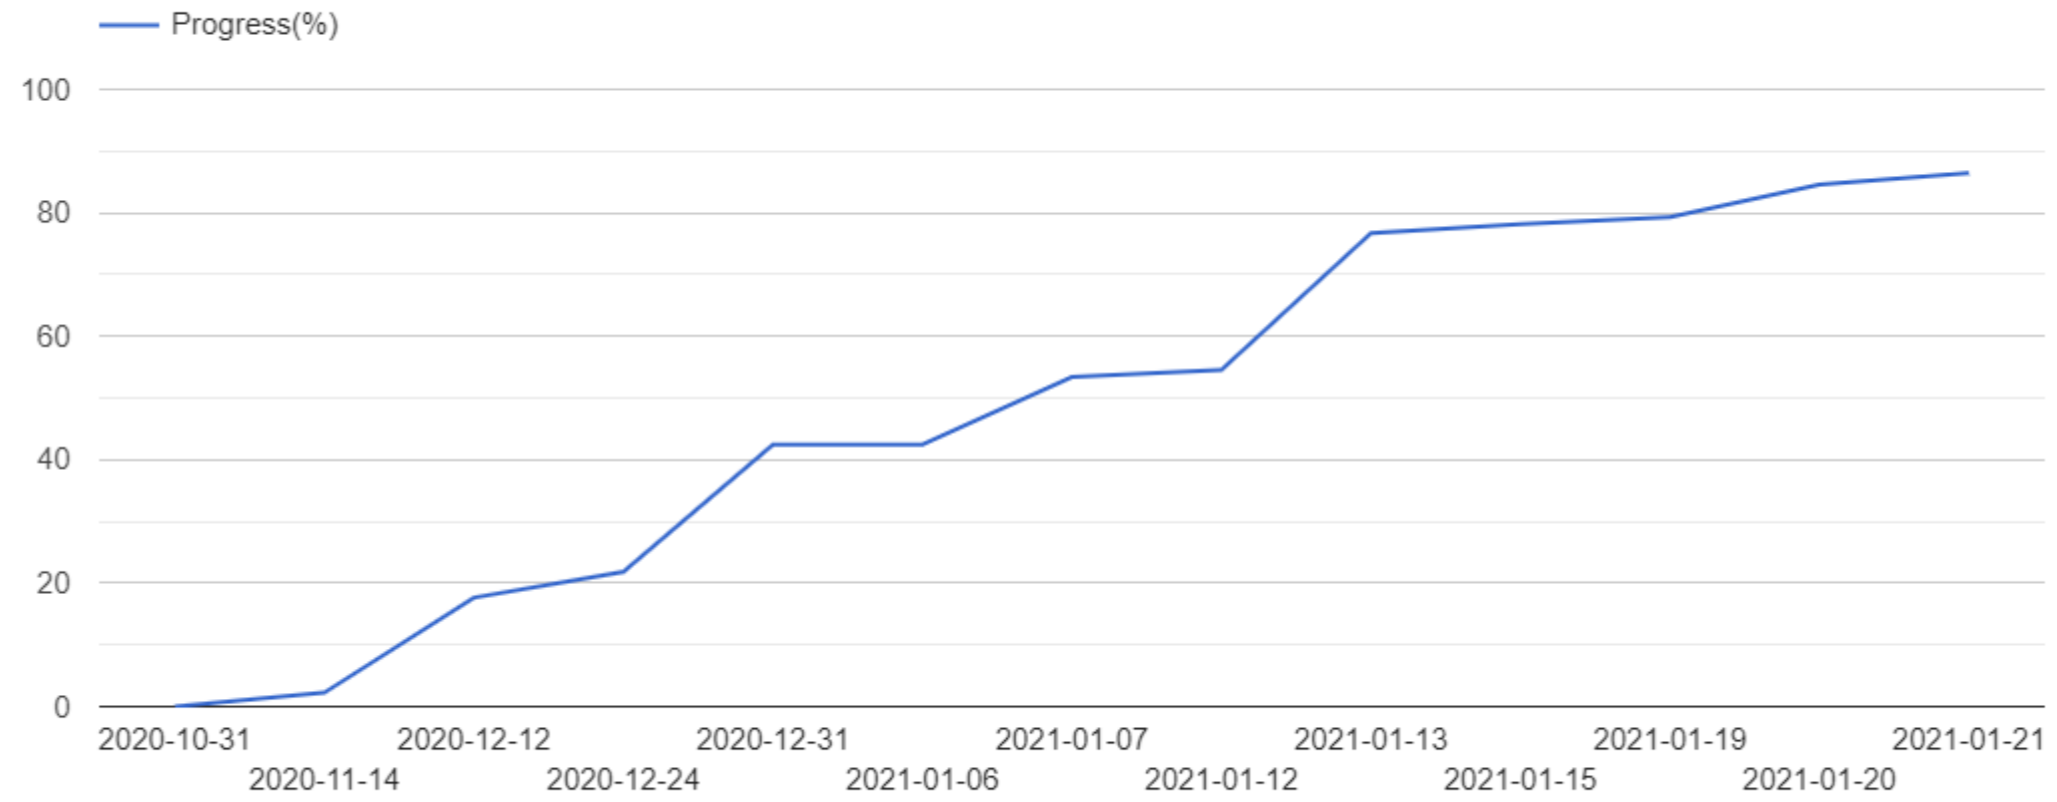

CUMMULATIVE WORK PROGRESS

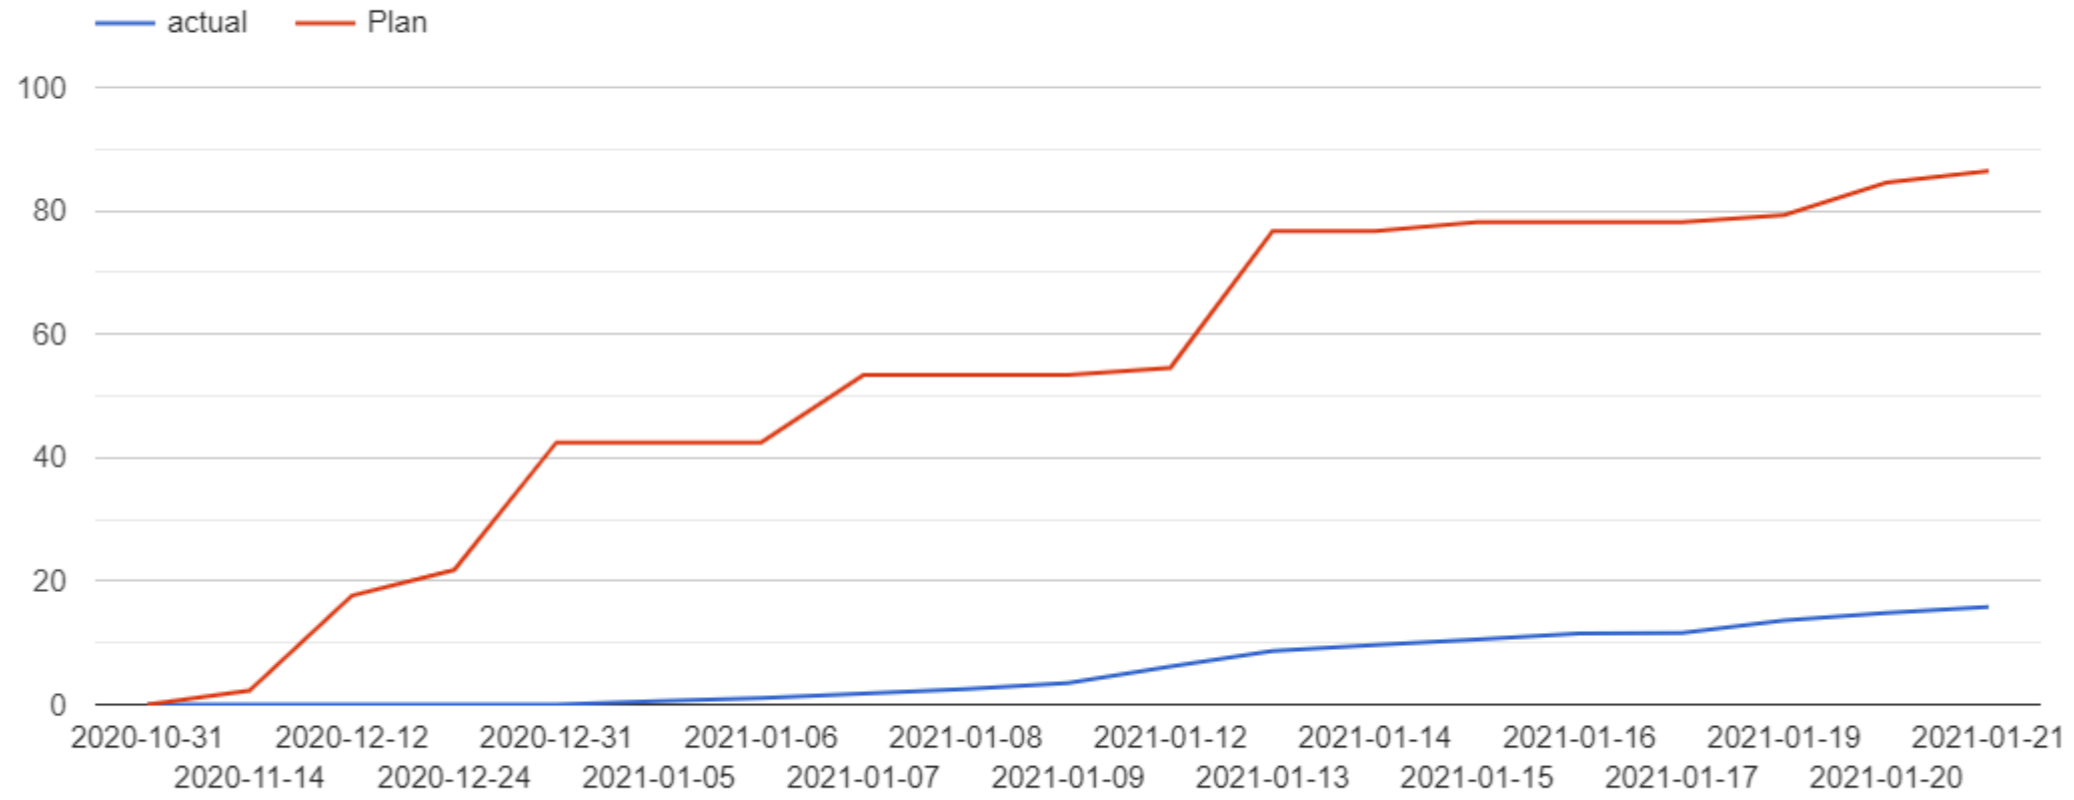

SCHEDULE AHEAD-BEHIND

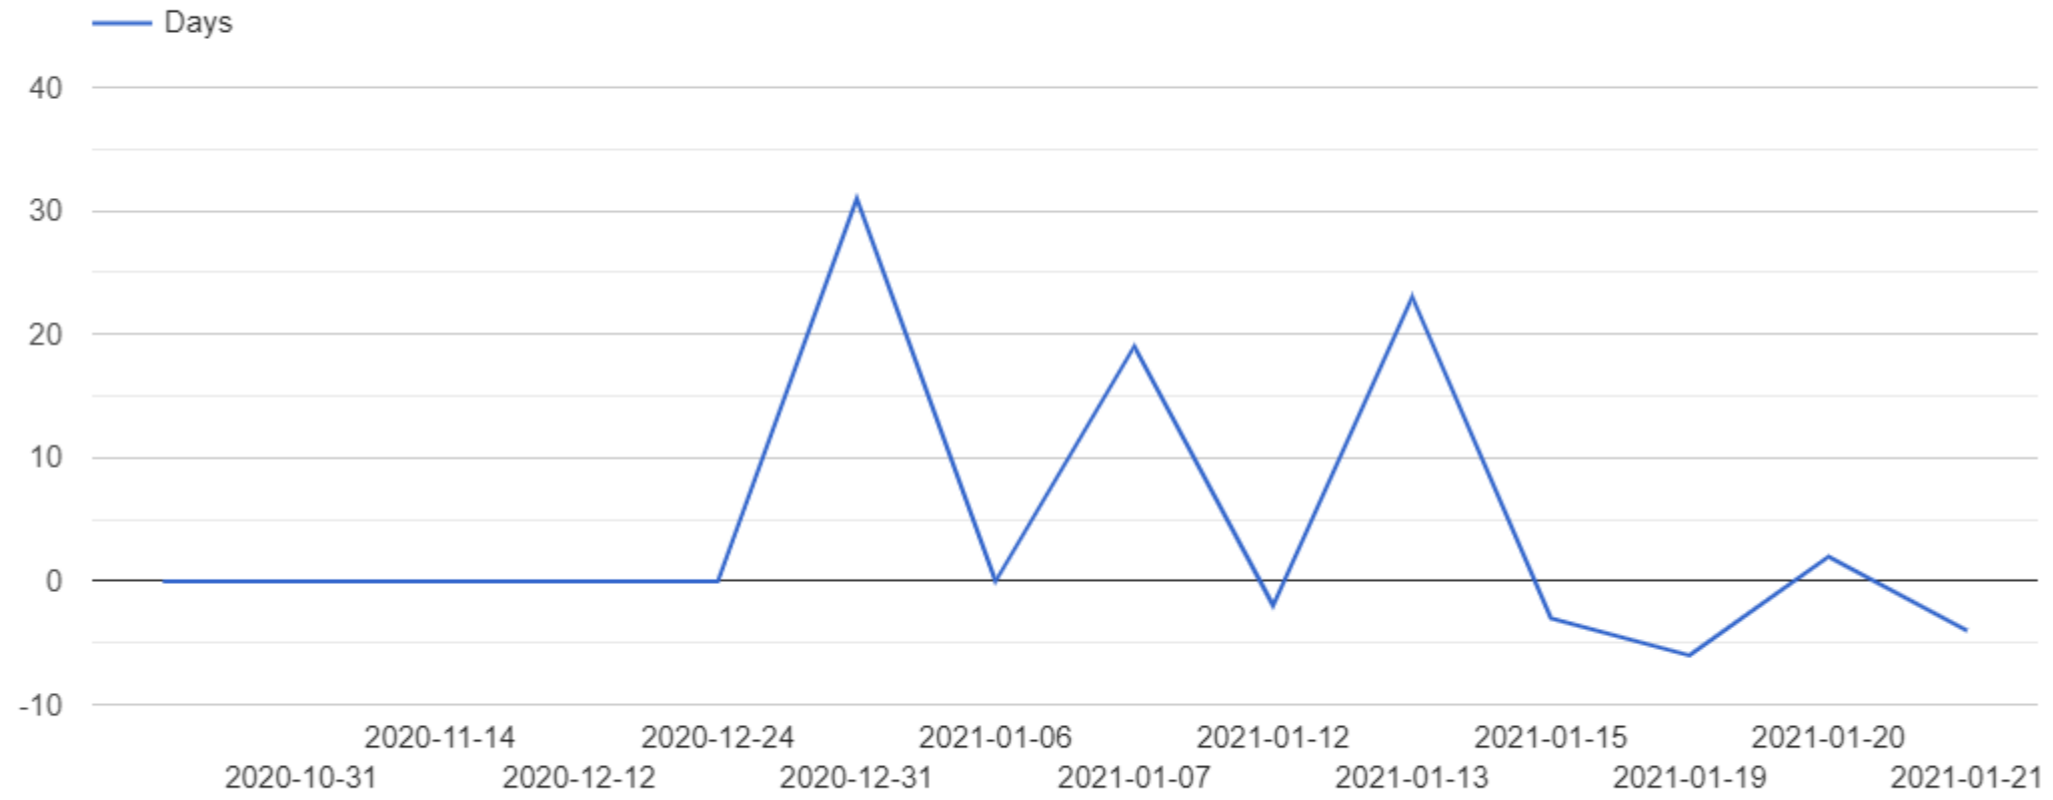

LAST MONTH REPORT
LAST DAY REPORT



MONTHLY PROGRESS REPORT


From 1-January-2021 to 21-January-2021

Project Code:	49	Name:	Marriot-Nilgiri at Bandarban
Client:	Contractor: Cityscape International Ltd.		


Monthly Progress

WBS	Task	Total Qty	Upto Last Month(%)	This Month(%)	Total Done(%)	Schedule Start	Schedule Finish	Actual Finish
03.02	Mobilization-Material for Prelimina		0	5	5	08-12-20	05-02-21	13-01-21
03.03.01	Soling n Plaster for PVC Water Tank		60	20	80	15-01-21	22-01-21	20-01-21
03.06.02	Mobilization-Mechanics Shed-Frame W		0	100	100	15-01-21	22-01-21	20-01-21
03.07	Mobilization-Grass Cutting-Roa		30	60	90	28-12-20	26-01-21	07-01-21
03.08.01	Mobilization-Guest House-Layout	130sqm	30	70	100	06-01-21	06-01-21	06-01-21
03.08.02	Mobilization-Guest House-Excavation	163cum	0	100	100	07-01-21	10-01-21	12-01-21
03.08.03	Mobilization-Guest House-Footi	16nos	0	100	100	08-01-21	12-01-21	15-01-21
03.08.04	Mobilization-Guest House-Pades	16nos	0	100	100	10-01-21	13-01-21	19-01-21
03.08.05	Mobilization-Guest House-Grade Beam	107m	0	65	65	12-01-21	17-01-21	21-01-21

MANPOWER HISTOGRAM

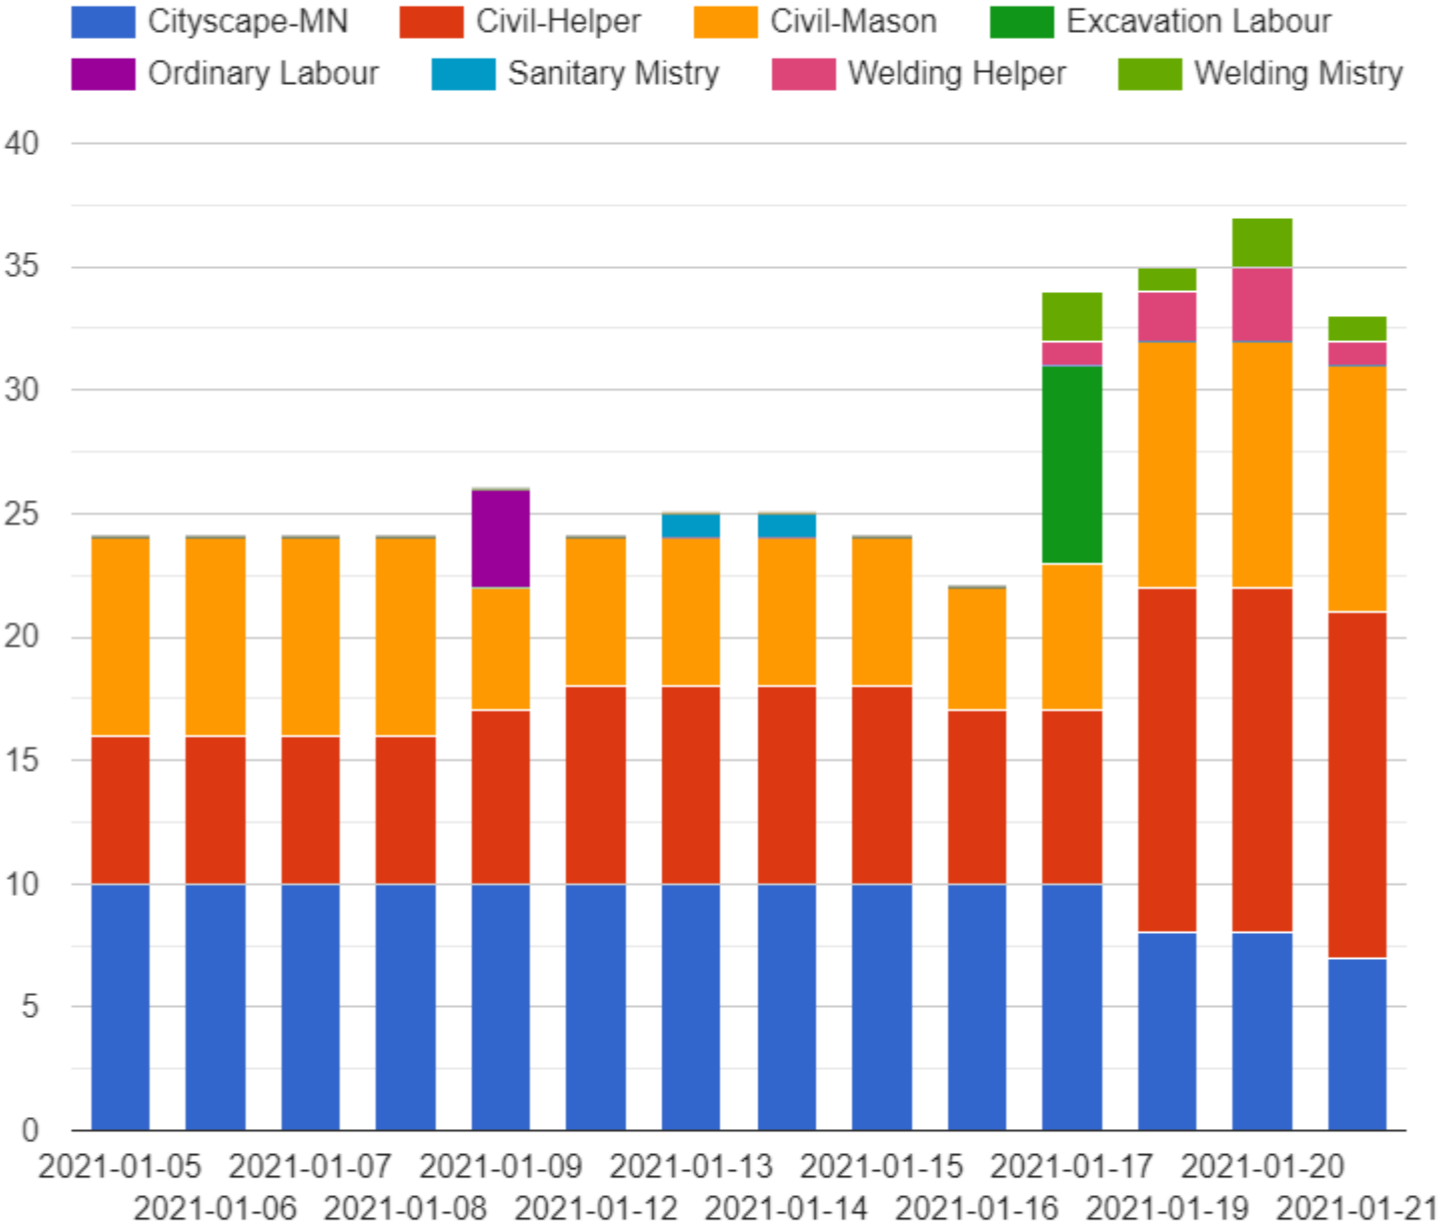

DAILY PROGRESS

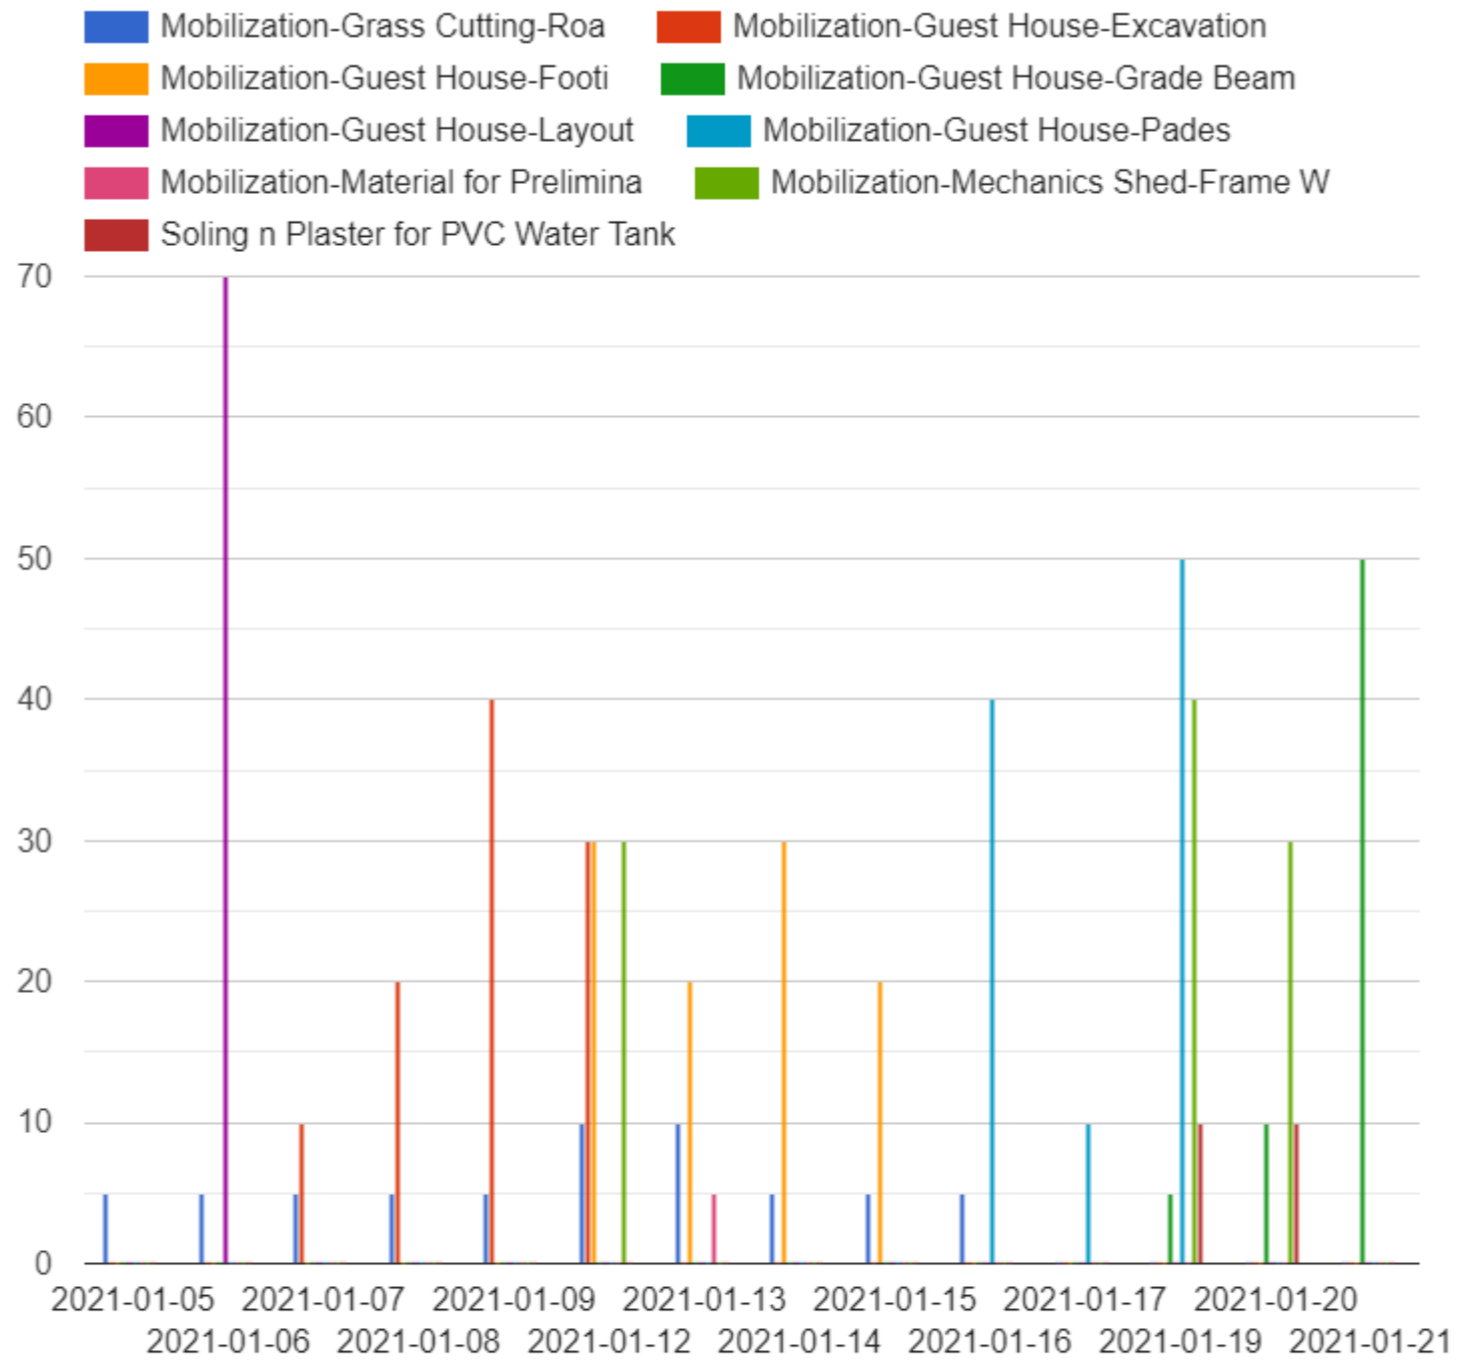



DAILY PROGRESS REPORT

Project:	Marriot-Nilgiri at Bandarban	Project Code:	49	Date:	21-January-2021
Client:		Report	041	Day	Thursday
Contractor:				Climate	Cloudy
					13-27C

Manpower

SN	Description	Nos.
01	Cityscape-MN	7
02	Civil-Mason	10
03	Civil-Helper	14
04	Welding Mistry	1
05	Welding Helper	1
TOTAL		33

Progress This Day

WBS	Task	Total Qty	Today Done(%)	Total Done(%)	Schedule Start	Schedule Finish
03.08.05	Mobilization-Guest House-Grade Beam	107m	50	65	12-01-21	17-01-21

Site Photographs



Rod binding work for grade beam at guest




Solling joint fillup & plaster work at w

Site Description	
Site Instruction	
Entry by:	Generated by:
Planning Engineer	www.bel3c.com, Developed by: Engr. Md. Sanaul Haque

WORK PLAN AND PROGRESS

MOBILIZATION PLAN FOR MARRIOT-NILGIRI AT BANDARBAN

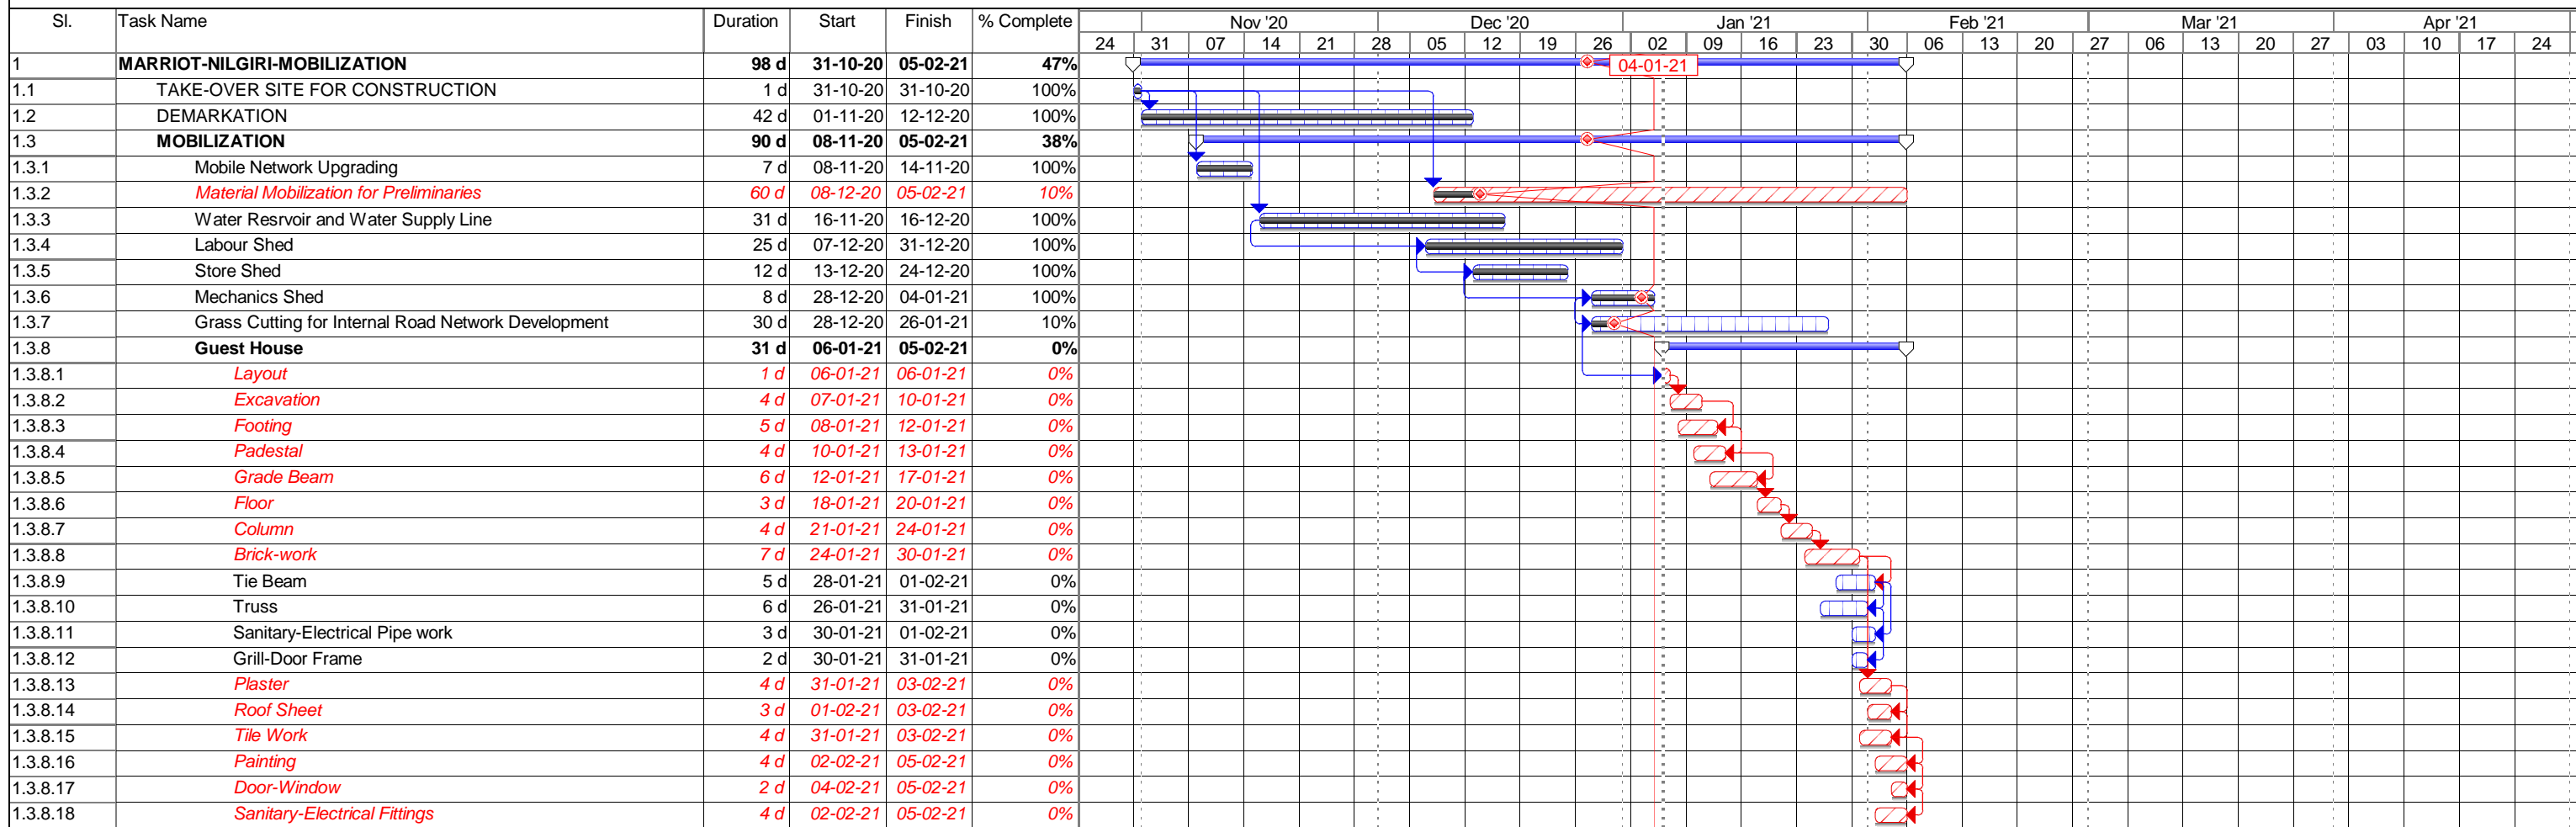

Task		Progress		Rolled Up Task		Rolled Up Progress		Group By Summary	
Critical Task		Summary		Rolled Up Critical Task		Project Summary			

PROGRESS PHOTO

Site Photographs



Guest House-Preparation for Layout on 05-01-21



Guest House-Preparation for Layout on 05-01-21



Guest House-Preparation for Layout on 06-01-21



Guest House-Preparation for Layout on 06-01-21



Guest House-Preparation for Layout on 07-01-21



Guest House-Preparation for Layout on 07-01-21



on 08-01-21



on 08-01-21



Guest House-Excavation on 09-01-21



Brick Carrying on 09-01-21



MS rod cutting & binding on 12-01-21



Plaster work for labour Shed on 12-01-21



Footing & column casting work on going on 13-01-21



Reached water tank at project on 13-01-21



Column standing work on going at G.House on 14-01-21



Footing & column casting work on going a on 14-01-21



Column standing work on going at G.House on 15-01-21



Footing casting work on going at G.House on 15-01-21



Shuttering fitting work for short column on 16-01-21



Short column casting work for guest hous on 16-01-21



Shuttering fitting work for short column on 17-01-21



Short column casting work for guest hous on 17-01-21



MS rod cutting & binding work for grade on 19-01-21



Brick soling work for water tank placei on 19-01-21



Soling for PVC Water Tank on 20-01-21



Mechanics Shed Frame Work on 20-01-21



Rod binding work for grade beam at guest on 21-01-21



Solling joint fillup & plaster work at w on 21-01-21
