

**CONSTRUCTION OF RIVER FRONT SATELITE CITY
AT RAYERBAZAR, DHAKA**

RUNNING PROGRESS



11 APRIL 2021

Generated by: Cityscape International Limited

TABLE OF CONTENTS

- TOTAL PROGRESS
- TOTAL MANPOWER CHART
- CUMMULATIVE PROGRESS CHART
- SCHEDULE LEAD-LAG CHART
- LAST MONTH PROGRESS
- LAST MONTH MANPOWER HISTOGRAM
- LAST MONTH PROGRESS CHART
- DAILY PROGRESS REPORT
- WORK PLAN AND PROGRESS
- PROGRESS PHOTO



TOTAL PROGRESS REPORT

From 27-January-2021 to 11-April-2021


Project Code:	56	Name:	River Front Satellite City
Client:	Sikder Group	Contractor:	Cityscape International Ltd.

Total Progress


WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Finish	Lead-Lag(day)
02.01	River-side Walkway-Side Wall	835m	100	07-12-20	04-02-21	05-02-21	-1
02.02	River-side Walkway-Filling	835m	100	10-12-20	07-02-21	05-02-21	2
02.03	River-side Walkway-Soling	5007sqm	100	13-12-20	10-02-21	05-02-21	5
02.04	River-side Walkway-CC	5007sqm	100	16-01-21	13-02-21	05-02-21	8
02.06	River-side Boundary-Bottom Beam	835m	100	07-12-20	04-02-21	01-02-21	3
02.07	River-side Boundary-Bot Column	89nos	100	08-12-20	05-02-21	01-02-21	4
02.08	River-side Boundary-Brick Work	835m	100	10-12-20	07-02-21	01-02-21	6
02.09	River-side Boundary-Top Beam	835m	100	12-12-20	09-02-21	01-02-21	8
02.10	River-side Boundary-Top Column	89nos	100	14-12-20	11-02-21	01-02-21	10
02.11	River-side Boundary-Grill	835m	95	21-12-20	18-02-21	08-02-21	10
02.12	River-side Boundary-Column Capital	89nos	95	21-12-20	18-02-21	01-02-21	17
02.13	River-side Boundary-Bontile Texture	835m	95	28-12-20	25-02-21	03-04-21	-37
02.14	River-side Boundary-Grill Enamel Pa	835m	95	14-02-21	28-02-21	08-03-21	-8
03.03	40 feet Road Levelling and Dressing	886m	18	26-02-21	11-03-21	31-03-21	-20
04.01	12 ft Inner Road-Filling	m	80	20-12-20	12-02-21	28-02-21	-16
04.02	12 Ft Inner Road-Soling	sqm	60	21-12-20	13-02-21	08-02-21	5
04.03	12 ft Inner Road-CC	sqm	50	22-12-20	14-02-21	08-02-21	6
05.01	Outside Plaster-Building-B		10	26-01-21	25-02-21	29-01-21	27
05.06	Outside Plaster-Building-J		60	11-01-21	09-02-21	28-01-21	12
05.10	Outside Plaster-Building-N		84	11-01-21	10-02-21	03-04-21	-52
05.11	Outside Plaster-Building-Q		90	18-01-21	16-02-21	05-02-21	11
05.12	Outside Plaster-Building-R		88	18-01-21	16-02-21	03-04-21	-46
06.03	Mock-up Flat-Const Joint & Extensn		100	18-01-21	31-01-21	05-02-21	-5

WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Finish	Lead-Lag(day)
06.04.1	Mock-up Flat-Brick Work		95	17-01-21	31-01-21	05-02-21	-5
06.04.2	Mock-up Flat-Plaster		87	07-01-21	10-02-21	25-02-21	-15
06.06.2	Mock-up Flat-Elect Conceal		90	15-01-21	31-01-21	25-02-21	-25
07.04.2	Mosque-Ground Floor Slab	790m2	100	10-03-21	21-03-21	21-03-21	0
07.05.1	Mosque-Ground Floor-Column		100	22-03-21	02-04-21	28-03-21	5
07.05.2	Mosque-Ground Floor-Roof Slab	790m2	100	03-04-21	09-04-21	06-04-21	3
07.05.3	Mosque-Ground Floor-Stair	6nos	83	22-03-21	15-04-21	11-04-21	4
07.06.1	Mosque-Basement Tile work	790m2	35	10-04-21	19-04-21	11-04-21	8
07.07.1	Mosque- 20ft Connecting Road-Fillin		5	01-04-21	14-04-21	31-03-21	14


DAILY MANPOWER

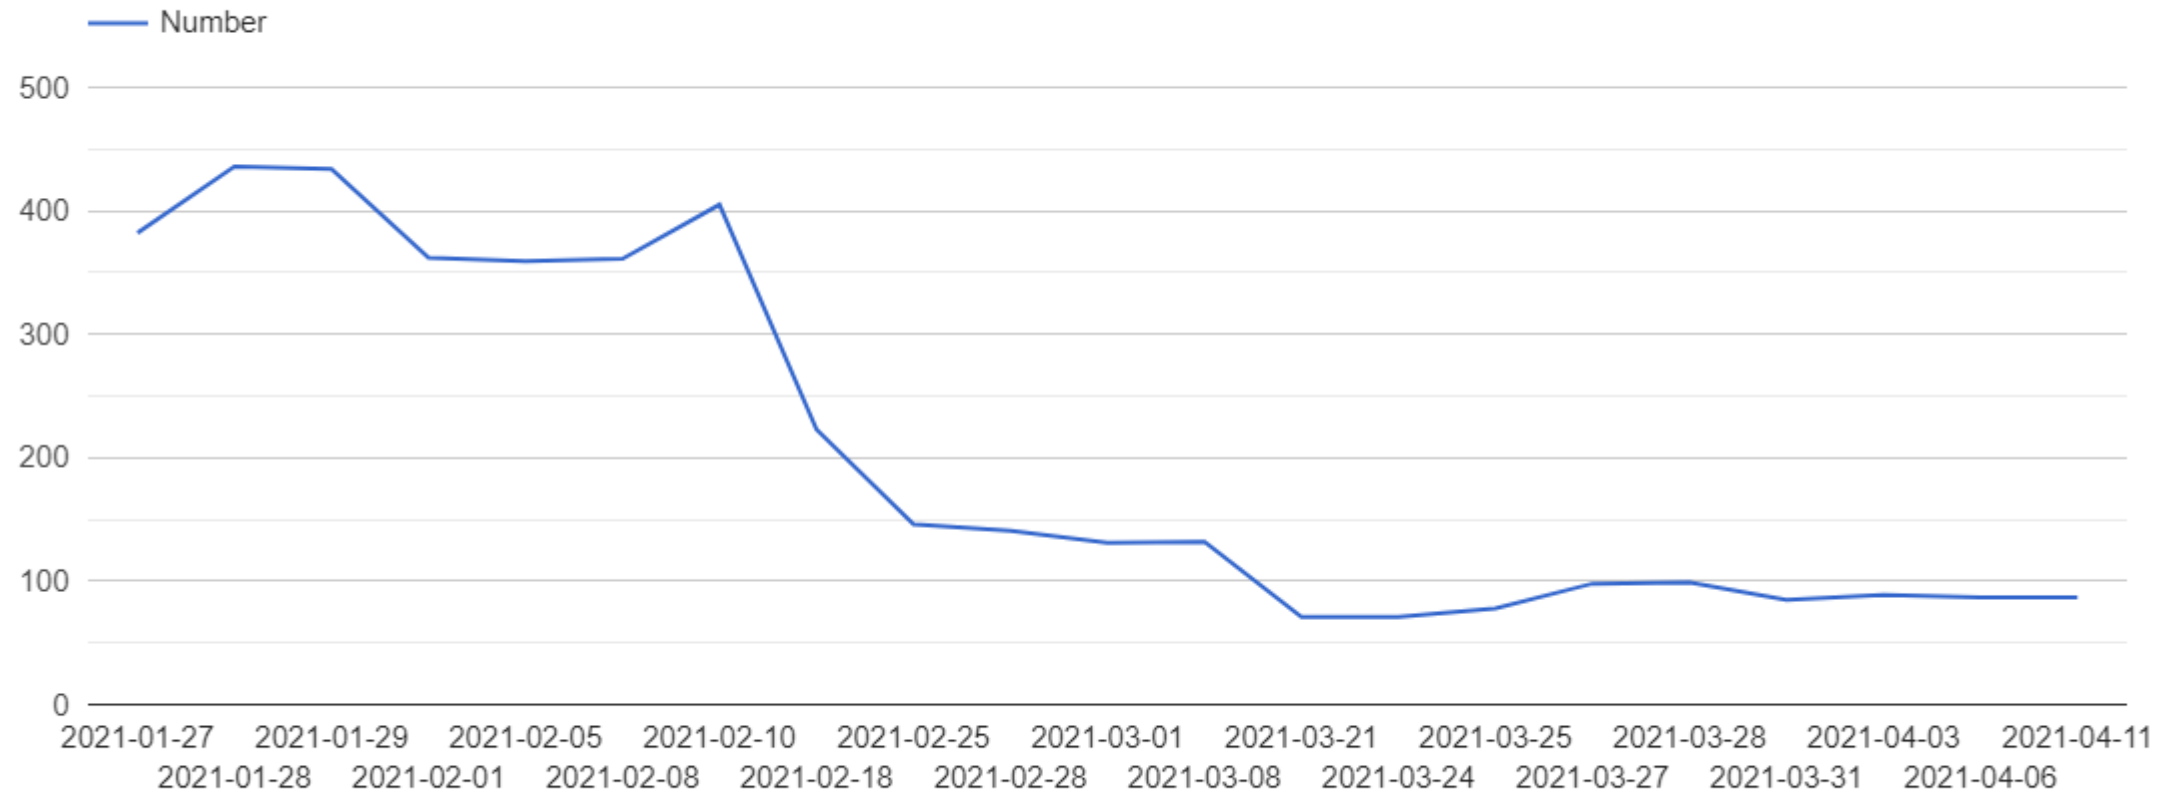

CUMMULATIVE WORK PROGRESS

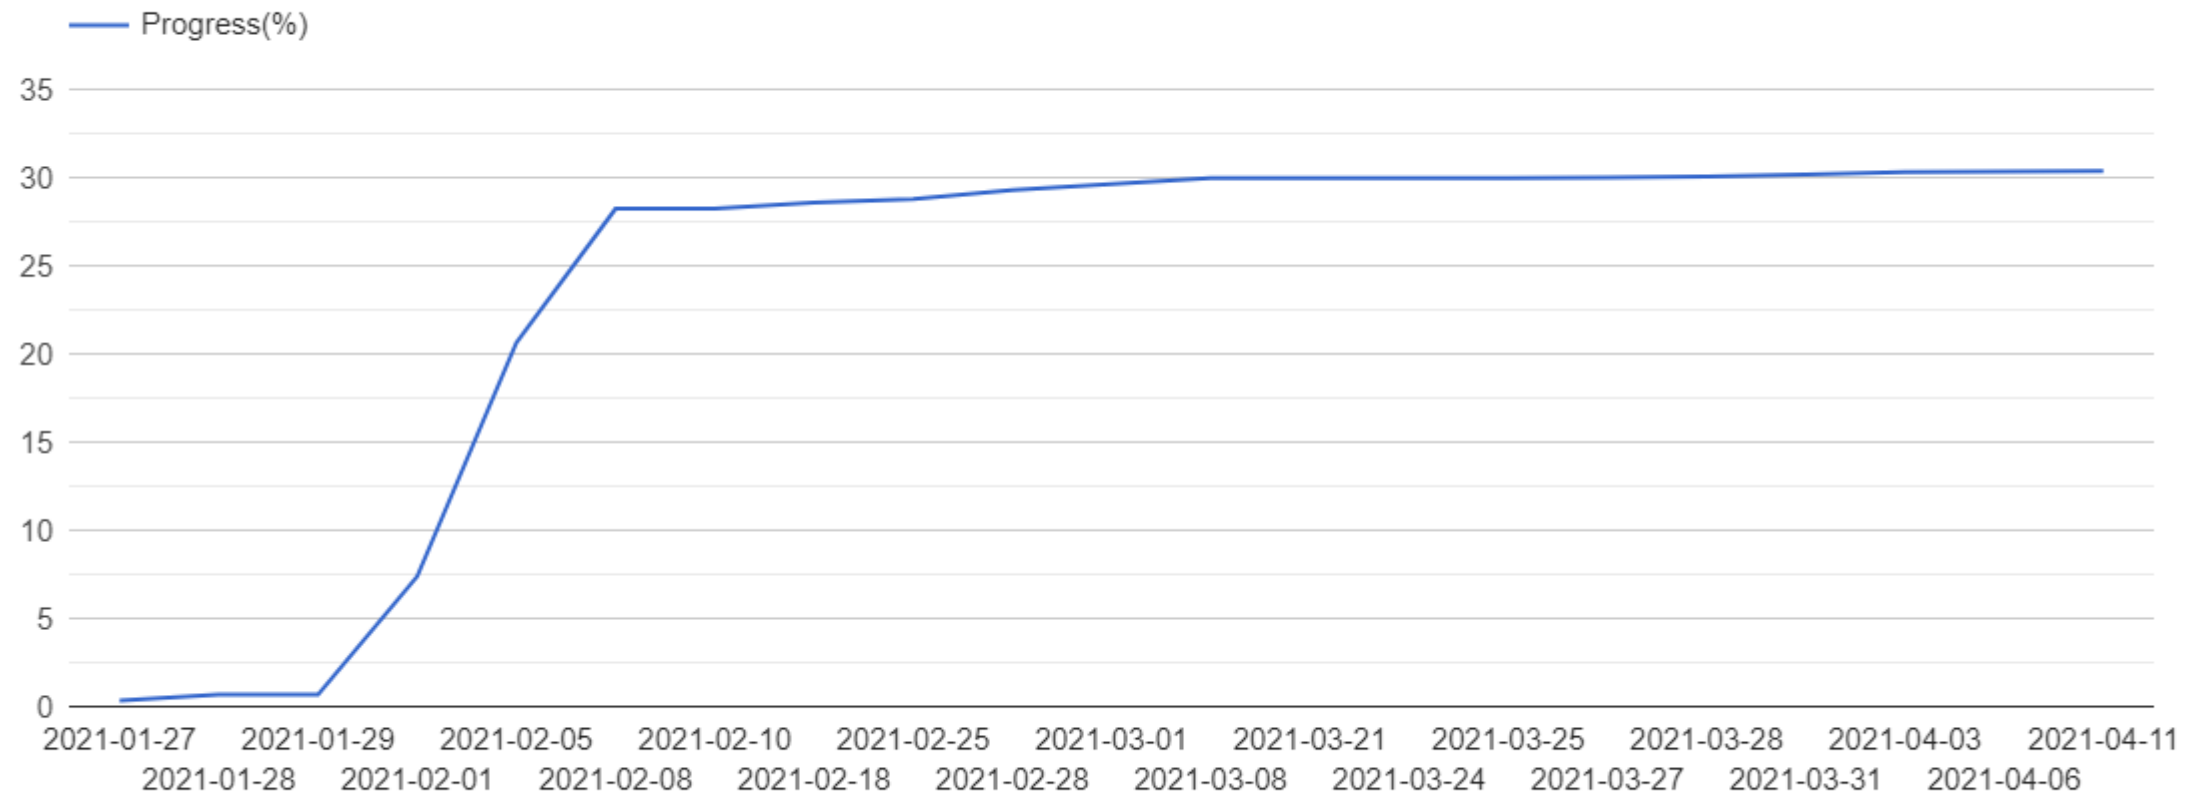

SCHEDULE AHEAD-BEHIND

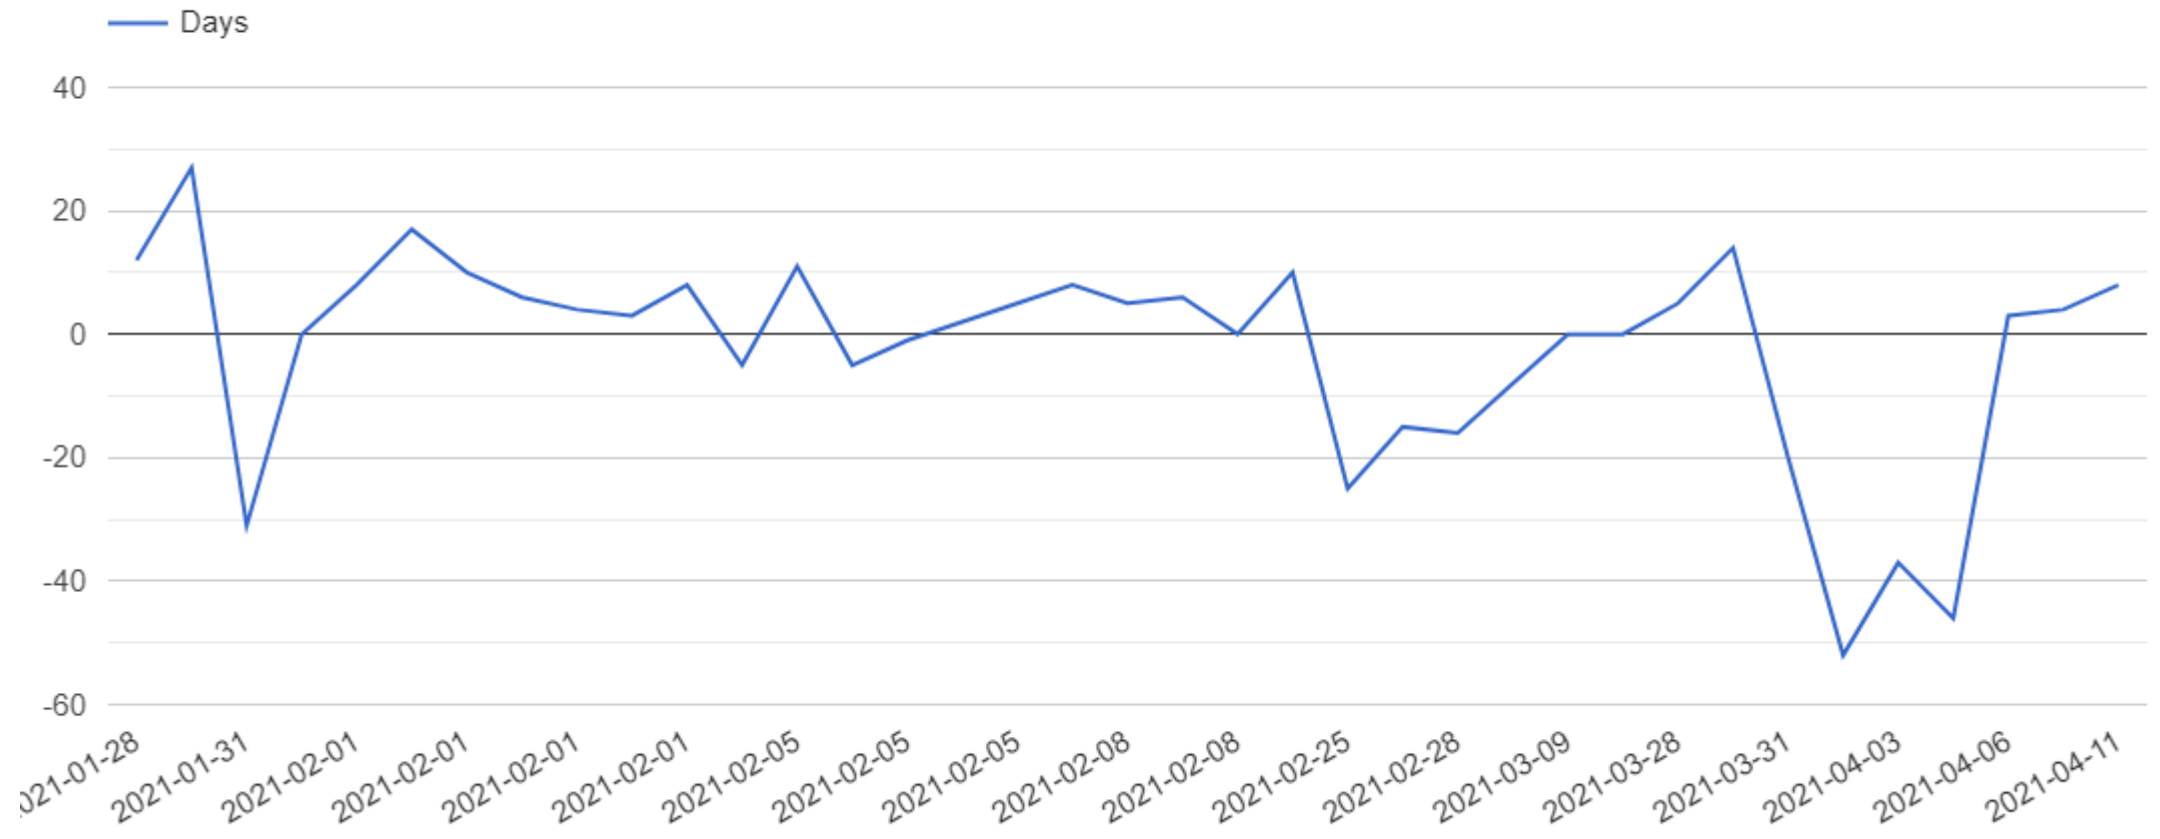

MONTHLY REPORT
DAILY REPORT



MONTHLY PROGRESS REPORT


From 1-March-2021 to 31-March-2021

Project Code:	56	Name:	River Front Satellite City
Client:	Sikder Group	Contractor:	Cityscape International Ltd.


Monthly Progress

WBS	Task	Total Qty	Upto Last Month(%)	This Month(%)	Total Done(%)	Schedule Start	Schedule Finish	Actual Finish
02.13	River-side Boundary-Bontile Texture	835m	83	12	95	28-12-20	25-02-21	31-03-21
02.14	River-side Boundary-Grill Enamel Pa	835m	85	10	95	14-02-21	28-02-21	08-03-21
03.03	40 feet Road Levelling and Dressing	886m	15	3	18	26-02-21	11-03-21	31-03-21
05.10	Outside Plaster-Building-N		80	3	83	11-01-21	10-02-21	27-03-21
05.12	Outside Plaster-Building-R		83	4	87	18-01-21	16-02-21	31-03-21
07.04.2	Mosque-Ground Floor Slab	790m2	0	100	100	10-03-21	21-03-21	21-03-21
07.05.1	Mosque-Ground Floor-Column		0	100	100	22-03-21	02-04-21	28-03-21
07.05.2	Mosque-Ground Floor-Roof Slab	790m2	0	25	25	03-04-21	09-04-21	31-03-21
07.05.3	Mosque-Ground Floor-Stair	6nos	0	15	15	22-03-21	15-04-21	28-03-21
07.07.1	Mosque- 20ft Connecting Road-Fillin		0	5	5	01-04-21	14-04-21	31-03-21

MANPOWER HISTOGRAM

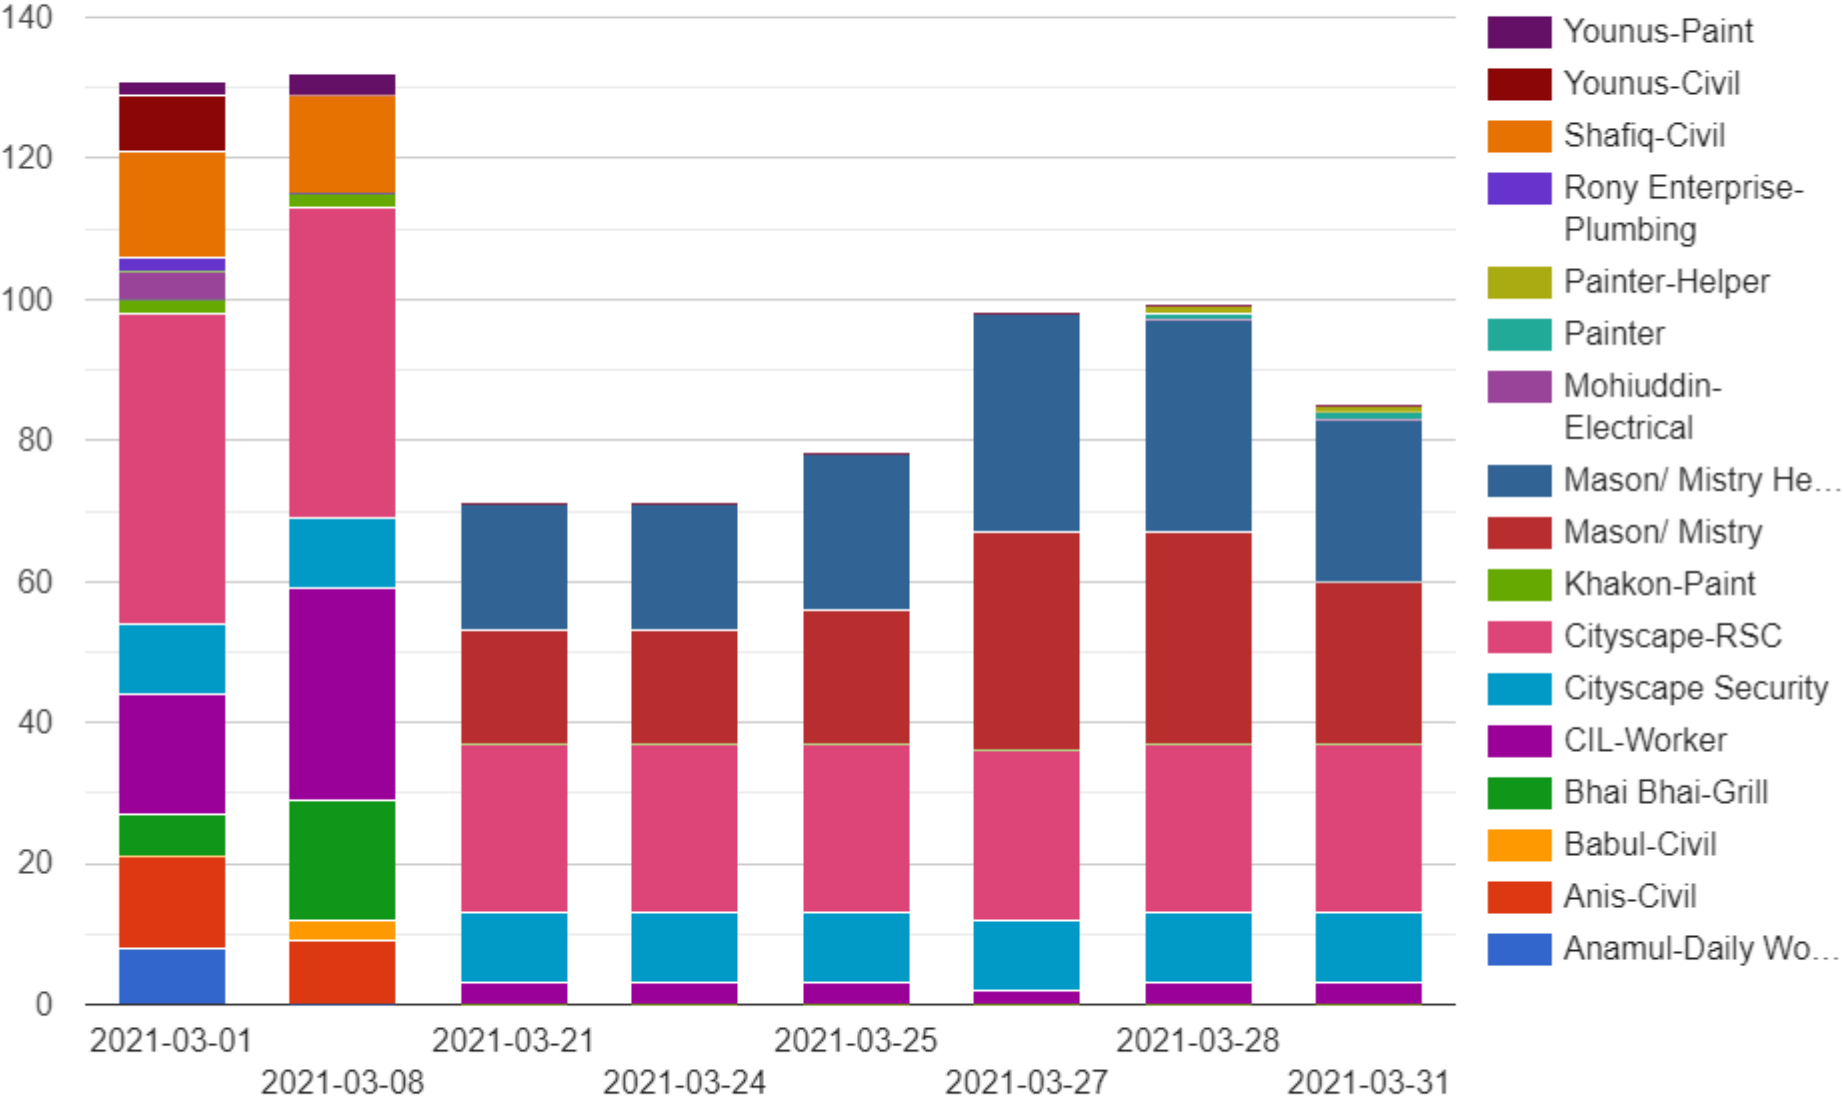

DAILY PROGRESS

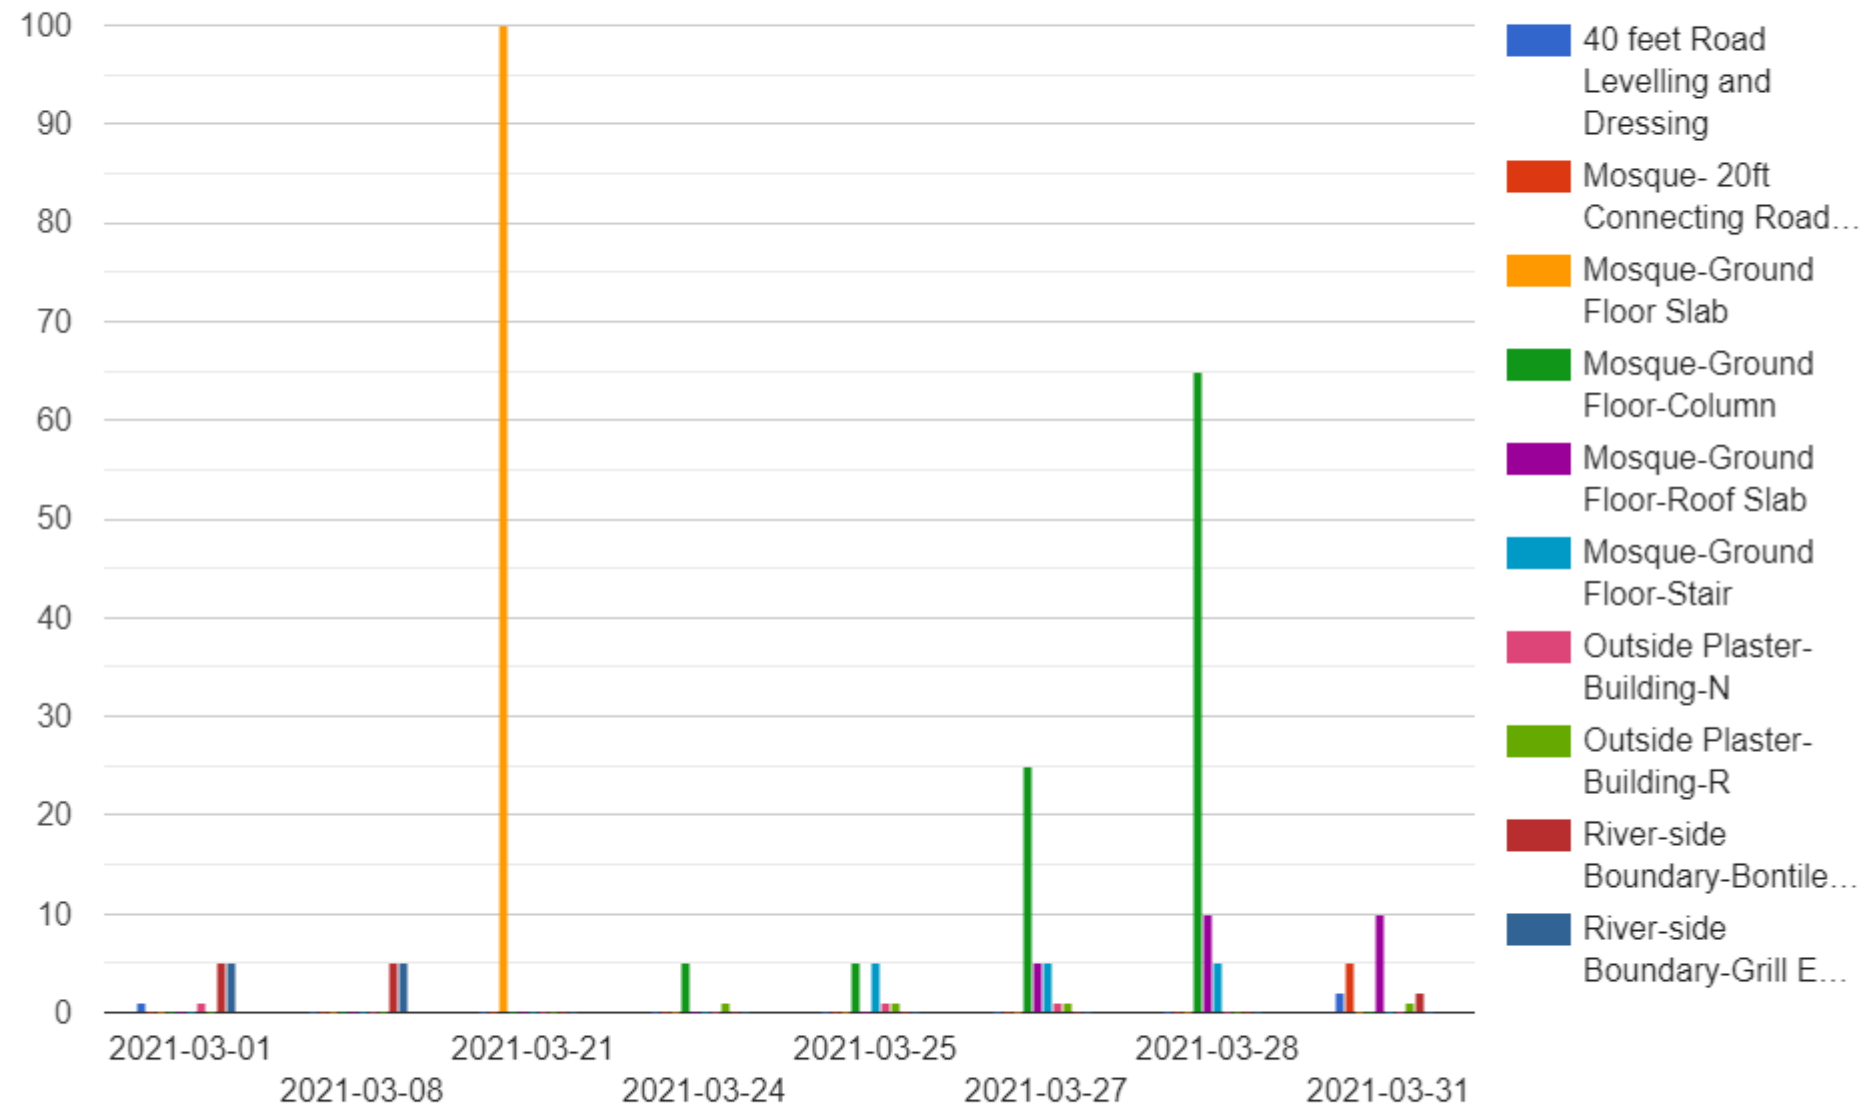

Project:	River Front Satellite City	Project Code:	56	Date:	11-April-2021
Client:	Sikder Group	Report	021	Day	Thu
Contractor:	Cityscape International Ltd.			Climate	Sunny
					27-34C

Manpower

SN	Description	Nos.
01	Cityscape-RSC	24
03	CIL-Worker	3
26	Cityscape Security	10
27	Mason/ Mistry	25
28	Mason/ Mistry Helper	25
TOTAL		87

Progress This Day

WBS	Task	Total Qty	Today Done(%)	Total Done(%)	Start	Finish
07.05.3	Mosque-Ground Floor-Stair	6nos	53	83	22-03-21	15-04-21
07.06.1	Mosque-Basement Tile work	790m2	35	35	10-04-21	19-04-21

Site Photographs



Mosque-Esatside Stair Case



Mosque-Basement Tiles Work

Site Description

Site Instruction

Entry by:


Planning Engineer

Generated by:

www.bel3c.com, Developed by: Engr. Md. Sanaul Haque

WORK PLAN AND PROGRESS

WORK PLAN AND PROGRESS OF RIVER FRONT SATELLITE CITY

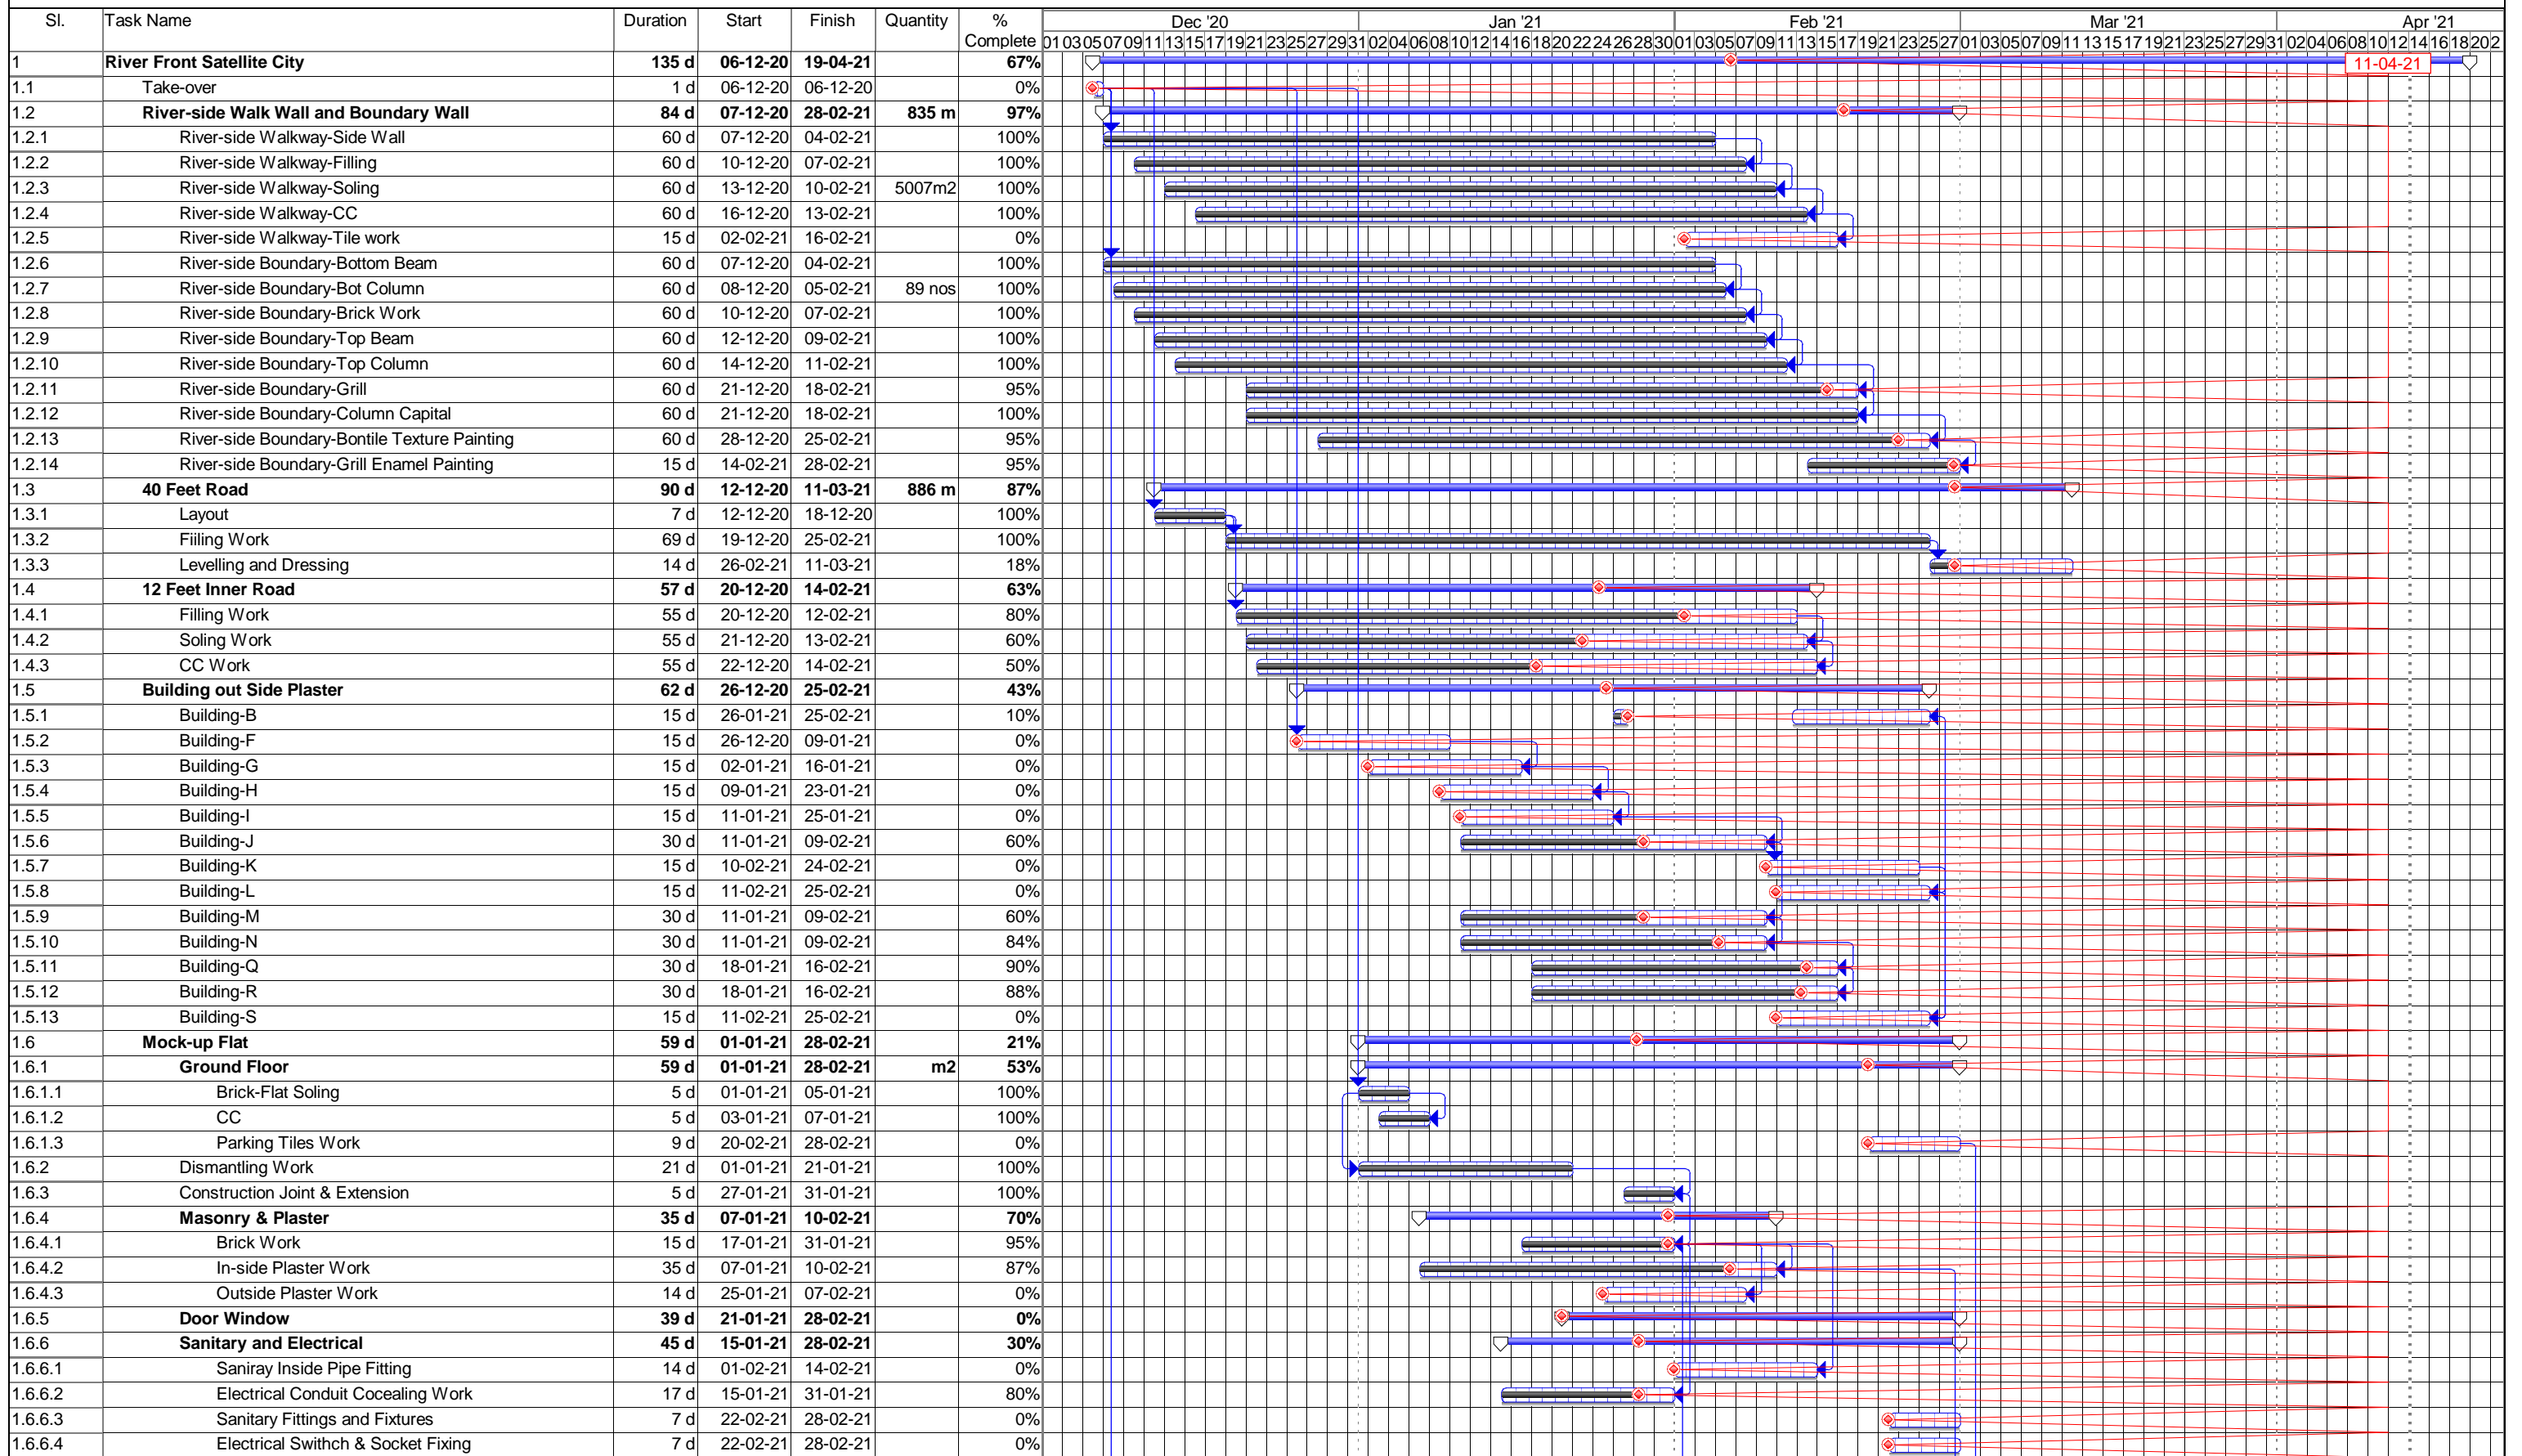

Date: 14-04-21 15.35
Sheet: 1 / 2

Task		Progress		Rolled Up Task		Rolled Up Progress		Group By Summary	
Critical Task		Summary		Rolled Up Critical Task		Project Summary			

WORK PLAN AND PROGRESS OF RIVER FRONT SATELLITE CITY



Sl.	Task Name	Duration	Start	Finish	Quantity	% Complete	Dec '20															Jan '21															Feb '21															Mar '21															Apr '21																																																																																																																																																																																																																																																																																																																										
							01	03	05	07	09	11	13	15	17	19	21	23	25	27	29	31	01	02	04	06	08	10	12	14	16	18	20	22	24	26	28	30	01	03	05	07	09	11	13	15	17	19	21	23	25	27	01	03	05	07	09	11	13	15	17	19	21	23	25	27	29	31	02	04	06	08	10	12	14	16	18	20	22	24	26	28	30																																																																																																																																																																																																																																																																																																										
1.6.7	Tile Work	38 d	22-01-21	28-02-21		0%																																																																																																																																																																																																																																																																																																																																																																																							
1.6.8	Stair Railing	15 d	01-02-21	15-02-21		0%																																																																																																																																																																																																																																																																																																																																																																																							
1.6.9	Lime Terracing/ Roof Treatment	15 d	14-02-21	28-02-21		0%																																																																																																																																																																																																																																																																																																																																																																																							
1.6.10	Inside Painting	30 d	28-01-21	26-02-21		0%																																																																																																																																																																																																																																																																																																																																																																																							
1.6.11	Electro Mechanical Works	22 d	07-02-21	28-02-21		0%																																																																																																																																																																																																																																																																																																																																																																																							
1.6.12	Landscaping	20 d	09-02-21	28-02-21		0%																																																																																																																																																																																																																																																																																																																																																																																							
1.6.13	Snaging and Finshing Touch	7 d	22-02-21	28-02-21		0%																																																																																																																																																																																																																																																																																																																																																																																							
1.6.14	Handover	1 d	28-02-21	28-02-21		0%																																																																																																																																																																																																																																																																																																																																																																																							
1.7	New Mosque	134 d	07-12-20	19-04-21		86%																																																																																																																																																																																																																																																																																																																																																																																							
1.7.1	Pile Work	25 d	07-12-20	31-12-20		100%																																																																																																																																																																																																																																																																																																																																																																																							
1.7.2	Excavation and Pile Head Breaking	40 d	23-12-20	31-01-21		100%																																																																																																																																																																																																																																																																																																																																																																																							
1.7.3	Mat Concreting	20 d	20-01-21	08-02-21		100%																																																																																																																																																																																																																																																																																																																																																																																							
1.7.4	Basement	41 d	09-02-21	21-03-21		100%																																																																																																																																																																																																																																																																																																																																																																																							
1.7.4.1	Retaining wall, Column, Lift Core, Stair	29 d	09-02-21	09-03-21		100%																																																																																																																																																																																																																																																																																																																																																																																							
1.7.4.2	Ground Floor Slab	12 d	10-03-21	21-03-21		100%																																																																																																																																																																																																																																																																																																																																																																																							
1.7.5	Ground Floor	25 d	22-03-21	15-04-21		90%																																																																																																																																																																																																																																																																																																																																																																																							
1.7.5.1	Column	12 d	22-03-21	02-04-21		100%																																																																																																																																																																																																																																																																																																																																																																																							
1.7.5.2	Roof Slab	7 d	03-04-21	09-04-21	790 m2	100%																																																																																																																																																																																																																																																																																																																																																																																							
1.7.5.3	Stair-6 nos	25 d	22-03-21	15-04-21	6 nos	83%																																																																																																																																																																																																																																																																																																																																																																																							
1.7.6	Finishing Works	10 d	10-04-21	19-04-21		5%																																																																																																																																																																																																																																																																																																																																																																																							
1.7.6.1	Basement Tiles	10 d	10-04-21	19-04-21		5%																																																																																																																																																																																																																																																																																																																																																																																							
1.7.7	20 ft Connection Road	14 d	01-04-21	14-04-21		5%																																																																																																																																																																																																																																																																																																																																																																																							
1.7.7.1	Sand Filling	14 d	01-04-21	14-04-21		5%																																																																																																																																																																																																																																																																																																																																																																																							

PROGRESS PHOTO

Site Photographs



Inner Road CC Work



Scaffolding for Outside Plaster-Buildin

Site Description

Site Instruction



Building-J outside plastering



Riverside walkway CC work

Site Description

Site Instruction



Building- outside plastering



Scaffolding for outside plastering Build

Site Description

Site Instruction



Riverside Bontile Rectification & Lighti



Landscape Lighting

Site Description

Site Instruction



Boundary Grill Painting



Out-side Plaster Work

Site Description

Site Instruction



Riverside Boundary Fencing



Building Outside Painting

Site Description

Site Instruction



40 ft Road Levelling and dressing



River Side Boundary Fencing

Site Description

Site Instruction





Site Description

Project was closed 11-17 Feb 2021 due to Honourable Z.H. Sikder death

Site Instruction



Mock-up-Exterior Sand Stone Fixing



Electrical Conduit Con sealing

Site Description

Site Instruction



40 ft Road Dressing and Levelling



12 ft Road Filling

Site Description

Site Instruction



40 ft Road Dressing and Levelling



Building Outside Plastering

Site Description

Site Instruction



Building Outside Plastering



Riverside Boundary Fencing

Site Description

Site Instruction



Briefing instruction before Concreting



Mosque Ground Floor Slab Concreting

Site Description

Site Instruction



Cityscape Security Training



Mosque GF Column 2nd Lift Re-bar Work

Site Description

Site Instruction



Mosque-GF Column Work



Mosque-GF-Stair Case Foundation Work

Site Description

Site Instruction



Mosque 1st Floor Slab Shuttering



Mosque Ground Floor Stair Concreting

Site Description

Site Instruction



Mosque 1st Floor Slab Shuttering



Mosque Ground Floor Stair Concreting

Site Description

Site Instruction



Mosque-20ft Connecting Road-Filling



Mosque-Night Shift Work

Site Description

Site Instruction



Mosque 1st Floor Slab Re-bar Work



Mosque Building in Construction

Site Description

Site Instruction



Mosque 1st Floor Slab Concreting



Mosque 1st Floor Slab Concreting

Site Description

Site Instruction



Mosque-Esatside Stair Case



Mosque-Basement Tiles Work	
Site Description	
Site Instruction	
Entry by:	Generated by:
Planning Engineer	www.bel3c.com, Developed by: Engr. Md. Sanaul Haque
