


**CONSTRUCTION OF CONTINENTAL BEVERAGES LTD.
AT LEVEL-15 CITYSCAPE TOWER, GULSHAN, DHAKA**

MONTHLY PROGRESS REPORT



28 FEBRUARY 2023

Generated by: Cityscape International Limited

TABLE OF CONTENTS

- LAST MONTH PROGRESS
- LAST MONTH MANPOWER HISTOGRAM
- LAST MONTH PROGRESS CHART
- DAILY PROGRESS REPORT

- TOTAL PROGRESS
- TOTAL MANPOWER CHART
- CUMMULATIVE PROGRESS CHART
- SCHEDULE LEAD-LAG CHART

- WORK PLAN AND PROGRESS
- PROGRESS PHOTO



MONTHLY PROGRESS REPORT

From 1-February-2023 to 27-February-2023


Project Code:	61	Name:	Cityscape Tower Level-15 Bar					
Client:	Cityscape	Contractor:	Cityscape International Ltd.					

Monthly Progress


WBS	Task	Total Qty	Upto Last Month(%)	This Month(%)	Total Done(%)	Schedule Start	Schedule Finish	Actual Finish
01	Glass Work	01	65	20	85	22-12-22	21-01-23	27-02-23
05	Floor Finsh-NCF	1sum	60	40	100	26-12-22	31-12-22	12-02-23
06	Wall Paneling	1sum	0	5	5	08-02-23	09-03-23	08-02-23

MANPOWER HISTOGRAM

Bar-Carpenter Bar-Civil Helper Bar-Mason Glass Engr
Glass Worker

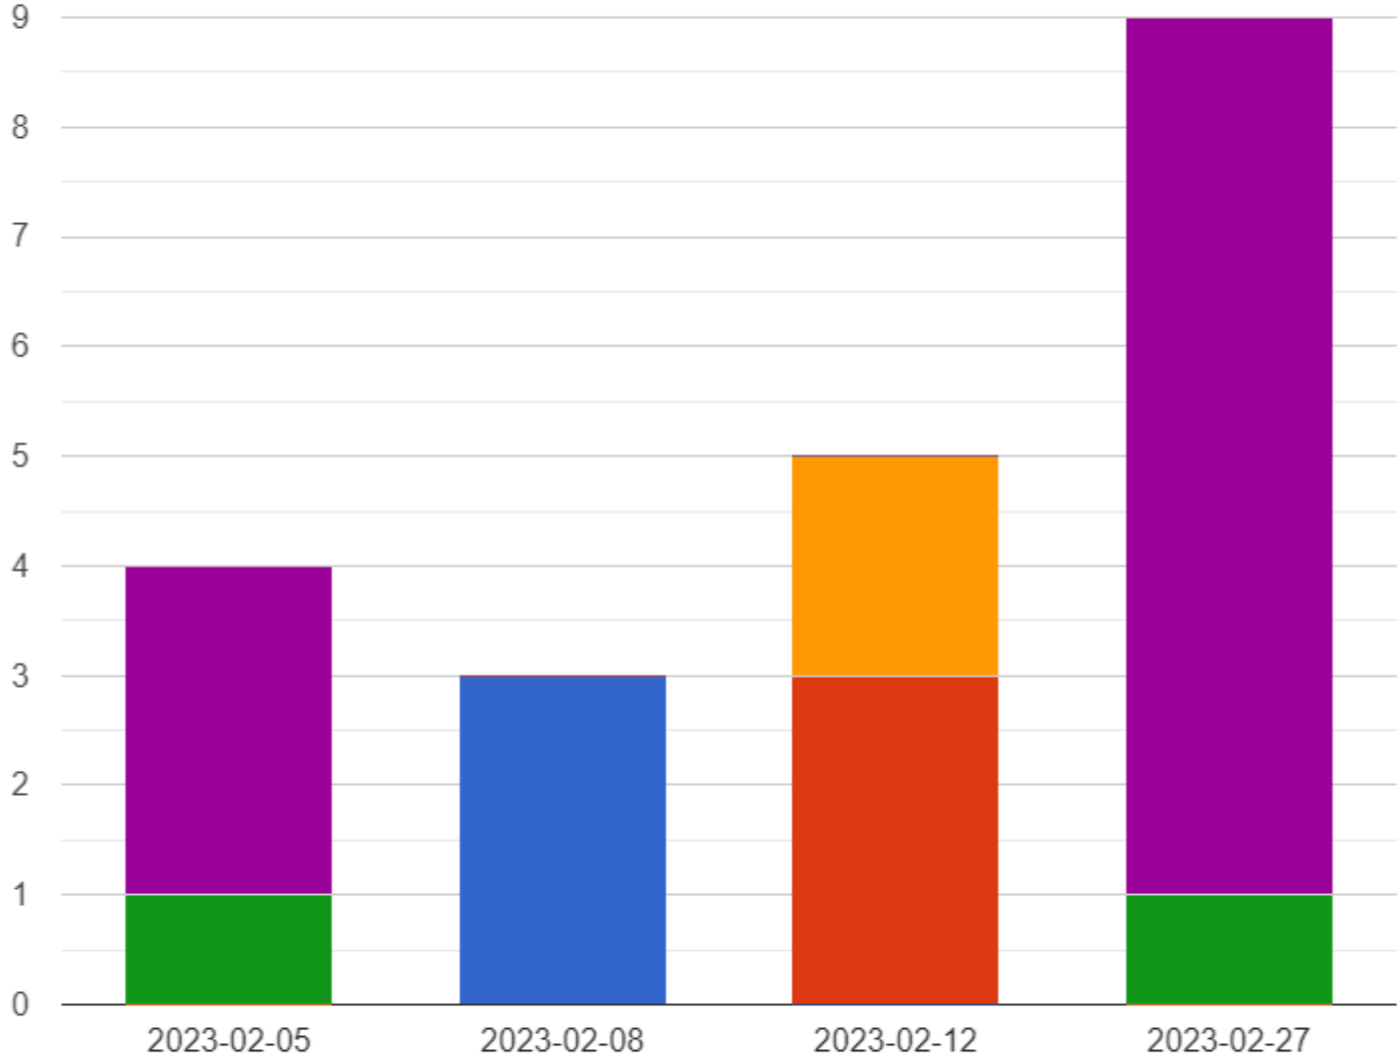

DAILY PROGRESS

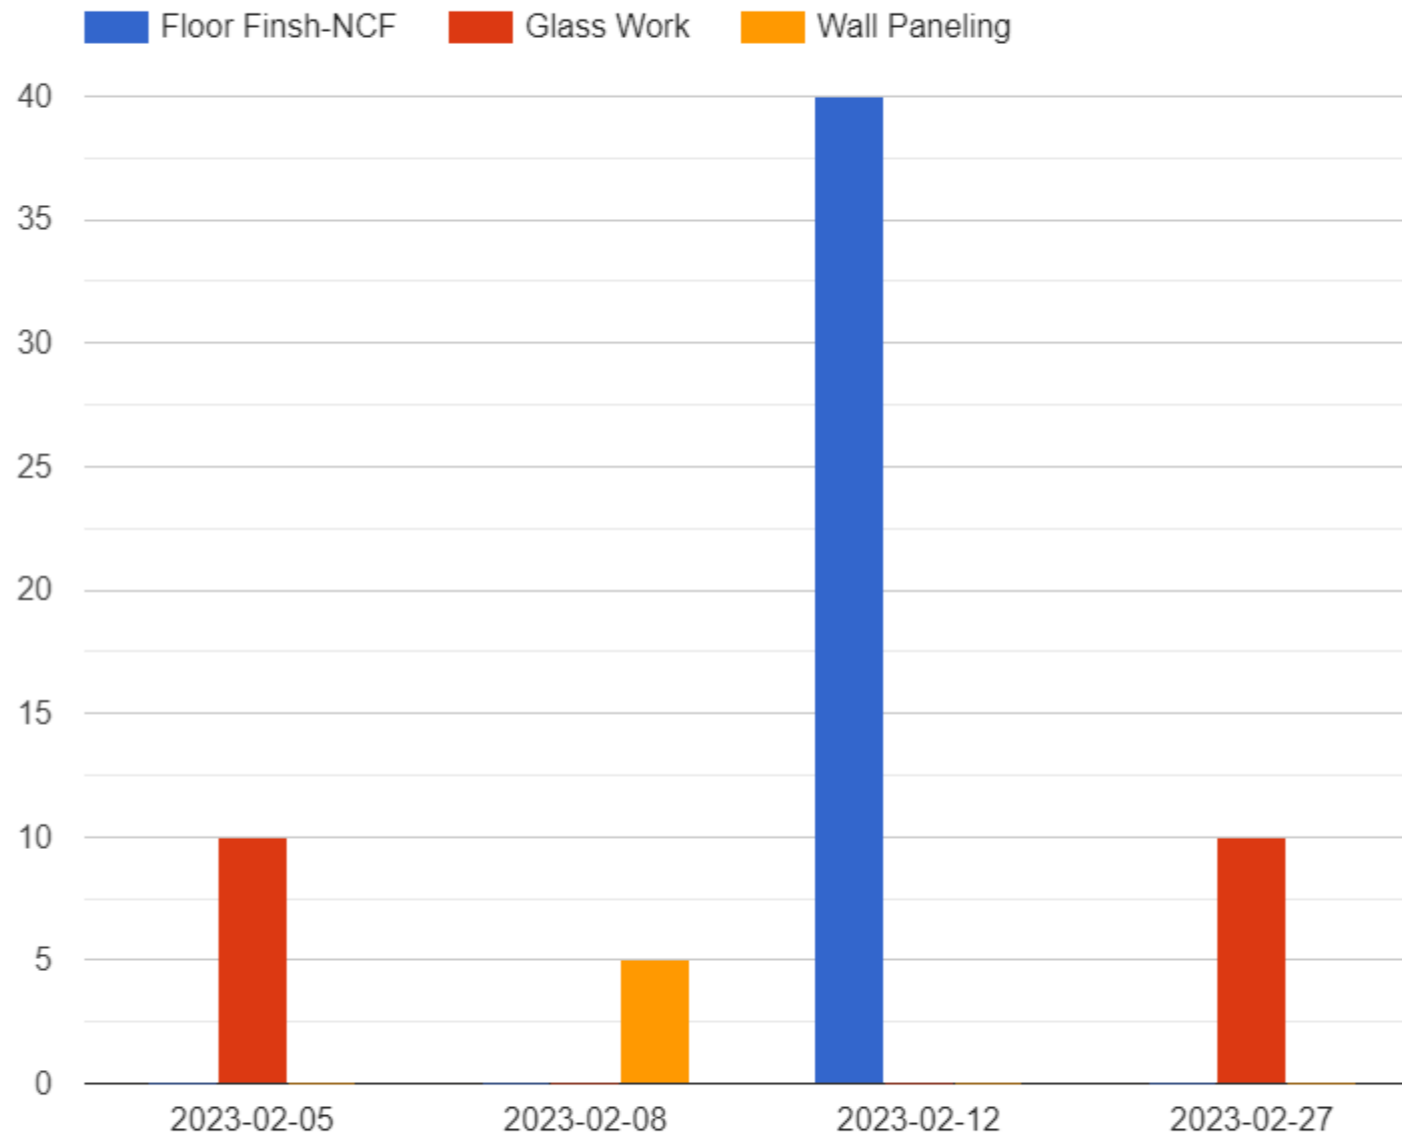



DAILY PROGRESS REPORT

Project:	Cityscape Tower Level-15 Bar	Project Code:	61	Date:	27-February-2023
Client:	Cityscape	Report	014	Day	Monday
Contractor:	Cityscape International Ltd.			Climate	Sunny
					20-32C

Manpower

SN	Description	Nos.
01	Glass Engr	1
02	Glass Worker	8
TOTAL		9

Progress This Day

WBS	Task	Total Qty	Today Done(%)	Total Done(%)	Schedule Start	Schedule Finish
01	Glass Work	01	10	85	22-12-22	21-01-23

Site Photographs



L-15-North Side Glass Framing

L-15-North Side Glass Framing

Site Description	
Site Instruction	
Entry by:	Generated by:
Planning Engineer	www.bel3c.com, Developed by: Engr. Md. Sanaul Haque

TOTAL REPORT



TOTAL PROGRESS REPORT


From 22-December-2022 to 27-February-2023

Project Code:	61	Name:	Cityscape Tower Level-15 Bar		
Client:	Cityscape	Contractor:	Cityscape International Ltd.		


Total Progress

WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)
01	Glass Work	01	85	22-12-22	21-01-23	22-12-22	27-02-23	-37
02	Carpentry Mock-up	1sum	100	22-12-22	23-12-22	22-12-22	26-12-22	-3
03	Bar Counter	1sum	50	22-12-22	06-01-23	22-12-22	26-01-23	-20
04	Washroom Brickwork	1sum	90	22-12-22	27-12-22	22-12-22	03-01-23	-7
05	Floor Finsh-NCF	1sum	100	26-12-22	31-12-22	03-01-23	12-02-23	-43
06	Wall Paneling	1sum	5	08-02-23	09-03-23	08-02-23	08-02-23	29


DAILY MANPOWER

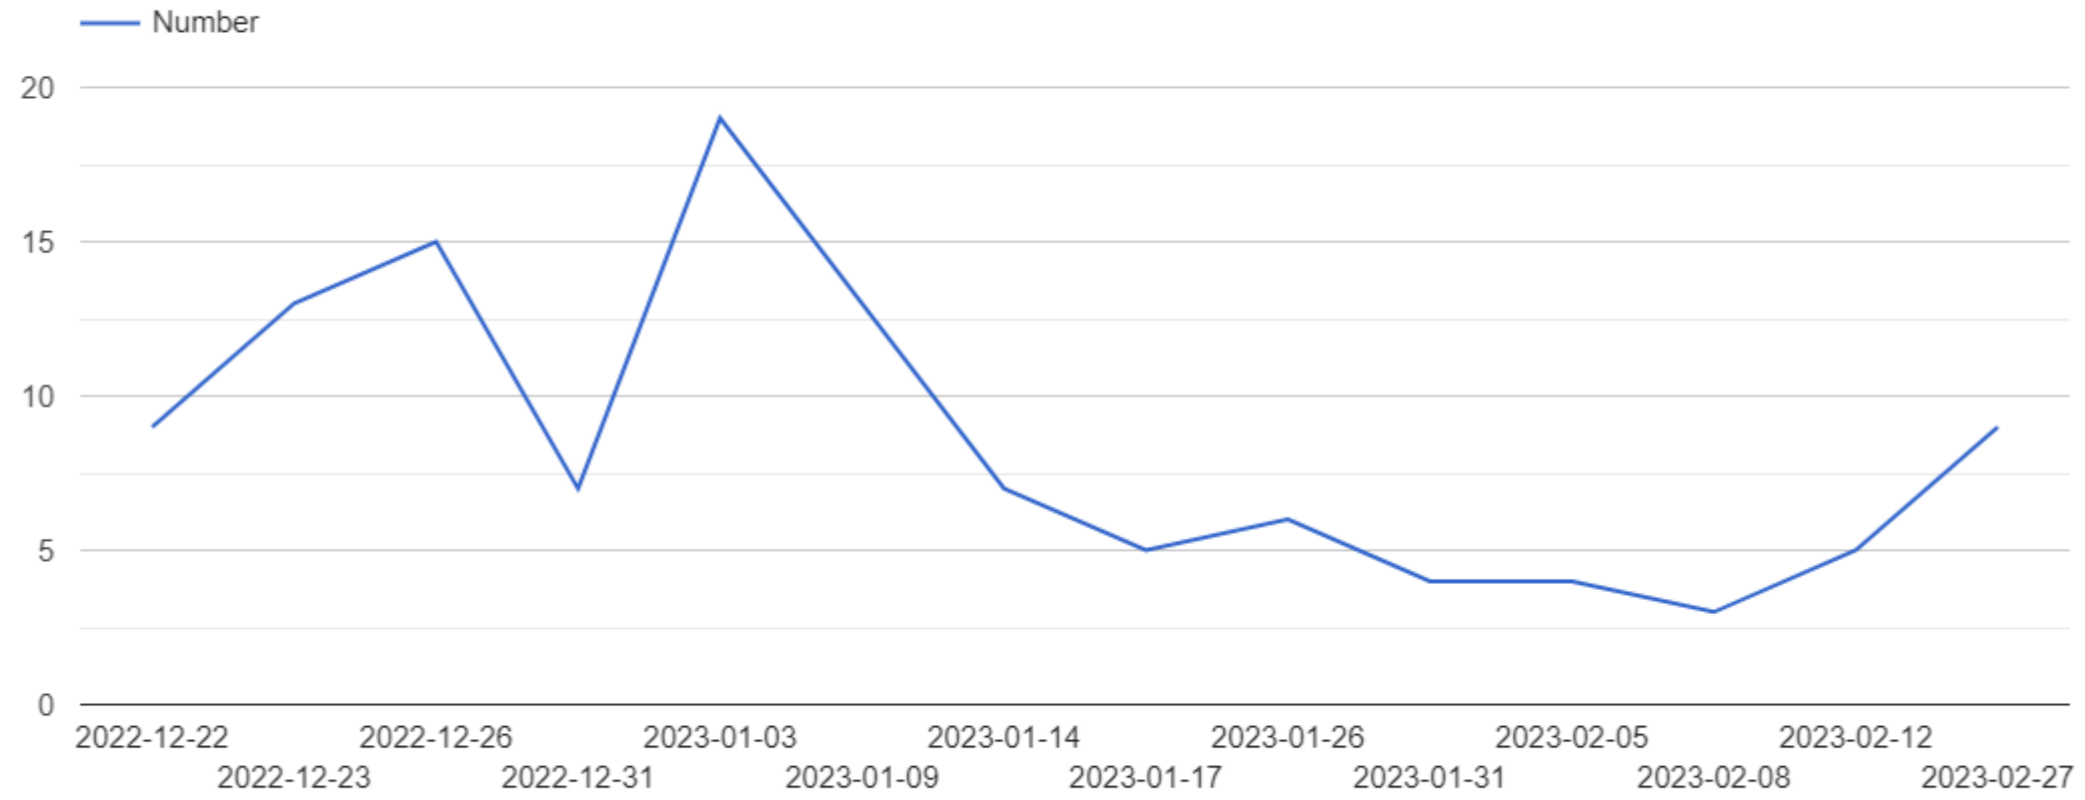

CUMMULATIVE WORK PROGRESS

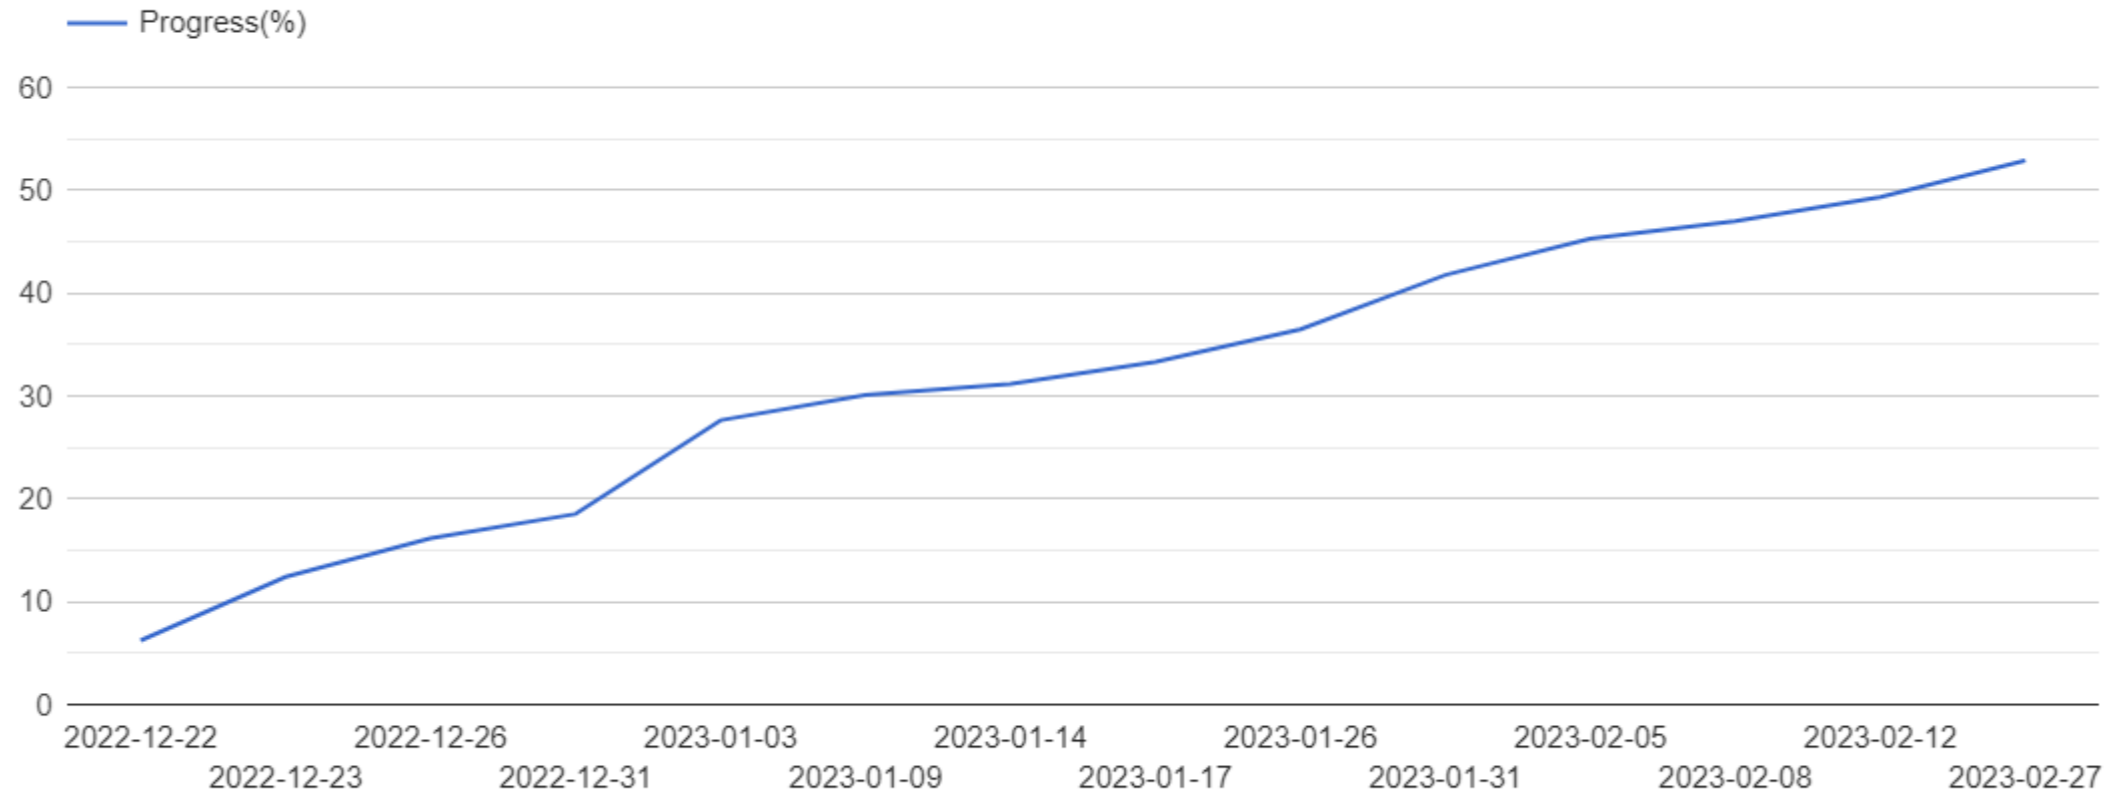

SCHEDULE AHEAD-BEHIND

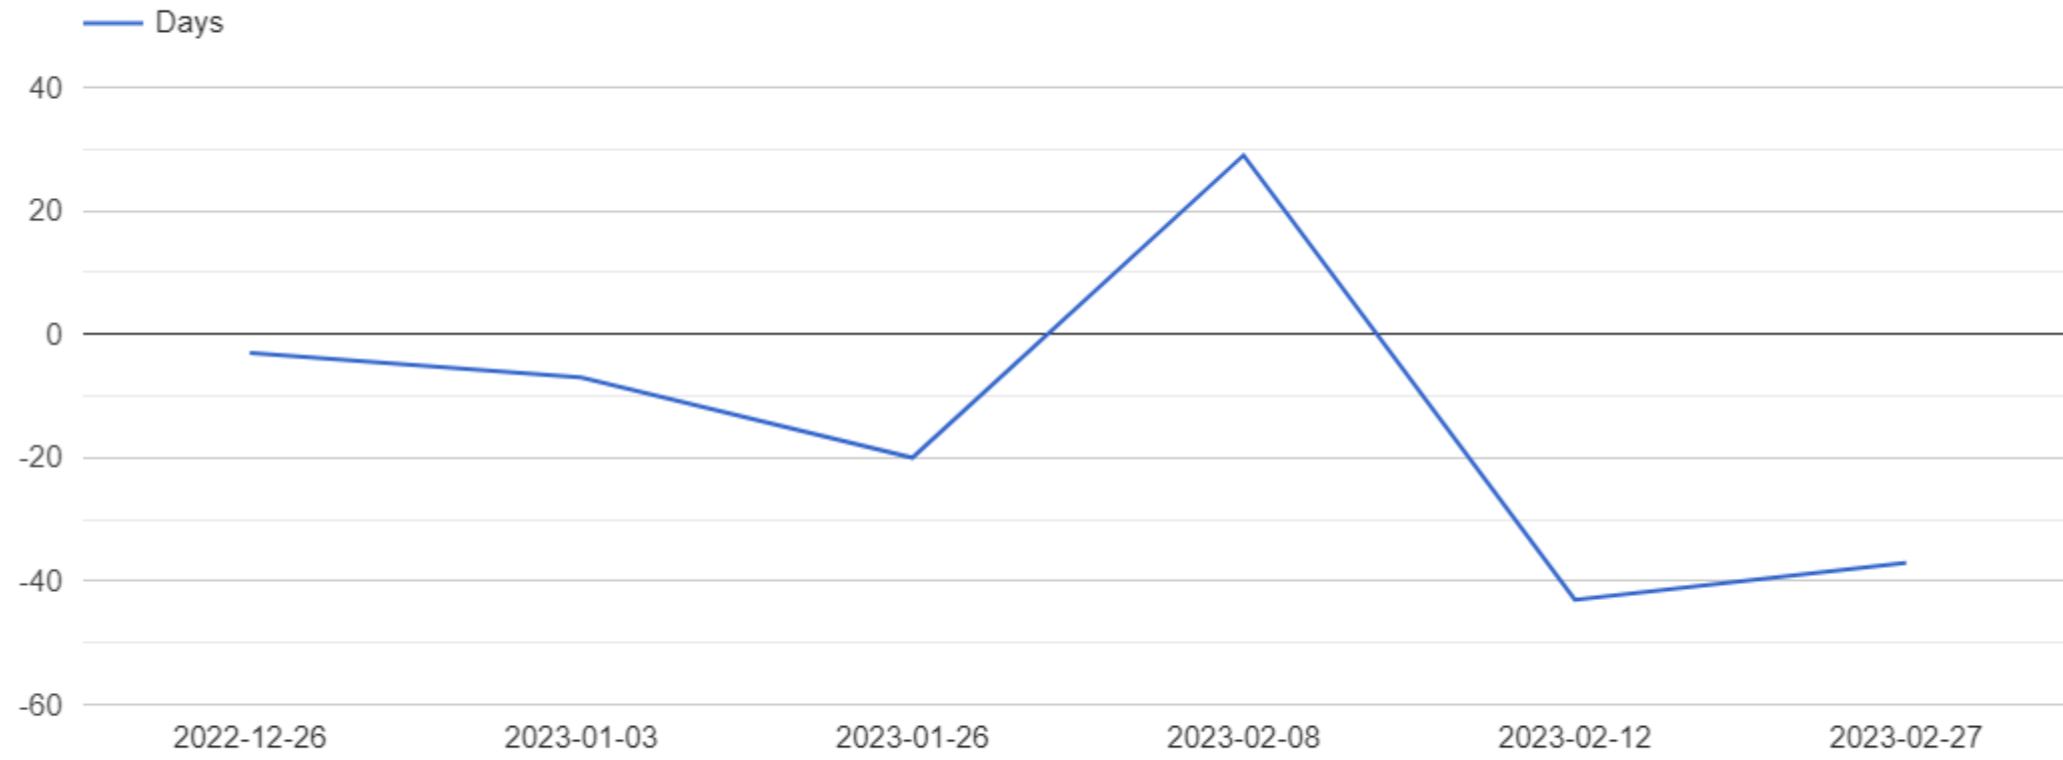

WORK PLAN AND PROGRESS

WORK PLAN FOR LEVEL-15 BAR AT CITYSCAPE TOWER



WBS	Task Name	Duration	Start	Finish	% Complete	Gantt Chart													
						22	17	24	31	07	14	21	28	04	11	18	25	04	
1	Level 15 Bar	78 d	22-12-22	09-03-23	54%	[Gantt bar for Level 15 Bar, 54% complete, ending at 28-02-23]													
1.1	Glss Work	31 d	22-12-22	21-01-23	85%	[Gantt bar for Glss Work, 85% complete]													
1.2	Carpentry Mock-up	2 d	22-12-22	23-12-22	100%	[Gantt bar for Carpentry Mock-up, 100% complete]													
1.3	Bar Counter	16 d	22-12-22	06-01-23	50%	[Gantt bar for Bar Counter, 50% complete]													
1.4	Washroom Brickwork	6 d	22-12-22	27-12-22	90%	[Gantt bar for Washroom Brickwork, 90% complete]													
1.5	Floor Finsh-NCF	6 d	26-12-22	31-12-22	100%	[Gantt bar for Floor Finsh-NCF, 100% complete]													
1.6	<i>Wall Panelling</i>	<i>30 d</i>	<i>08-02-23</i>	<i>09-03-23</i>	<i>5%</i>	[Gantt bar for Wall Panelling, 5% complete]													

Task		Progress		Rolled Up Task		Rolled Up Progress		Group By Summary
Critical Task		Summary		Rolled Up Critical Task		Project Summary		

PROGRESS PHOTO

Site Photographs



on 05-02-23



on 05-02-23

Site Description

Site Instruction



Wall Paneling on 08-02-23



Wall Paneling on 08-02-23

Site Description

Site Instruction



L-15-Floor Neat Cement Finishing on 12-02-23



L-15-Floor Neat Cement Finishing on 12-02-23

Site Description

Site Instruction



L-15-North Side Glass Framing on 27-02-23

L-15-North Side Glass Framing on 27-02-23

Site Description

Site Instruction

Entry by:	Generated by:
Planning Engineer	www.bel3c.com, Developed by: Engr. Md. Sanaul Haque
