

**CONSTRUCTION OF CITYSCAPE LIFE STYLE  
AT CITYSCAPE TOWER 53, GULSHAN AVENUE, DHAKA,  
BANGLADESH**

**WEEKLY  
RUNNING PROGRESS**



**28 OCTOBER 2023**

Generated by: Cityscape International Ltd.

## TABLE OF CONTENTS

- LAST WEEK PROGRESS
- LAST WEEK MANPOWER HISTOGRAM
- LAST WEEK PROGRESS CHART
- DAILY PROGRESS REPORT
  
- TOTAL PROGRESS
- TOTAL MANPOWER CHART
- CUMMULATIVE PROGRESS CHART
- SCHEDULE LEAD-LAG CHART
  
- TOTAL WORK PLAN AND PROGRESS
- WEEKLY PLAN
- PROGRESS PHOTO



# WEEKLY PROGRESS REPORT

From 22-October-2023 to 28-October-2023


Project Code:	63	Name:	Cityscape Lifestyle
Client:	Cityscape Lifestyle	Contractor:	Cityscape

## Weekly Progress


WBS	Task	Total Qty	Upto Last Week(%)	This Week(%)	Total Done(%)	Schedule Start	Schedule Finish	Actual Finish
03.1.3	L-14-Kitchen Floor dismantling	16m3	92	5	97	17-10-23	19-10-23	25-10-23
03.1.4	L-14-Old Kitchen Floor debris shift	1sum	20	55	75	20-10-23	22-10-23	28-10-23

**MANPOWER HISTOGRAM**

Sikder-Foreman    Sikder-Labor-Day shift    Sikder-Labor-Night shift  
Sikder-Mason-Day shift    Sikder-Mason-Night shift

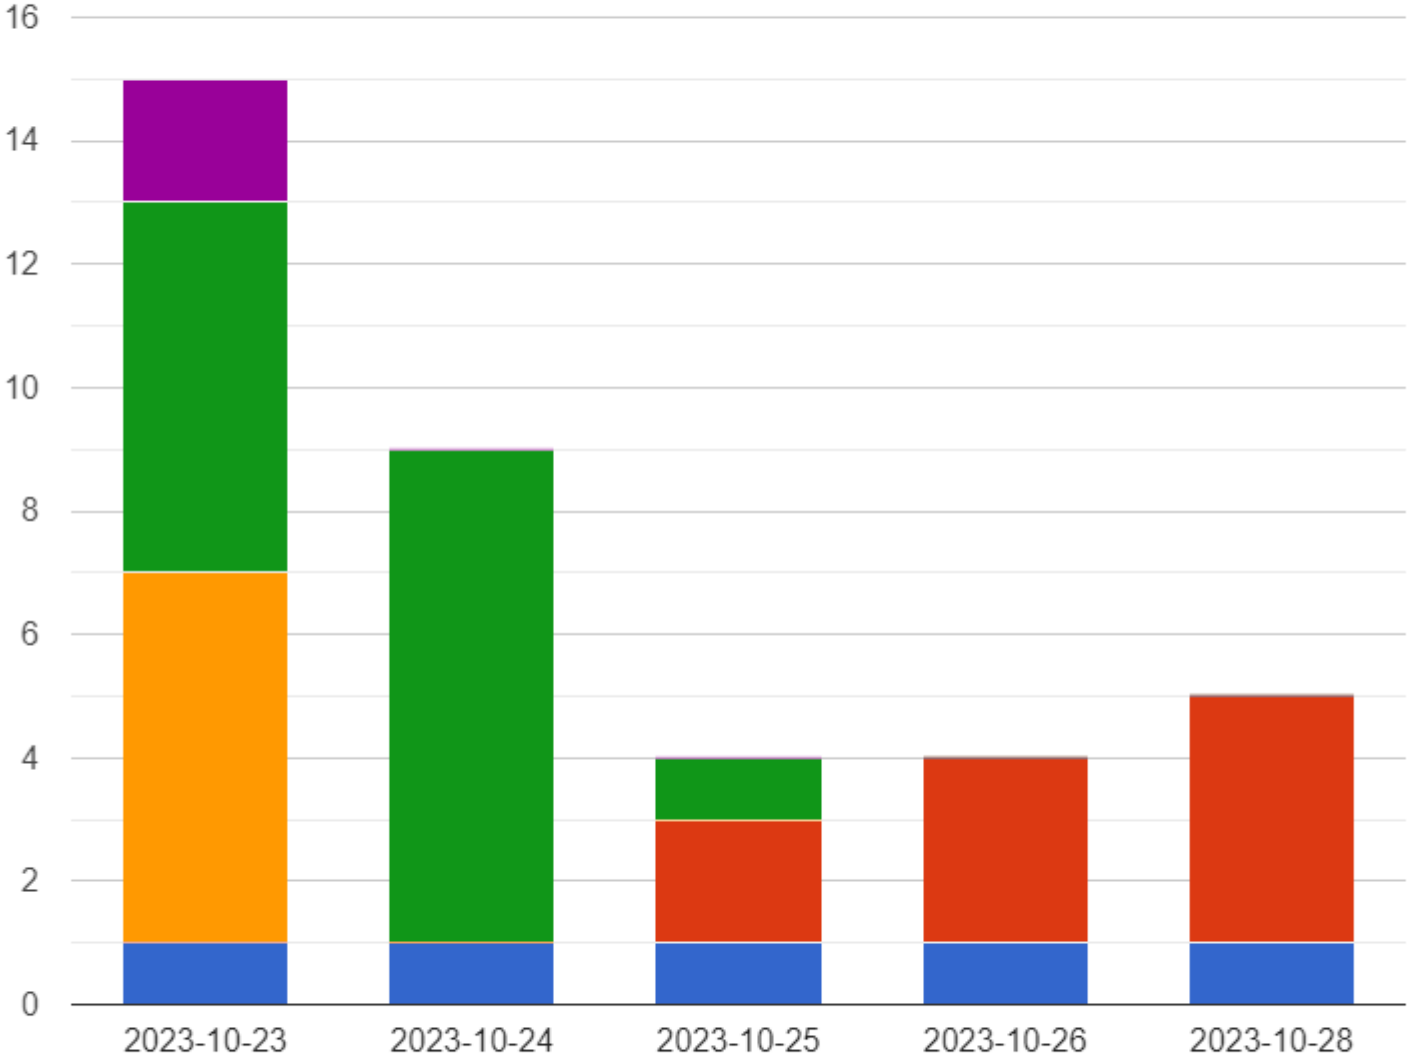

# DAILY PROGRESS

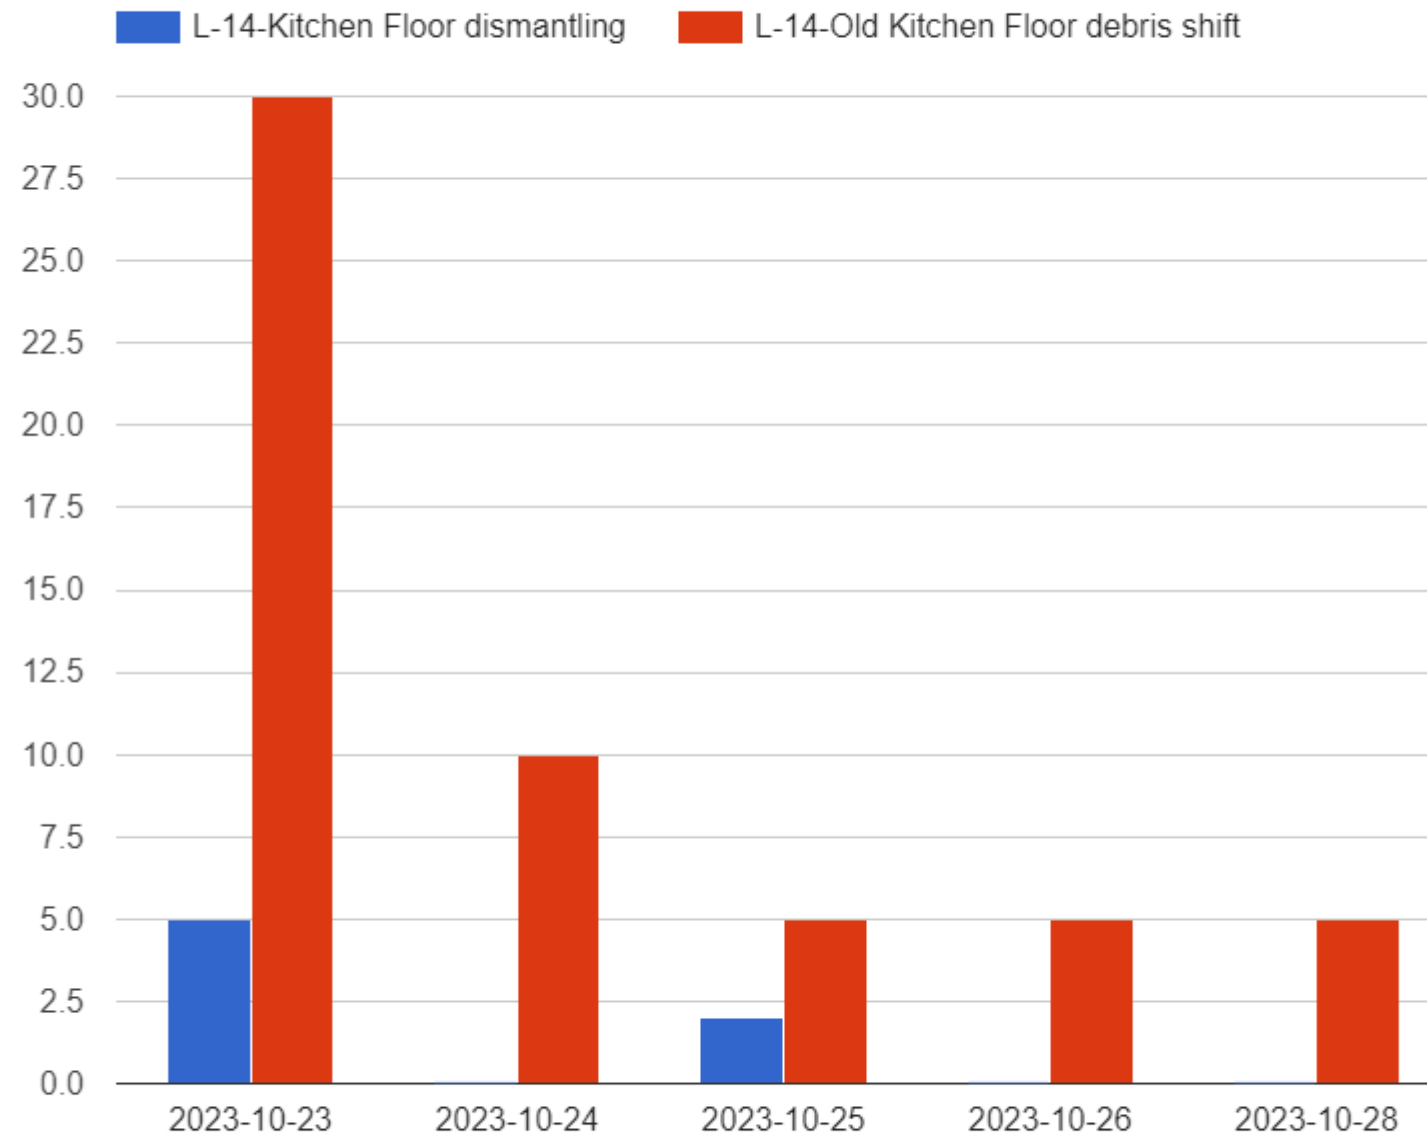



# DAILY PROGRESS REPORT

Project:	Cityscape Lifestyle	Project Code:	63	Date:	28-October-2023
Client:	Cityscape Lifestyle	Report	017	Day	Saturday
Contractor:	Cityscape			Climate	Sunny
					25-32C

## Manpower

SN	Description	Nos.
02	Sikder-Foreman	1
06	Sikder-Labor-Day shift	4
TOTAL		5

## Progress This Day

WBS	Task	Total Qty	Today Done(%)	Total Done(%)	Schedule Start	Schedule Finish
03.1.4	L-14-Old Kitchen Floor debris shift	1sum	5	75	20-10-23	22-10-23

## Site Photographs



L-14-Old Kitchen Area



L-14-Old Kitchen Area

Site Description	
Site Instruction	
Entry by:	Generated by:
Planning Engineer	www.bel3c.com, Developed by: Engr. Md. Sanaul Haque

TOTAL REPORT



# TOTAL PROGRESS REPORT

From 7-October-2023 to 28-October-2023


Project Code:	63	Name:	Cityscape Lifestyle						
Client:	Cityscape Lifestyle			Contractor:	Cityscape				
Planning Progress =	100%	Actual Progress=	97.2%	SPI=	0.97	Behind Schedule			

## Total Progress


WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)	Not Yet
03.1.1	L14-Old Kitchen Wall-Shelf dismantl	1sum	100	09-10-23	12-10-23	09-10-23	15-10-23	-3	
03.1.2	L14-Old Kitchen Wall Debris shiftin	1sum	100	13-10-23	16-10-23	13-10-23	19-10-23	-3	
03.1.3	L-14-Kitchen Floor dismantling	16m3	97	17-10-23	19-10-23	17-10-23	25-10-23	-6	Completed
03.1.4	L-14-Old Kitchen Floor debris shift	1sum	75	20-10-23	22-10-23	19-10-23	28-10-23	-6	Completed
03.1.5	L-14-East-South Brickwall dismantli	20m2	100	17-10-23	17-10-23	17-10-23	17-10-23	0	
03.1.6	L-14-Wall Debris shifting	1sum	100	18-10-23	18-10-23	17-10-23	17-10-23	1	
03.2	L-14-Stair Case-South-Door Cutting	1nos	100	14-10-23	16-10-23	14-10-23	17-10-23	-1	
12.1.1	L-4-North-East-Vault Dismantling	1sum	100	05-10-23	12-10-23	07-10-23	14-10-23	-2	
12.1.2	L-4-North-East-Vault debris shiftin	1sum	100	13-10-23	14-10-23	10-10-23	15-10-23	-1	




# DAILY MANPOWER

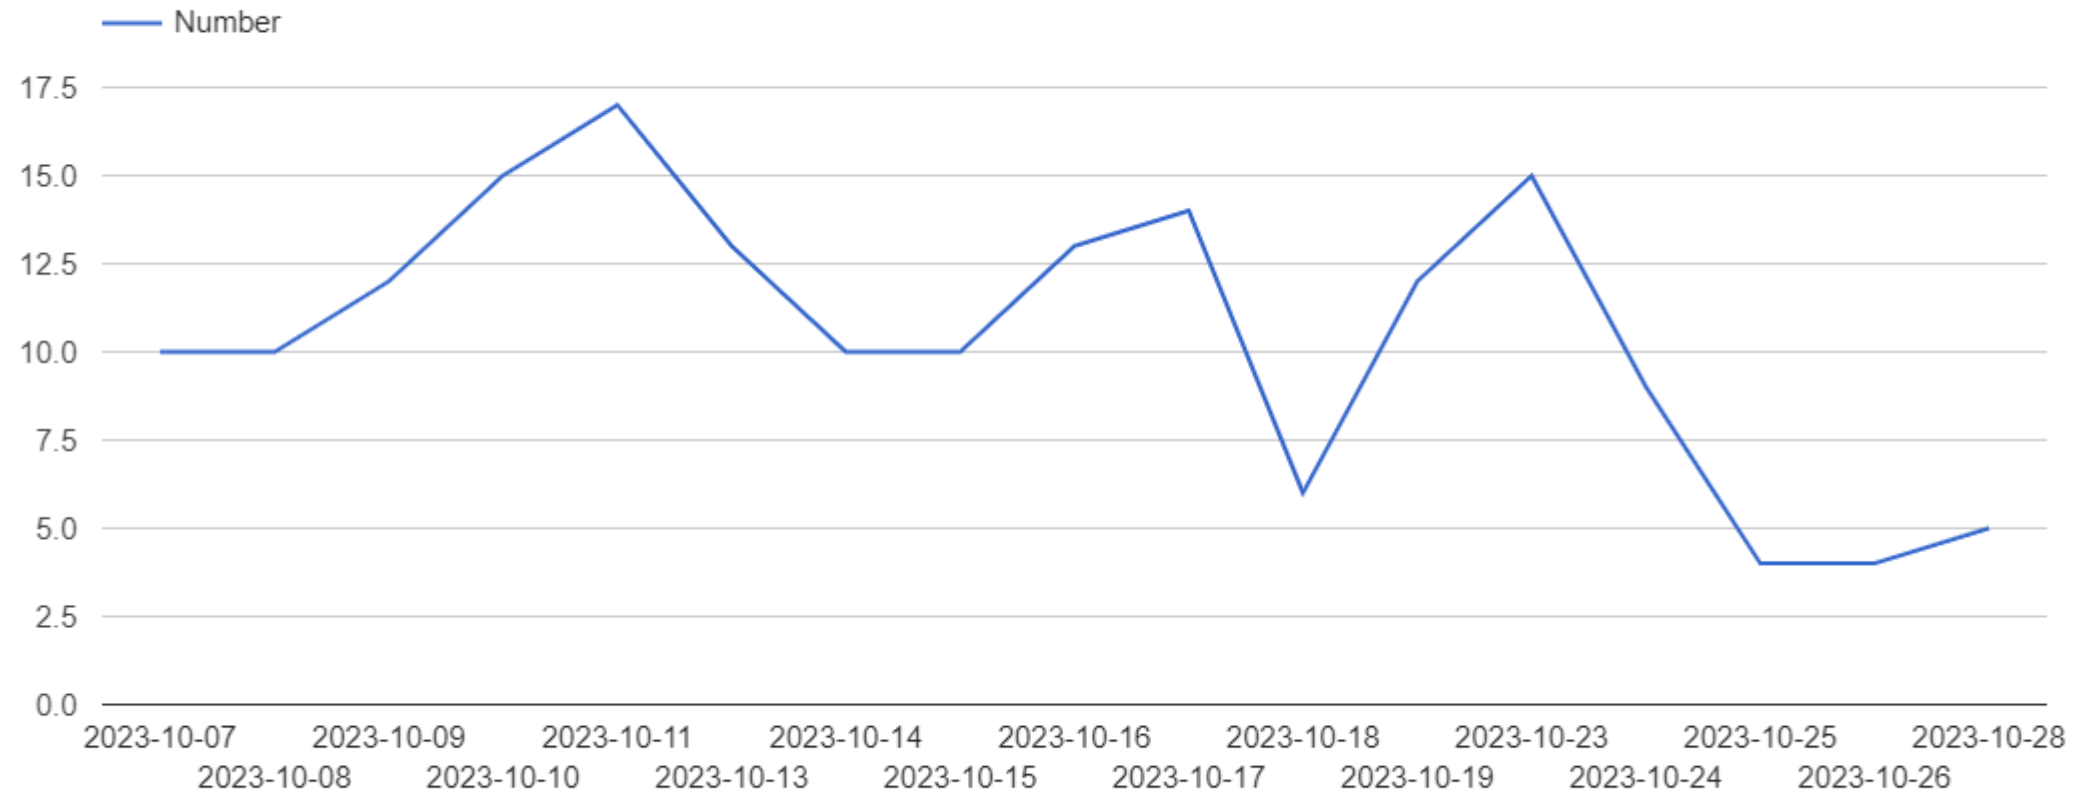


### CUMMULATIVE ACTUAL WORK PROGRESS

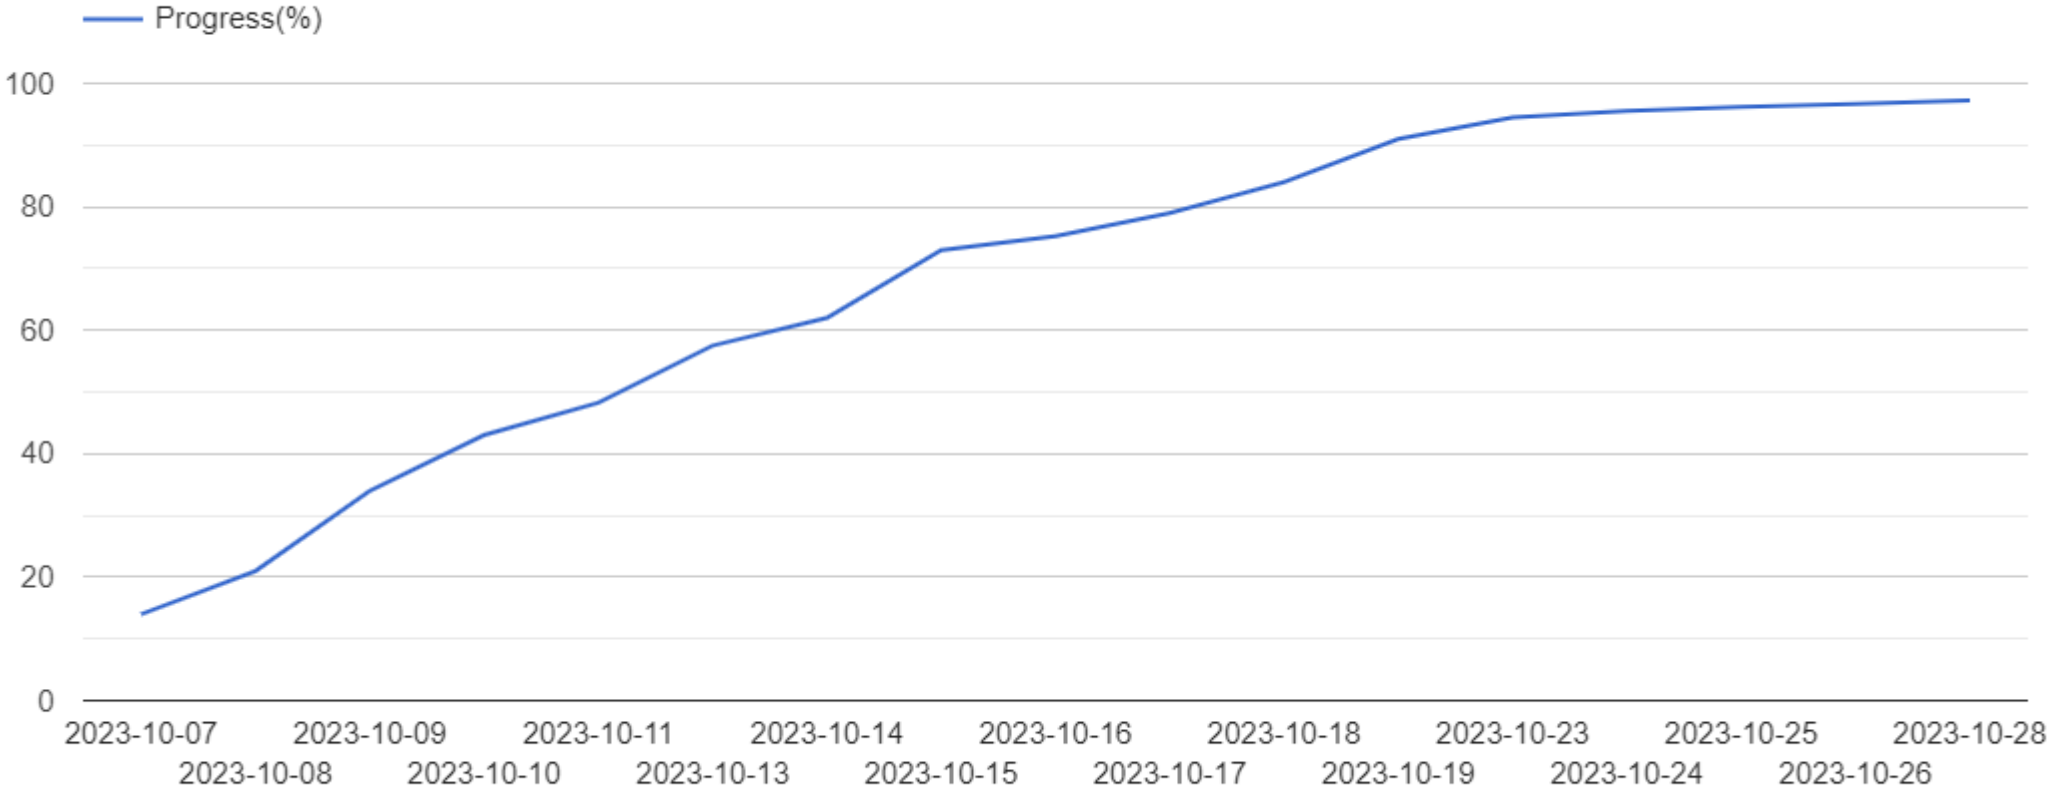


### CUMMULATIVE PLAN WORK PROGRESS

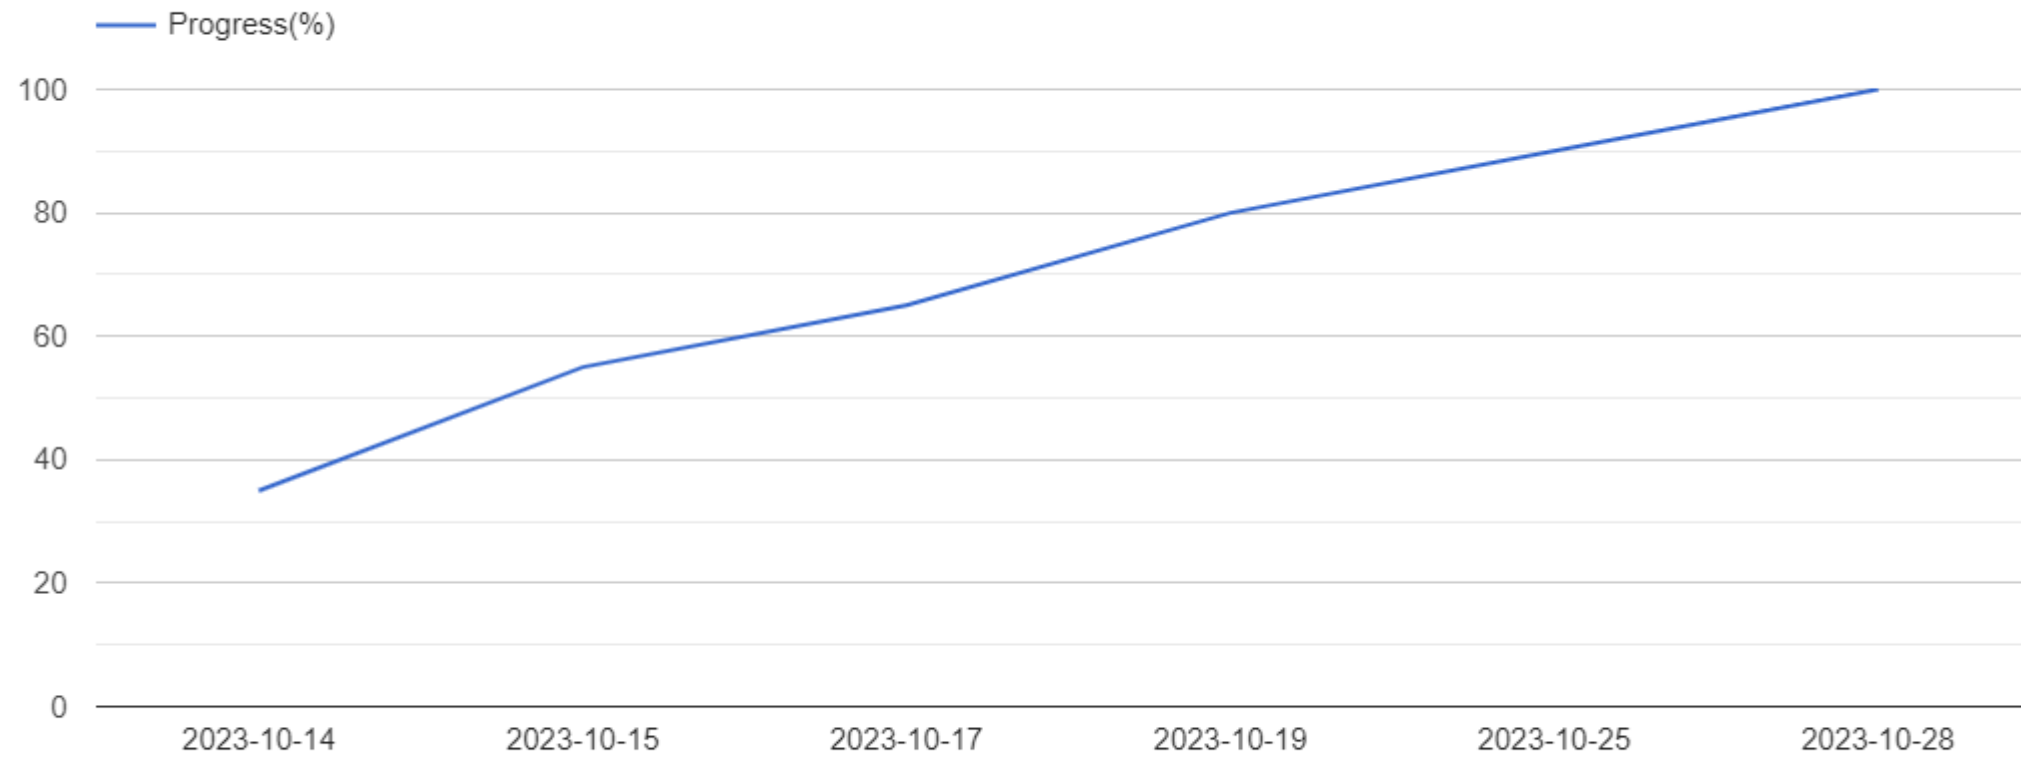

# CUMMULATIVE WORK PROGRESS

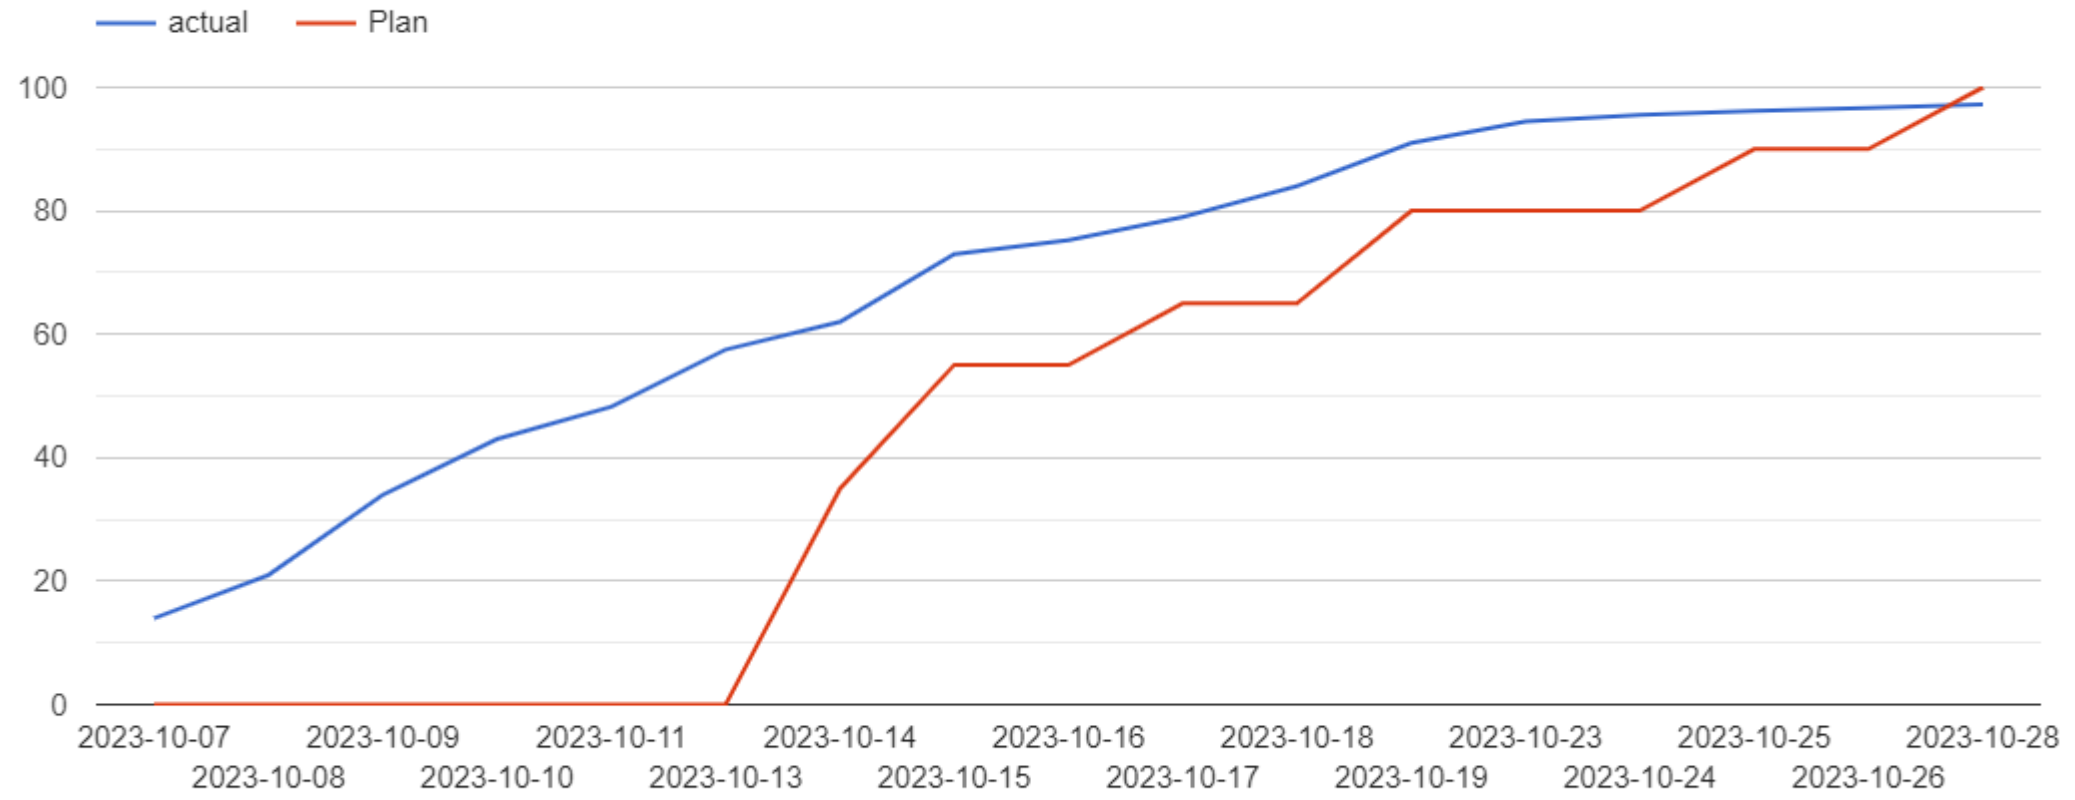

# SCHEDULE AHEAD-BEHIND

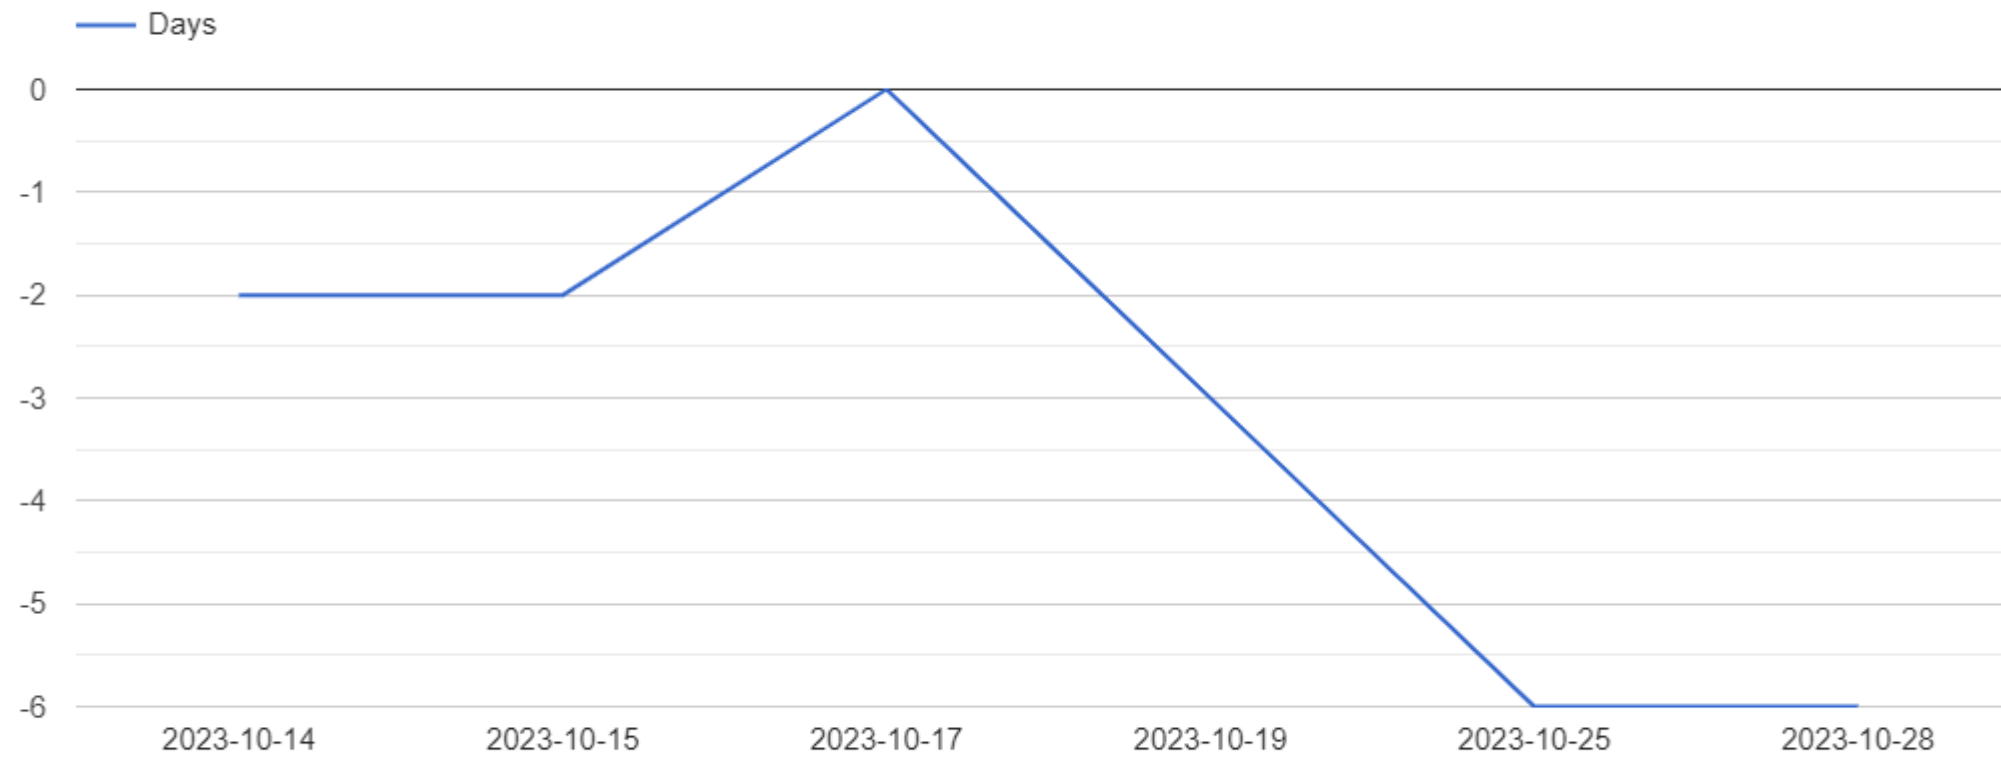

# **WORK PLAN AND PROGRESS**

# WORK PLAN AND PROGRESS FOR CITYSCAPE LIFESTYLE

Sl.	Task Name	Service	User	Duration	Shedule Start	Shedule Finish	% Complete	Oct '23							Nov '23				Dec '23			Jan '24				
								30	07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	
1	<b>Cityscape Lifestyle</b>			123 d	01/10/23	31/01/24	3%																			
1.1	Level-17: Rooftop Bar	Outdoor, Open to Sky/ Tent, Shisha, Prep Kitchen, Party Stage, Mazzanine	Public	122 d	01/10/23	30/01/24	0%																			
1.2	<i>Level-15-16: Premium Bar &amp; Restaurant</i>	<i>High Voltage Bar, Restaurant, Cigar, Shisha</i>	<i>Member</i>	123 d	01/10/23	31/01/24	0%																			
1.3	<b>Level-14: Upbeat Bar &amp; Restaurant</b>	<b>Bar, Restaurant, Shisha</b>	<b>Corporate &amp; Member</b>	14 d	09/10/23	22/10/23	96%																			
1.3.1	<b>Demolition</b>			14 d	09/10/23	22/10/23	95%																			
1.3.1.1	Old Kitchen Wall and Shelf			4 d	09/10/23	12/10/23	100%																			
1.3.1.2	Kitchen debris shifting to Basement			4 d	13/10/23	16/10/23	100%																			
1.3.1.3	Kitchen Floor-Dismantling			3 d	17/10/23	19/10/23	97%																			
1.3.1.4	Kitchen Floor Debris Shifting to Basement			3 d	20/10/23	22/10/23	75%																			
1.3.1.5	East-South Brick Wall			1 d	17/10/23	17/10/23	100%																			
1.3.1.6	Wall Debris Shifting to Basement			1 d	18/10/23	18/10/23	100%																			
1.3.2	Door Cutting at Staircase-South			3 d	14/10/23	16/10/23	100%																			
1.4	Level-13 : Andaz	Casual Restaurant	Public	31 d	01/10/23	31/10/23	0%																			
1.5	Level-12 : Corporate Event Vanue	Event Floor, Art Gallery, Pantry Space	Corporate	31 d	01/10/23	31/10/23	0%																			
1.6	Level-11 : Executive Business Lounge	Mini Bar, Pool, Card Room, Mini Theater	Member	31 d	01/10/23	31/10/23	0%																			
1.7	<b>Level-9-10: Premium Suit</b>	<b>Residential Suites</b>	<b>Member</b>	60 d	01/10/23	29/11/23	0%																			
1.7.1	Level-9: Mock-up			60 d	01/10/23	29/11/23	0%																			
1.8	Level-8: Cityscape Corporate Office	Cityscape Lifestyle & Executive Office	HQ	7 d	01/10/23	07/10/23	0%																			
1.9	Level-7: Wellness Center-Unisex	Gym, Suana, Steam, Consultation Room (Fitness & Stress Relieving)	Member	61 d	01/10/23	30/11/23	0%																			
1.10	Level-6: Wellness Center-Female	Gym, Suana, Steam, Consultation Room (Fitness & Stress Relieving)	Member	92 d	01/10/23	31/12/23	0%																			
1.11	Level-5: Cityscape Corporate Office	Cityscape Back Offices	HQ	92 d	01/10/23	31/12/23	0%																			
1.12	<b>Level-4:</b>			10 d	05/10/23	14/10/23	100%																			
1.12.1	<b>Demolition</b>			10 d	05/10/23	14/10/23	100%																			
1.12.1.1	North-East Vault-Dismantling			8 d	05/10/23	12/10/23	100%																			
1.12.1.2	North-East Vault debris shifting to Basement			2 d	13/10/23	14/10/23	100%																			
1.13	Level-3 : Cityscape Service Floor	Kitchen, F&B Operation, Store	HQ	61 d	01/10/23	30/11/23	0%																			
1.14	Level-2: Bank		Public	10 d	01/10/23	10/10/23	0%																			
1.15	Level-1: Happyness Café	Café	Public	30 d	01/10/23	30/10/23	0%																			
1.16	Entrance: Entry Gate & Lobby	Vehicular Entry, Security, Reception, Lift Lobby	Public	90 d	01/10/23	29/12/23	0%																			
1.17	Basement : VIP Lobby, Parking	VIP Entry & Parking, Security, Reception, Lift Lobby	Corporate & Member	90 d	01/10/23	29/12/23	0%																			

**PROGRESS PHOTO**



## Site Photographs



L-14-Kitchen Floor Debris Removing on 23-10-23



L-14-Kitchen Area on 23-10-23

Site Description

Site Instruction



L-14-Kitchen Area on 24-10-23



L-14-Kitchen Area on 24-10-23

Site Description

Site Instruction



L-14-Old Kitchen Floor Dismantling on 25-10-23



L-14-Old Kitchen Area on 25-10-23

Site Description

Site Instruction



L-14-Old Kitchen Area on 26-10-23

L-14-Old Kitchen Area Debris removing on 26-10-23

Site Description

Site Instruction



L-14-Old Kitchen Area on 28-10-23

L-14-Old Kitchen Area on 28-10-23

Site Description

Site Instruction

Entry by:  
Planning Engineer

Generated by:  
www.bel3c.com, Developed by: Engr. Md. Sanaul Haque
