

**CONSTRUCTION OF NBL TWIN TOWER  
AT PANTHAPTH, DHAKA**

**PROGRESS REPORT**



03 SEP 2021

Generated by: Cityscape International Limited

## TABLE OF CONTENTS

- TOTAL PROGRESS
- TOTAL MANPOWER CHART
- CUMMULATIVE PROGRESS CHART
- SCHEDULE LEAD-LAG CHART
  
- LAST MONTH PROGRESS
- LAST MONTH MANPOWER HISTOGRAM
- LAST MONTH PROGRESS CHART
- DAILY PROGRESS REPORT
  
- WORK PLAN AND PROGRESS

From 6-January-2021 to 2-September-2021

Project Code:	42	Name:	NBL Tower-Superstucure
Client:	National Bank Limited	Contractor:	Cityscape International Ltd.


## Total Progress

WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Finish	Lead-Lag(day)
01	Ground Floor		100	11-11-20	12-12-20	12-12-20	0
03	2nd Floor		100	18-12-20	06-01-21	06-01-21	0
04.1.1	3rd Floor-South Tower-Column	14nos	100	02-01-21	08-01-21	06-01-21	2
04.1.2	3rd Floor-South Tower-Lift Core	2nos	100	02-01-21	08-01-21	06-01-21	2
04.1.3	3rd Floor-South Tower-Stair	2nos	100	09-01-21	13-01-21	11-01-21	2
04.1.4	3rd Floor-South Tower-Roof Slab	958sqm	100	09-01-21	13-01-21	11-01-21	2
04.2.1	3rd Floor-North Tower-Column	11nos	100	07-01-21	13-01-21	14-01-21	-1
04.2.2	3rd Floor-North Tower-Lift Core	2nos	100	07-01-21	13-01-21	16-01-21	-3
04.2.3	3rd Floor-North Tower-Stair	2nos	100	14-01-21	18-01-21	18-01-21	0
04.2.4	3rd Floor-North Tower-Roof Slab	958sqm	100	14-01-21	18-01-21	18-01-21	0
05.1.1	4th Floor-South Tower-Column	14nos	100	14-01-21	20-01-21	14-01-21	6
05.1.2	4th Floor-South Tower-Lift Core	2nos	100	14-01-21	20-01-21	16-01-21	4
05.1.3	4th Floor-South Tower-Stair	2nos	100	21-01-21	25-01-21	21-01-21	4
05.1.4	4th Floor-South Tower-Roof Slab	960sqm	100	21-01-21	25-01-21	21-01-21	4
05.2.1	4th Floor-North Tower-Column	11nos	100	19-01-21	25-01-21	19-01-21	6
05.2.2	4th Floor-North Tower-Lift Core	2nos	100	19-01-21	25-01-21	22-01-21	3
05.2.3	4th Floor-North Tower-Stair	2nos	100	26-01-21	30-01-21	27-01-21	3
05.2.4	4th Floor-North Tower-Roof Slab	960sqm	100	26-01-21	30-01-21	27-01-21	3
06.1.1	5th Floor-South Tower-Column	14nos	100	26-01-21	01-02-21	22-01-21	10
06.1.2	5th Floor-South Tower-Lift Core	2nos	100	26-01-21	01-02-21	24-01-21	8
06.1.3	5th Floor-South Tower-Stair	2nos	100	02-02-21	06-02-21	01-02-21	5
06.1.4	5th Floor-South Tower-Roof Slab	840sqm	100	02-02-21	06-02-21	01-02-21	5
06.2.1	5th Floor-North Tower-Column	11nos	100	31-01-21	06-02-21	29-01-21	8


WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Finish	Lead-Lag(day)
06.2.2	5th Floor-North Tower-Lift Core	2nos	100	31-01-21	06-02-21	02-02-21	4
06.2.3	5th Floor-North Tower-Stair	2nos	100	07-02-21	11-02-21	06-02-21	5
06.2.4	5th Floor-North Tower-Roof Slab	960sqm	100	07-02-21	11-02-21	06-02-21	5
07.1.1	6th Floor-South Tower-Column	14nos	100	07-02-21	13-02-21	03-02-21	10
07.1.2	6th Floor-South Tower-Lift Core	2nos	100	07-02-21	13-02-21	06-02-21	7
07.1.3	6th Floor-South Tower-Stair	2nos	100	14-02-21	18-02-21	16-02-21	2
07.1.4	6th Floor-South Tower-Roof Slab	963sqm	100	14-02-21	18-02-21	16-02-21	2
07.2.1	6th Floor-North Tower-Column	11nos	100	12-02-21	18-02-21	08-02-21	10
07.2.2	6th Floor-North Tower-Lift Core	2nos	100	12-02-21	18-02-21	18-02-21	0
07.2.3	6th Floor-North Tower-Stair	2nos	100	19-02-21	23-02-21	23-02-21	0
07.2.4	6th Floor-North Tower-Roof Slab	960sqm	100	19-02-21	23-02-21	23-02-21	0
08.1.1	7th Floor-South Tower-Column	14nos	100	19-02-21	25-02-21	19-02-21	6
08.1.2	7th Floor-South Tower-Lift Core	2nos	100	19-02-21	25-02-21	22-02-21	3
08.1.3	7th Floor-South Tower-Stair Case	2nos	100	26-02-21	02-03-21	01-03-21	1
08.1.4	7th Floor-South Tower-Roof Slab	950sqm	100	26-02-21	02-03-21	01-03-21	1
08.2.1	7th Floor-North Tower-Column	11nos	100	24-02-21	02-03-21	25-02-21	5
08.2.2	7th Floor-North Tower-Lift Core	2nos	100	24-02-21	02-03-21	02-03-21	0
08.2.3	7th Floor-North Tower-Stair Case	2nos	100	03-03-21	07-03-21	08-03-21	-1
08.2.4	7th Floor-North Tower-Slab	960m2	100	03-03-21	07-03-21	08-03-21	-1
09.1.1	8th Floor-South Tower-Column	14nos	100	03-03-21	09-03-21	05-03-21	4
09.1.2	8th Floor-South Tower-Lift Core	2nos	100	03-03-21	09-03-21	11-03-21	-2
09.1.3	8th Floor-South Tower-Stair Case	2nos	100	10-03-21	14-03-21	17-03-21	-3
09.1.4	8th Floor-South Tower-Roof Slab	963m2	100	10-03-21	14-03-21	17-03-21	-3
09.2.1	8th Floor-North Tower-Column	11nos	100	08-03-21	14-03-21	12-03-21	2
09.2.2	8th Floor-North Tower-Lift Core	2nos	100	08-03-21	14-03-21	20-03-21	-6
09.2.3	8th Floor-North Tower-Stair Case	2nos	100	15-03-21	19-03-21	05-04-21	-17
09.2.4	8th Floor-North Tower-Roof Slab	958m2	100	15-03-21	19-03-21	05-04-21	-17

<b>WBS</b>	<b>Task</b>	<b>Total Qty</b>	<b>Total Done(%)</b>	<b>Shedule Start</b>	<b>Schedule Finish</b>	<b>Actual Finish</b>	<b>Lead-Lag(day)</b>
10.1.1	9th Floor-South Tower-Column	14nos	100	15-03-21	21-03-21	31-03-21	-10
10.1.2	9th Floor-South Tower-Lift Core	2nos	100	15-03-21	21-03-21	06-04-21	-16
10.1.3	9th Floor-South Tower-Stair	2nos	100	22-03-21	26-03-21	13-04-21	-18
10.1.4	9th Floor-South Tower-Roof Slab	963m2	100	22-03-21	26-03-21	13-04-21	-18
10.2.1	9th Floor-North Tower-Column	11nos	100	20-03-21	26-03-21	09-04-21	-14
10.2.2	9th Floor-North Tower-Lift Core	2nos	100	20-03-21	26-03-21	16-04-21	-21
10.2.3	9th Floor-North Tower-Stair	2nos	100	27-03-21	31-03-21	23-04-21	-23
10.2.4	9th Floor-North Tower-Roof Slab	958m2	100	27-03-21	31-03-21	23-04-21	-23
11.1.1	10th Floor-South Tower-Column	14nos	100	27-03-21	02-04-21	17-04-21	-15
11.1.2	10th Floor-South Tower-Lift Core	2nos	100	27-03-21	02-04-21	21-04-21	-19
11.1.3	10th Floor-South Tower-Stair	2nos	100	03-04-21	07-04-21	04-05-21	-27
11.1.4	10th Floor-South Tower-Roof Slab	963m2	100	03-04-21	07-04-21	04-05-21	-27
11.2.1	10th Floor-North Tower-Column	11nos	100	01-04-21	07-04-21	27-04-21	-20
11.2.2	10th Floor-North Tower-Lift Core	2nos	100	01-04-21	07-04-21	02-05-21	-25
11.2.3	10th Floor-North Tower-Stair	2nos	100	08-04-21	12-04-21	10-05-21	-28
11.2.4	10th Floor-North Tower-Roof Slab	958m2	100	08-04-21	12-04-21	10-05-21	-28
12.1.1	11th Floor-South Tower-Column	14nos	100	08-04-21	14-04-21	09-05-21	-25
12.1.2	11th Floor-South Tower-Lift Core	2nos	100	08-04-21	14-04-21	12-06-21	-59
12.1.3	11th Floor-South Tower-Stair	2nos	100	15-04-21	19-04-21	02-09-21	-136
12.1.4	11th Floor-South Tower-Roof Slab	963m2	100	15-04-21	19-04-21	02-09-21	-136
12.2.1	11th Floor-North Tower-Column	11nos	100	13-04-21	19-04-21	04-06-21	-46
12.2.2	11th Floor-North Tower-Lift Core	2nos	50	13-04-21	19-04-21	15-06-21	-57


# DAILY MANPOWER

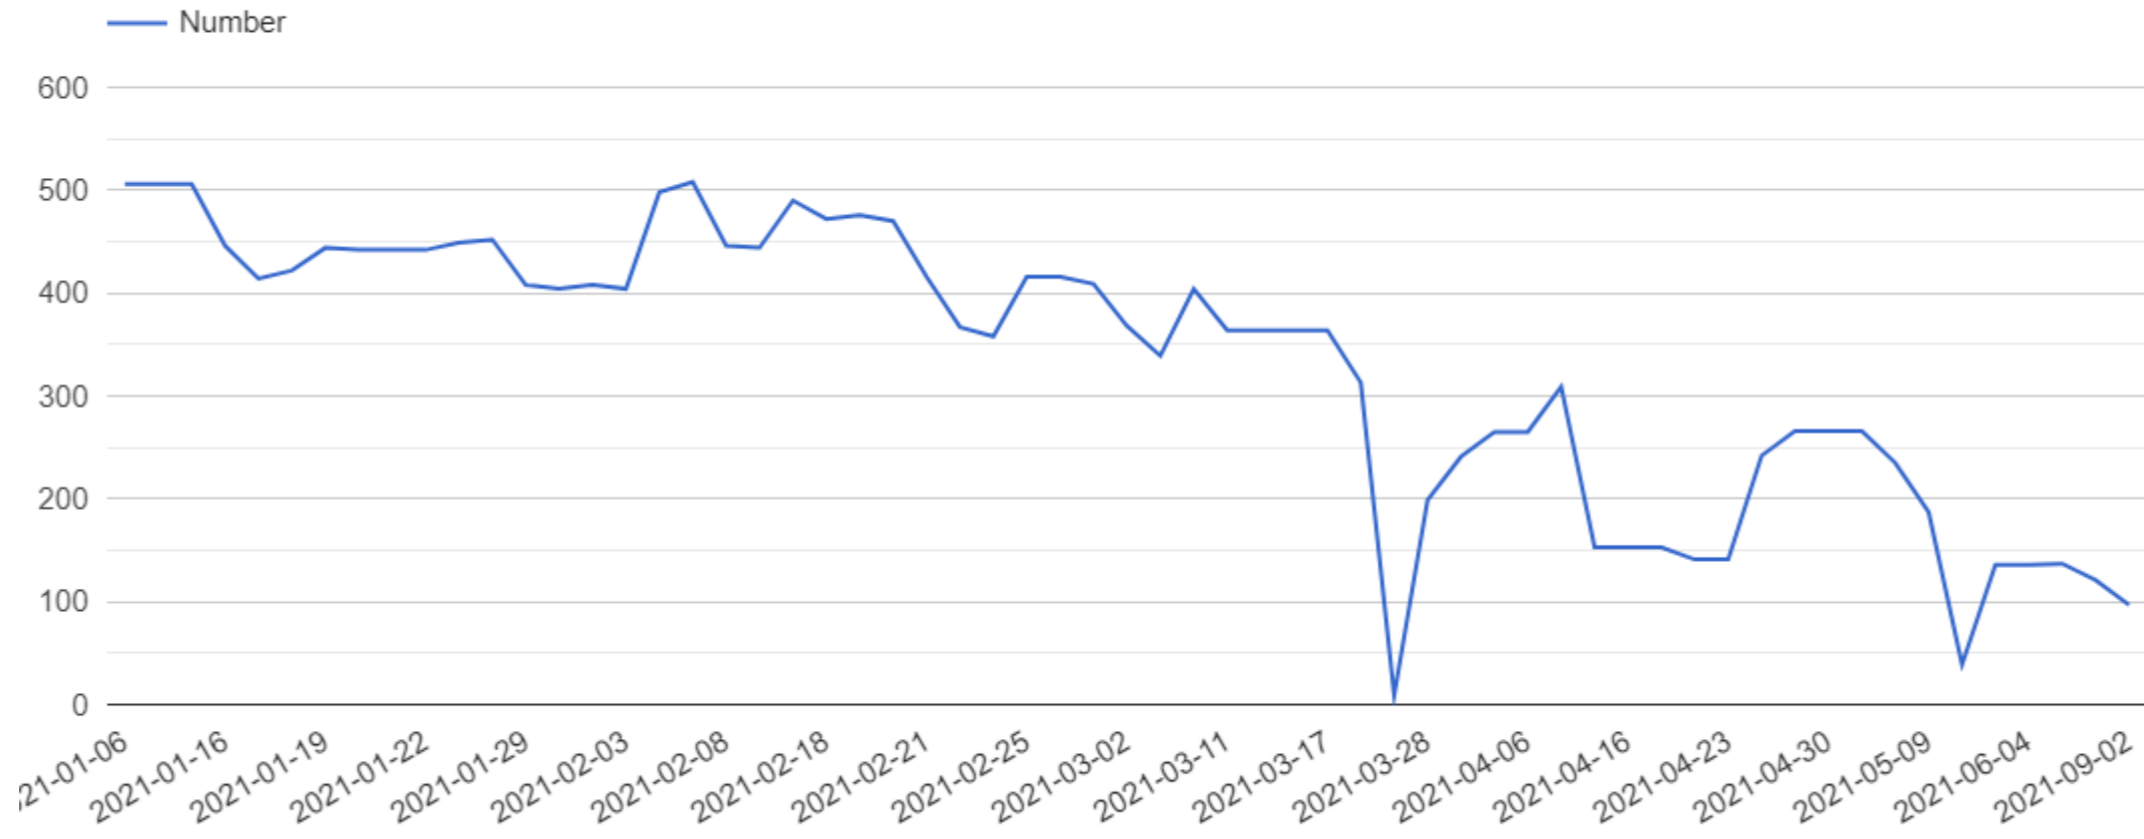

# CUMMULATIVE WORK PROGRESS

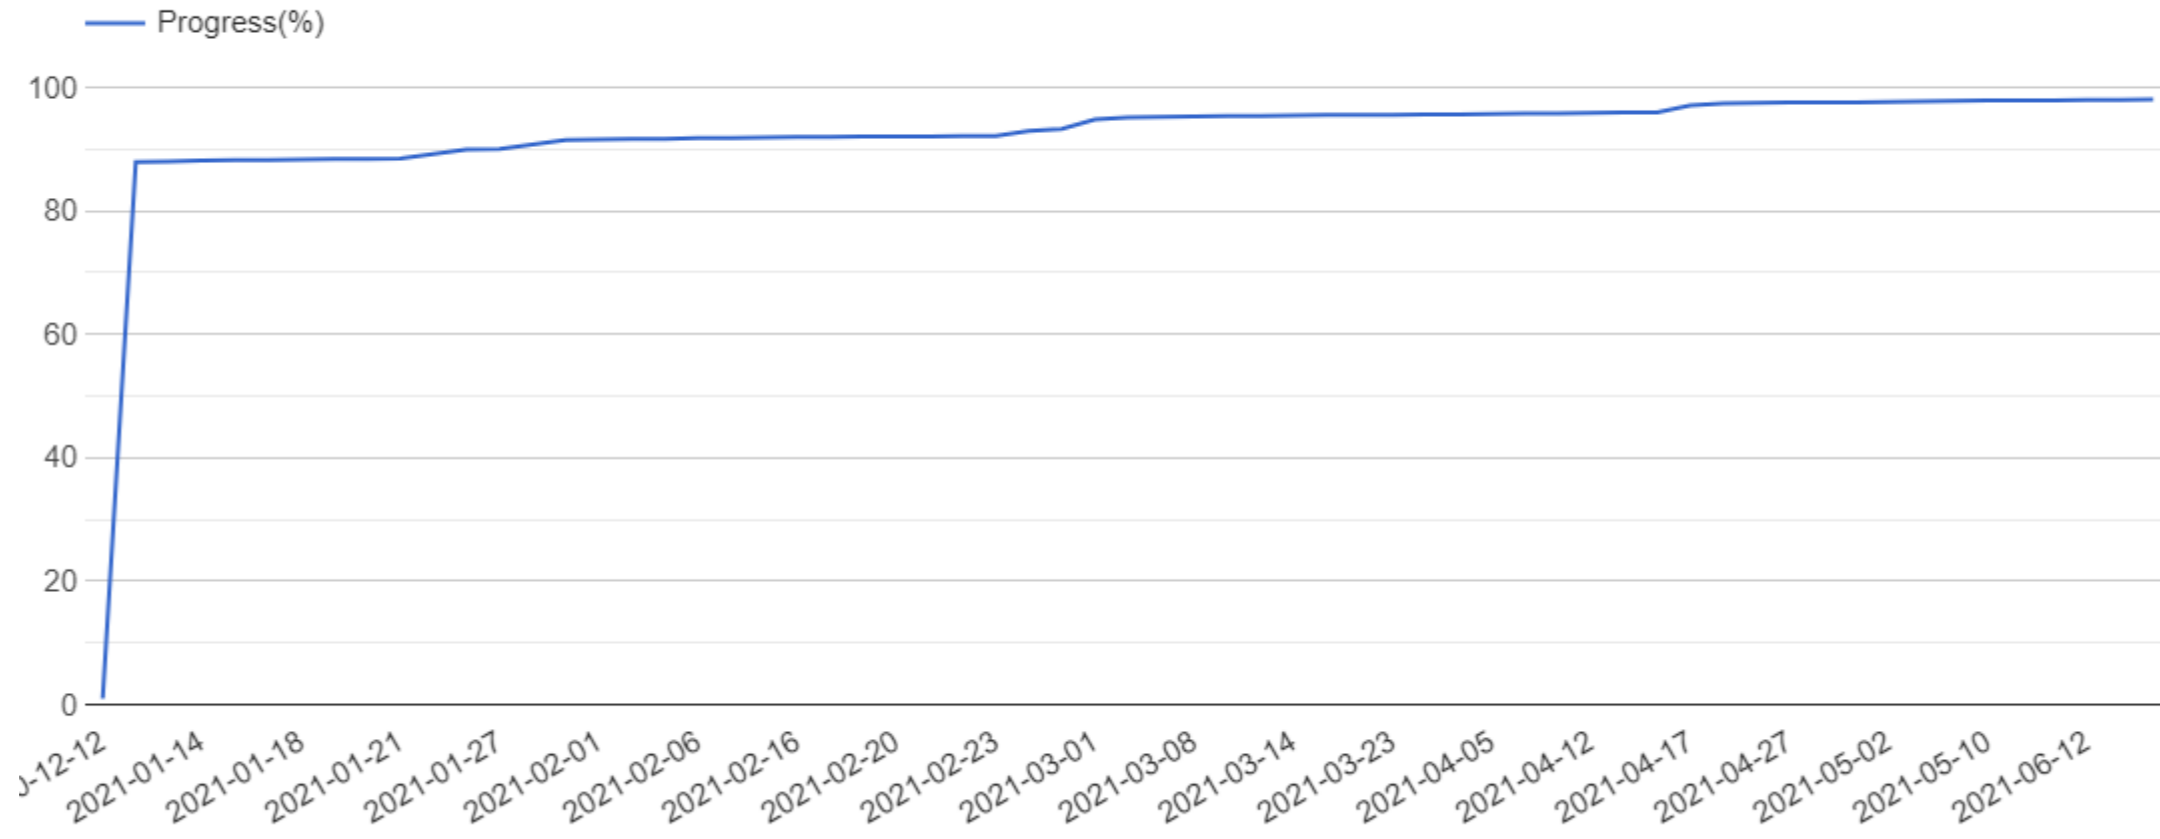

# SCHEDULE AHEAD-BEHIND

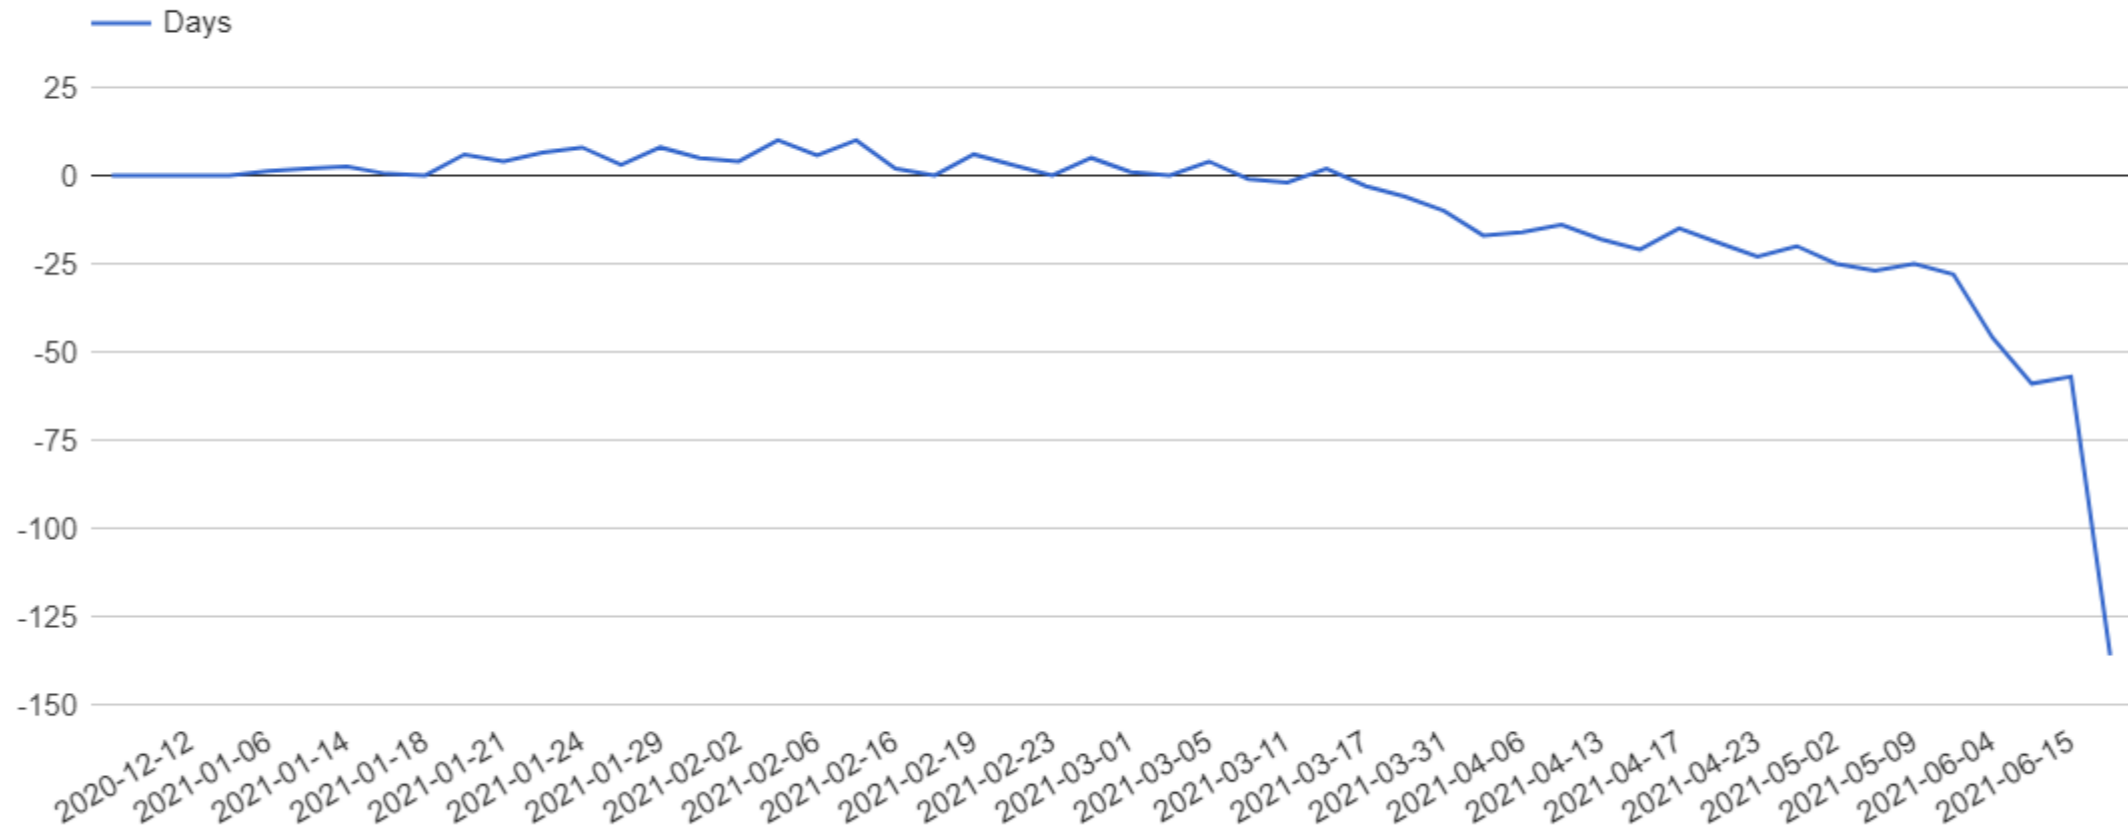



MONTHLY REPORT  
DAILY REPORT


From 1-May-2021 to 31-May-2021

Project Code:	42	Name:	NBL Tower-Superstucure
Client:	National Bank Limited	Contractor:	Cityscape International Ltd.


## Monthly Progress

WBS	Task	Total Qty	Upto Last Month(%)	This Month(%)	Total Done(%)	Schedule Start	Schedule Finish	Actual Finish
11.1.3	10th Floor-South Tower-Stair	2nos	0	100	100	03-04-21	07-04-21	04-05-21
11.1.4	10th Floor-South Tower-Roof Slab	963m2	0	100	100	03-04-21	07-04-21	04-05-21
11.2.2	10th Floor-North Tower-Lift Core	2nos	70	30	100	01-04-21	07-04-21	02-05-21
11.2.3	10th Floor-North Tower-Stair	2nos	0	100	100	08-04-21	12-04-21	10-05-21
11.2.4	10th Floor-North Tower-Roof Slab	958m2	0	100	100	08-04-21	12-04-21	10-05-21
12.1.1	11th Floor-South Tower-Column	14nos	0	100	100	08-04-21	14-04-21	09-05-21
12.1.2	11th Floor-South Tower-Lift Core	2nos	0	50	50	08-04-21	14-04-21	09-05-21
12.2.1	11th Floor-North Tower-Column	11nos	0	50	50	13-04-21	19-04-21	31-05-21

**MANPOWER HISTOGRAM**

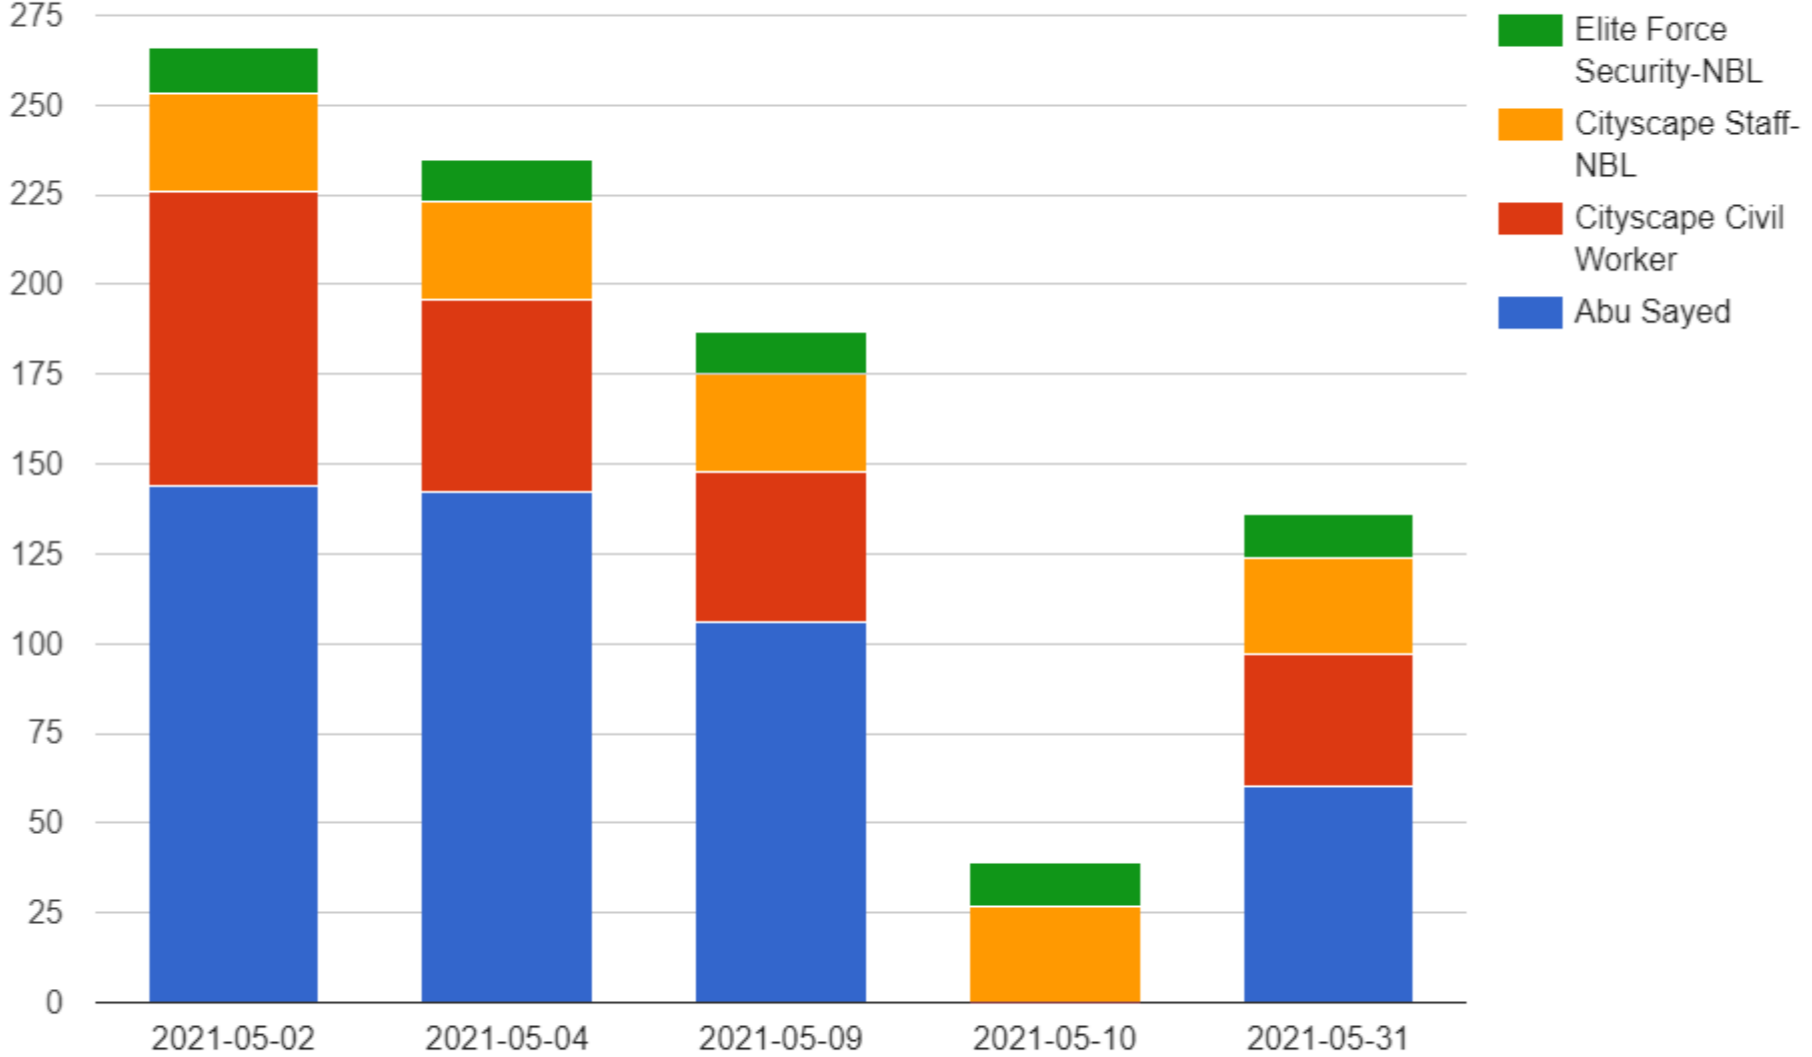

# DAILY PROGRESS

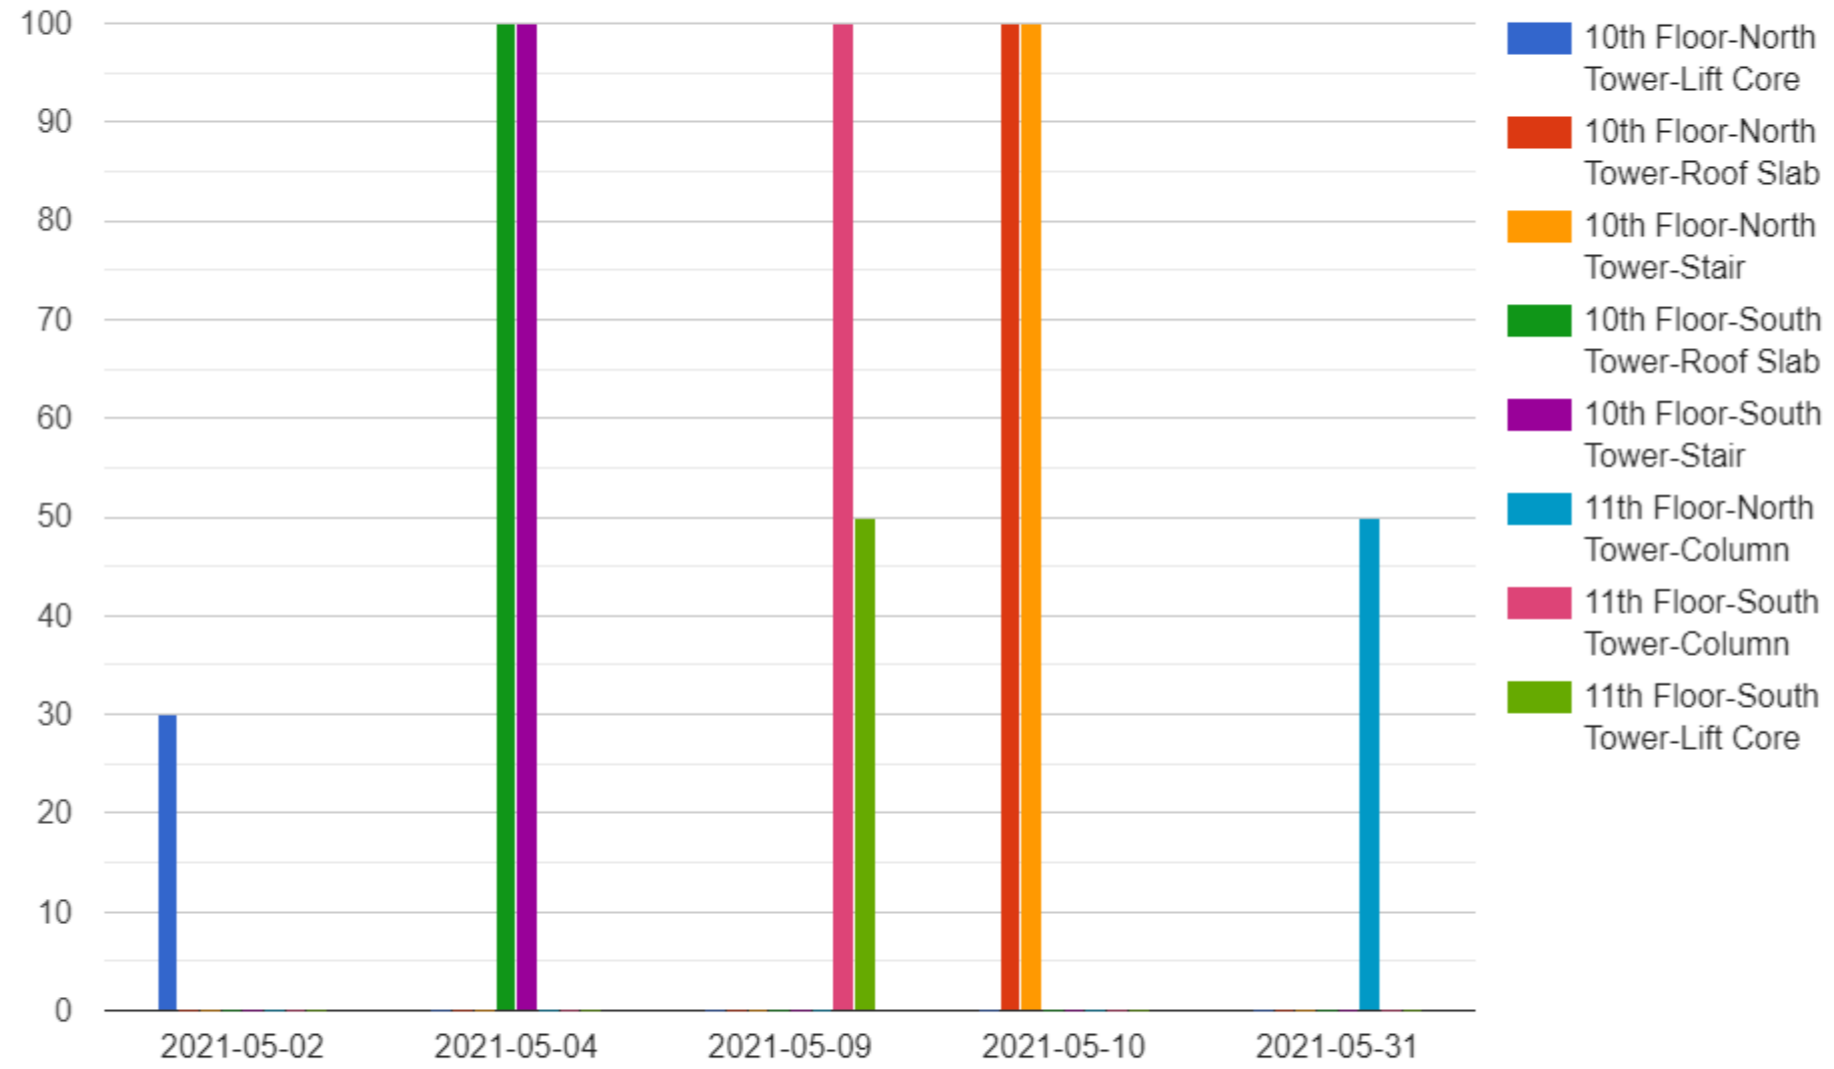

Project:	NBL Tower-Superstucure	Project Code:	42	Date:	2-September-2021
Client:	National Bank Limited	Report	061	Day	Thursday
Contractor:	Cityscape International Ltd.			Climate	Sunny
					28-34C

## Manpower

SN	Description	Nos.
01	Cityscape Staff-NBL	25
02	Elite Force Security-NBL	12
03	Abu Sayed	50
04	Cityscape Civil Worker	10
TOTAL		97

## Progress This Day

WBS	Task	Total Qty	Today Done(%)	Total Done(%)	Start	Finish
12.1.3	11th Floor-South Tower-Stair	2nos	100	100	15-04-21	19-04-21
12.1.4	11th Floor-South Tower-Roof Slab	963m2	100	100	15-04-21	19-04-21

## Site Photographs



South Tower 11th Floor Slab Concreting



South Tower 11th Floor Slab Concreting

Site Description

Site Instruction

Entry by:


Planning Engineer

Generated by:

www.bel3c.com, Developed by: Engr. Md. Sanaul Haque

# **WORK PLAN AND PROGRESS**

# WORK PLAN AND PROGRESS FOR SUPER STRUCTURE OF NBL TWIN TOWER AT KARWANBAZAR, DHAKA

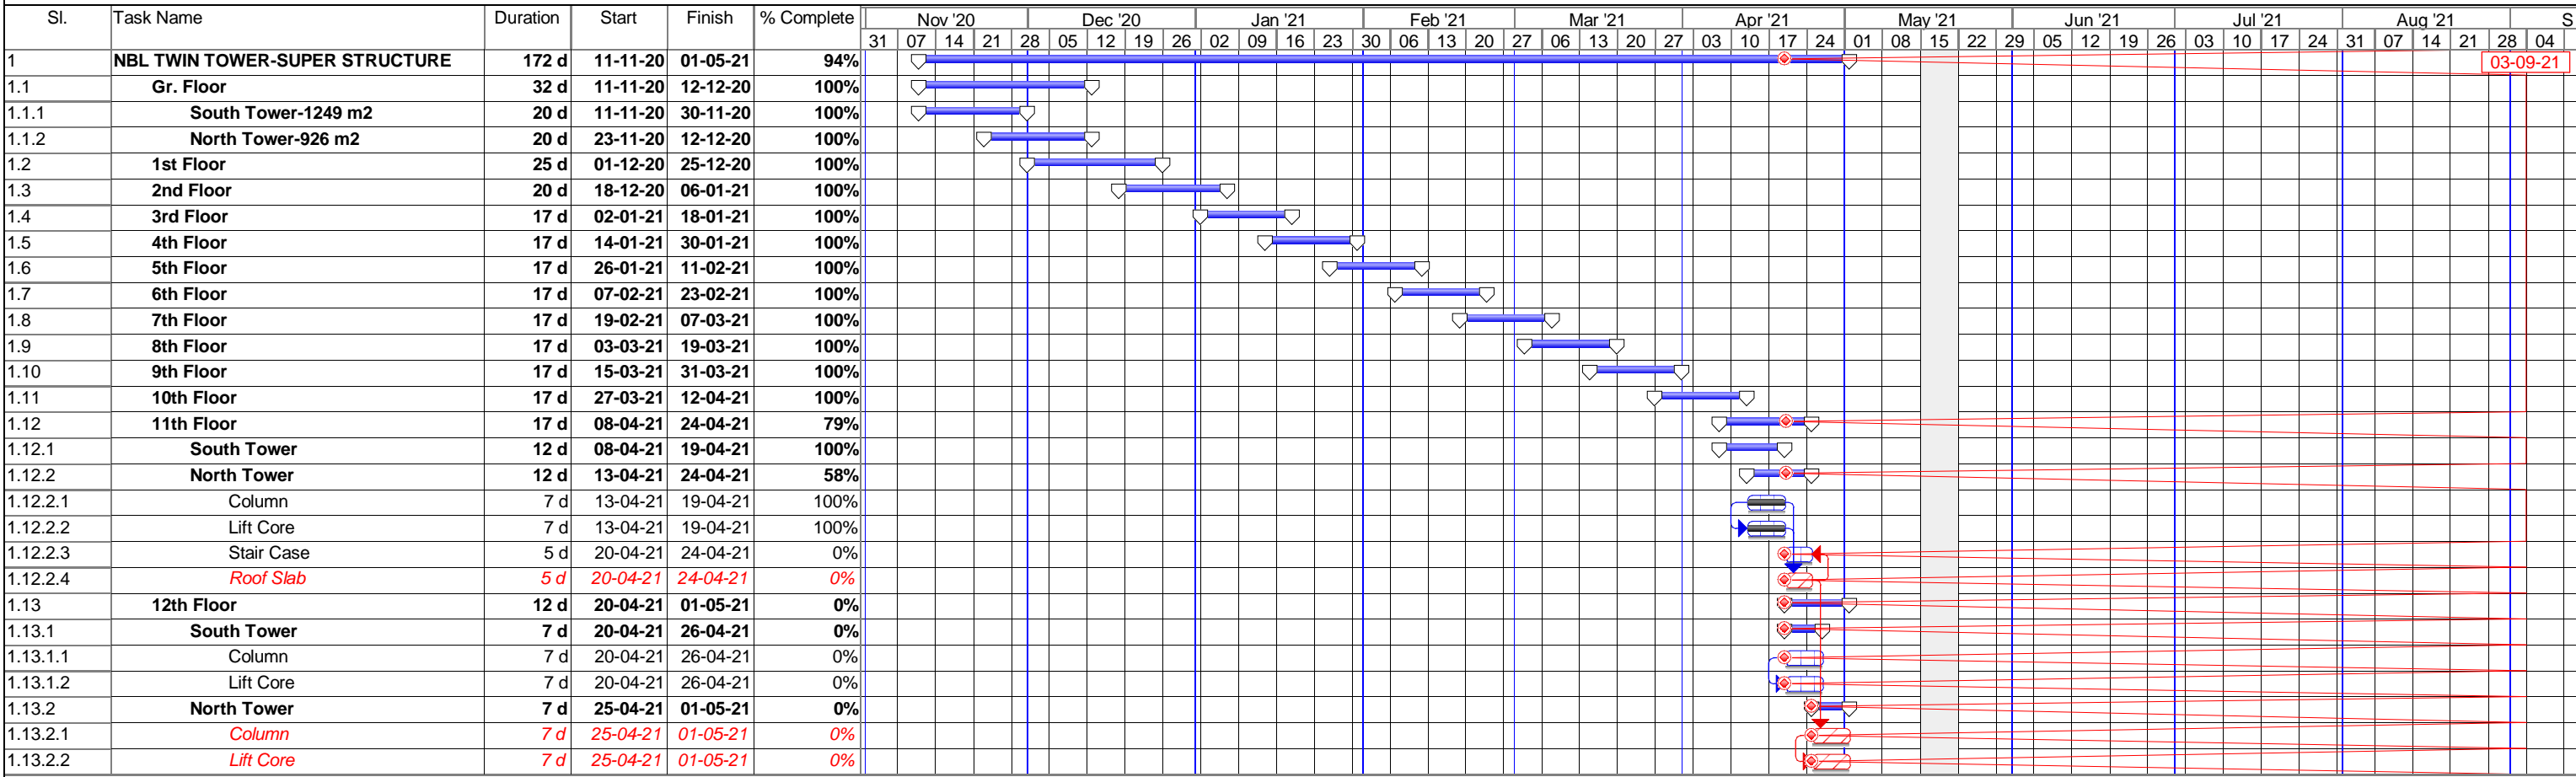

Task		Progress		Rolled Up Task		Rolled Up Progress		Group By Summary	
Critical Task		Summary		Rolled Up Critical Task		Project Summary			
