

**CONSTRUCTION OF RIVER FRONT SATELITE CITY
AT RAYERBAZAR, DHAKA**

RUNNING PROGRESS



11 APRIL 2021

Generated by: Cityscape International Limited

TABLE OF CONTENTS

- TOTAL PROGRESS
- TOTAL MANPOWER CHART
- CUMMULATIVE PROGRESS CHART
- SCHEDULE LEAD-LAG CHART
- LAST MONTH PROGRESS
- LAST MONTH MANPOWER HISTOGRAM
- LAST MONTH PROGRESS CHART
- DAILY PROGRESS REPORT
- WORK PLAN AND PROGRESS
- PROGRESS PHOTO



TOTAL PROGRESS REPORT

From 27-January-2021 to 31-May-2021


Project Code:	56	Name:	River Front Satellite City
Client:	Sikder Group	Contractor:	Cityscape International Ltd.

Total Progress


WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Finish	Lead-Lag(day)
02.01	River-side Walkway-Side Wall	835m	100	07-12-20	04-02-21	05-02-21	-1
02.02	River-side Walkway-Filling	835m	100	10-12-20	07-02-21	05-02-21	2
02.03	River-side Walkway-Soling	5007sqm	100	13-12-20	10-02-21	05-02-21	5
02.04	River-side Walkway-CC	5007sqm	100	16-01-21	13-02-21	05-02-21	8
02.06	River-side Boundary-Bottom Beam	835m	100	07-12-20	04-02-21	01-02-21	3
02.07	River-side Boundary-Bot Column	89nos	100	08-12-20	05-02-21	01-02-21	4
02.08	River-side Boundary-Brick Work	835m	100	10-12-20	07-02-21	01-02-21	6
02.09	River-side Boundary-Top Beam	835m	100	12-12-20	09-02-21	01-02-21	8
02.10	River-side Boundary-Top Column	89nos	100	14-12-20	11-02-21	01-02-21	10
02.11	River-side Boundary-Grill	835m	95	21-12-20	18-02-21	08-02-21	10
02.12	River-side Boundary-Column Capital	89nos	100	21-12-20	18-02-21	01-02-21	17
02.13	River-side Boundary-Bontile Texture	835m	95	28-12-20	25-02-21	03-04-21	-37
02.14	River-side Boundary-Grill Enamel Pa	835m	95	14-02-21	28-02-21	08-03-21	-8
03.03	40 feet Road Levelling and Dressing	886m	18	26-02-21	11-03-21	31-03-21	-20
04.01	12 ft Inner Road-Filling	m	80	20-12-20	12-02-21	28-02-21	-16
04.02	12 Ft Inner Road-Soling	sqm	60	21-12-20	13-02-21	08-02-21	5
04.03	12 ft Inner Road-CC	sqm	60	22-12-20	14-02-21	08-02-21	6
05.01	Outside Plaster-Building-B		10	26-01-21	25-02-21	29-01-21	27
05.06	Outside Plaster-Building-J		60	11-01-21	09-02-21	28-01-21	12
05.10	Outside Plaster-Building-N		2	11-01-21	10-02-21	31-05-21	-110
05.11	Outside Plaster-Building-Q		91	18-01-21	16-02-21	09-05-21	-82
05.12	Outside Plaster-Building-R		95	18-01-21	16-02-21	01-05-21	-74
06.03	Mock-up Flat-Const Joint & Extensn		100	18-01-21	31-01-21	05-02-21	-5

WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Finish	Lead-Lag(day)
06.04.1	Mock-up Flat-Brick Work		100	17-01-21	31-01-21	05-02-21	-5
06.04.2	Mock-up Flat-Plaster		87	07-01-21	10-02-21	25-02-21	-15
06.06.2	Mock-up Flat-Elect Conceal		85	15-01-21	31-01-21	08-02-21	-8
07.04.2	Mosque-Ground Floor Slab	790m2	100	10-03-21	21-03-21	21-03-21	0
07.04.3	Mosque-Basement-Plaster Work		5	10-04-21	09-05-21	14-04-21	25
07.04.4	Mosque-Basement Tile work	790m2		10-04-21	19-04-21	31-05-21	-42
07.04.5	Mosque-Basement-Ancillary Works		30	16-04-21	25-05-21	04-05-21	21
07.05.1	Mosque-Ground Floor-Column		100	22-03-21	02-04-21	28-03-21	5
07.05.2	Mosque-Ground Floor-Roof Slab	790m2	100	03-04-21	09-04-21	06-04-21	3
07.05.3	Mosque-Ground Floor-Stair	6nos	83	22-03-21	15-04-21	11-04-21	4
07.05.4	Mosque-Ground Floor-Ancillary works		30	16-04-21	25-05-21	31-05-21	-6
07.06.1	Mosque- 20ft Connecting Road-Fillin		5	01-04-21	14-04-21	31-03-21	14
07.07.1	Mosque-1st Floor-Column			10-04-21	21-05-21	24-04-21	27
08.1	Landing Station-Excavation		5	22-05-21	04-06-21	22-05-21	13


DAILY MANPOWER

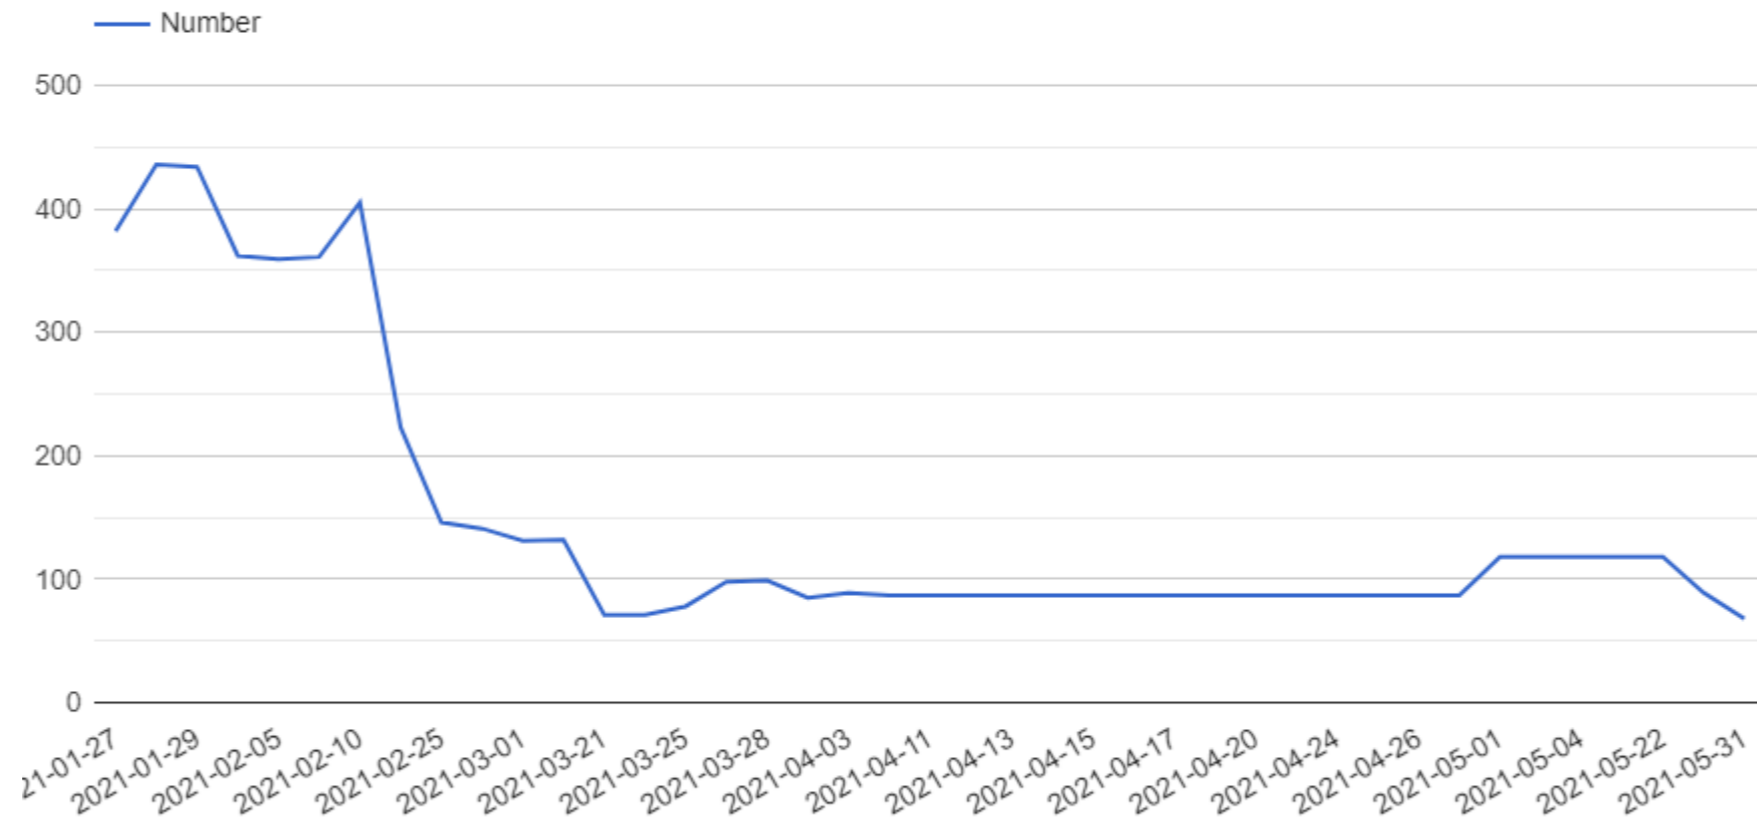

CUMMULATIVE WORK PROGRESS

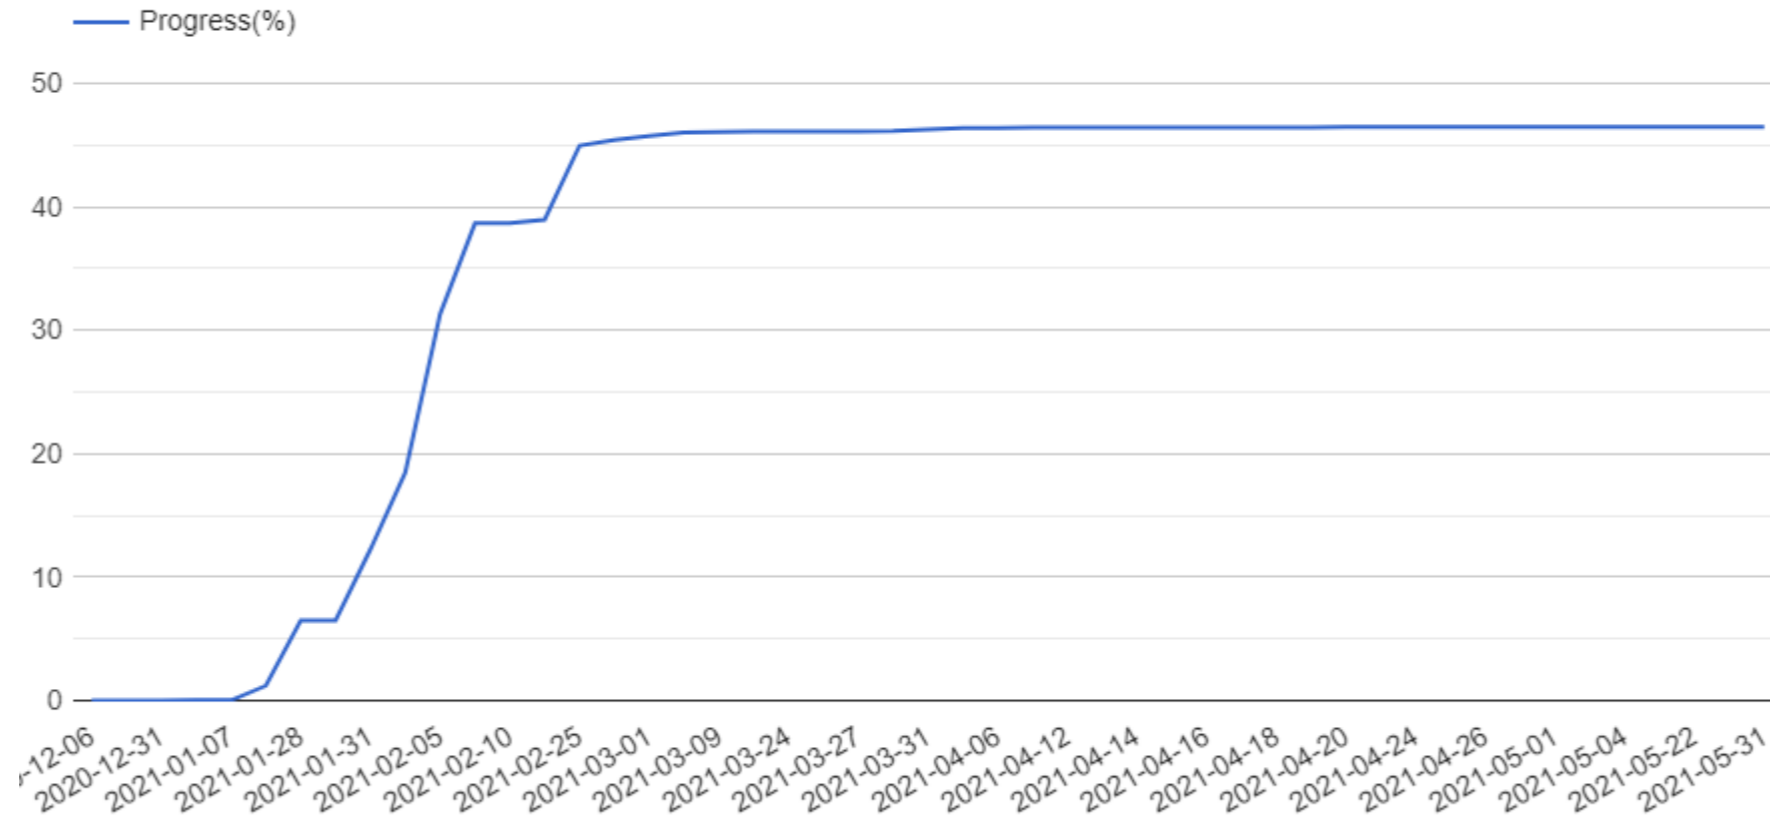

SCHEDULE AHEAD-BEHIND

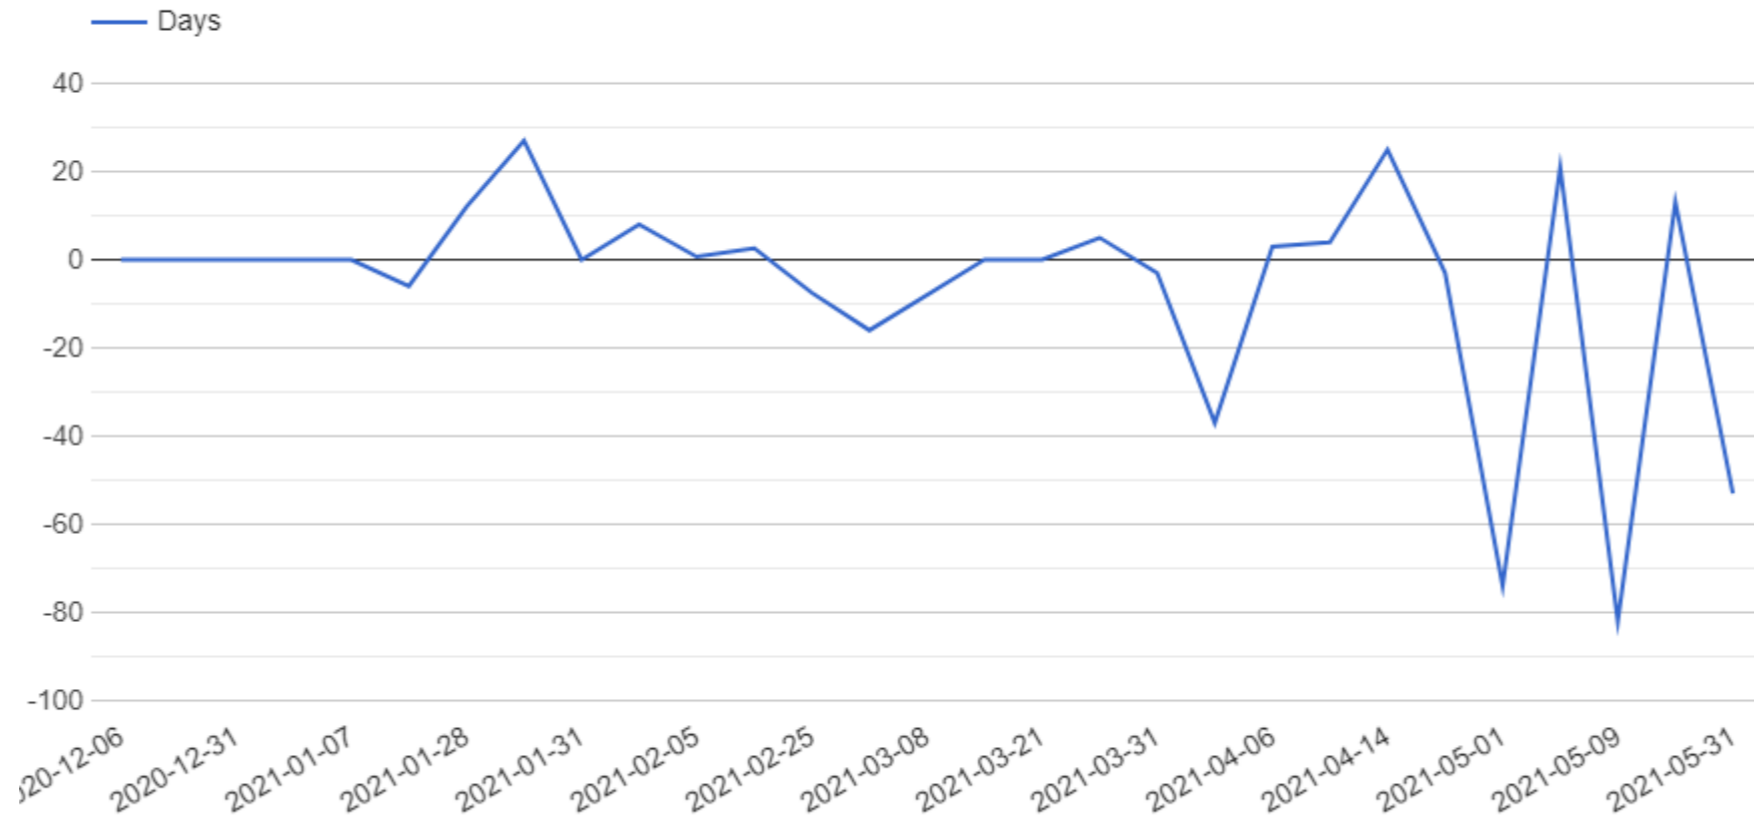

MONTHLY REPORT
DAILY REPORT



MONTHLY PROGRESS REPORT


From 1-March-2021 to 31-March-2021

Project Code:	56	Name:	River Front Satellite City
Client:	Sikder Group	Contractor:	Cityscape International Ltd.


Monthly Progress

WBS	Task	Total Qty	Upto Last Month(%)	This Month(%)	Total Done(%)	Schedule Start	Schedule Finish	Actual Finish
02.13	River-side Boundary-Bontile Texture	835m	83	12	95	28-12-20	25-02-21	31-03-21
02.14	River-side Boundary-Grill Enamel Pa	835m	85	10	95	14-02-21	28-02-21	08-03-21
03.03	40 feet Road Levelling and Dressing	886m	15	3	18	26-02-21	11-03-21	31-03-21
05.10	Outside Plaster-Building-N		80	3	83	11-01-21	10-02-21	27-03-21
05.12	Outside Plaster-Building-R		83	4	87	18-01-21	16-02-21	31-03-21
07.04.2	Mosque-Ground Floor Slab	790m2	0	100	100	10-03-21	21-03-21	21-03-21
07.05.1	Mosque-Ground Floor-Column		0	100	100	22-03-21	02-04-21	28-03-21
07.05.2	Mosque-Ground Floor-Roof Slab	790m2	0	25	25	03-04-21	09-04-21	31-03-21
07.05.3	Mosque-Ground Floor-Stair	6nos	0	15	15	22-03-21	15-04-21	28-03-21
07.07.1	Mosque- 20ft Connecting Road-Fillin		0	5	5	01-04-21	14-04-21	31-03-21

MANPOWER HISTOGRAM

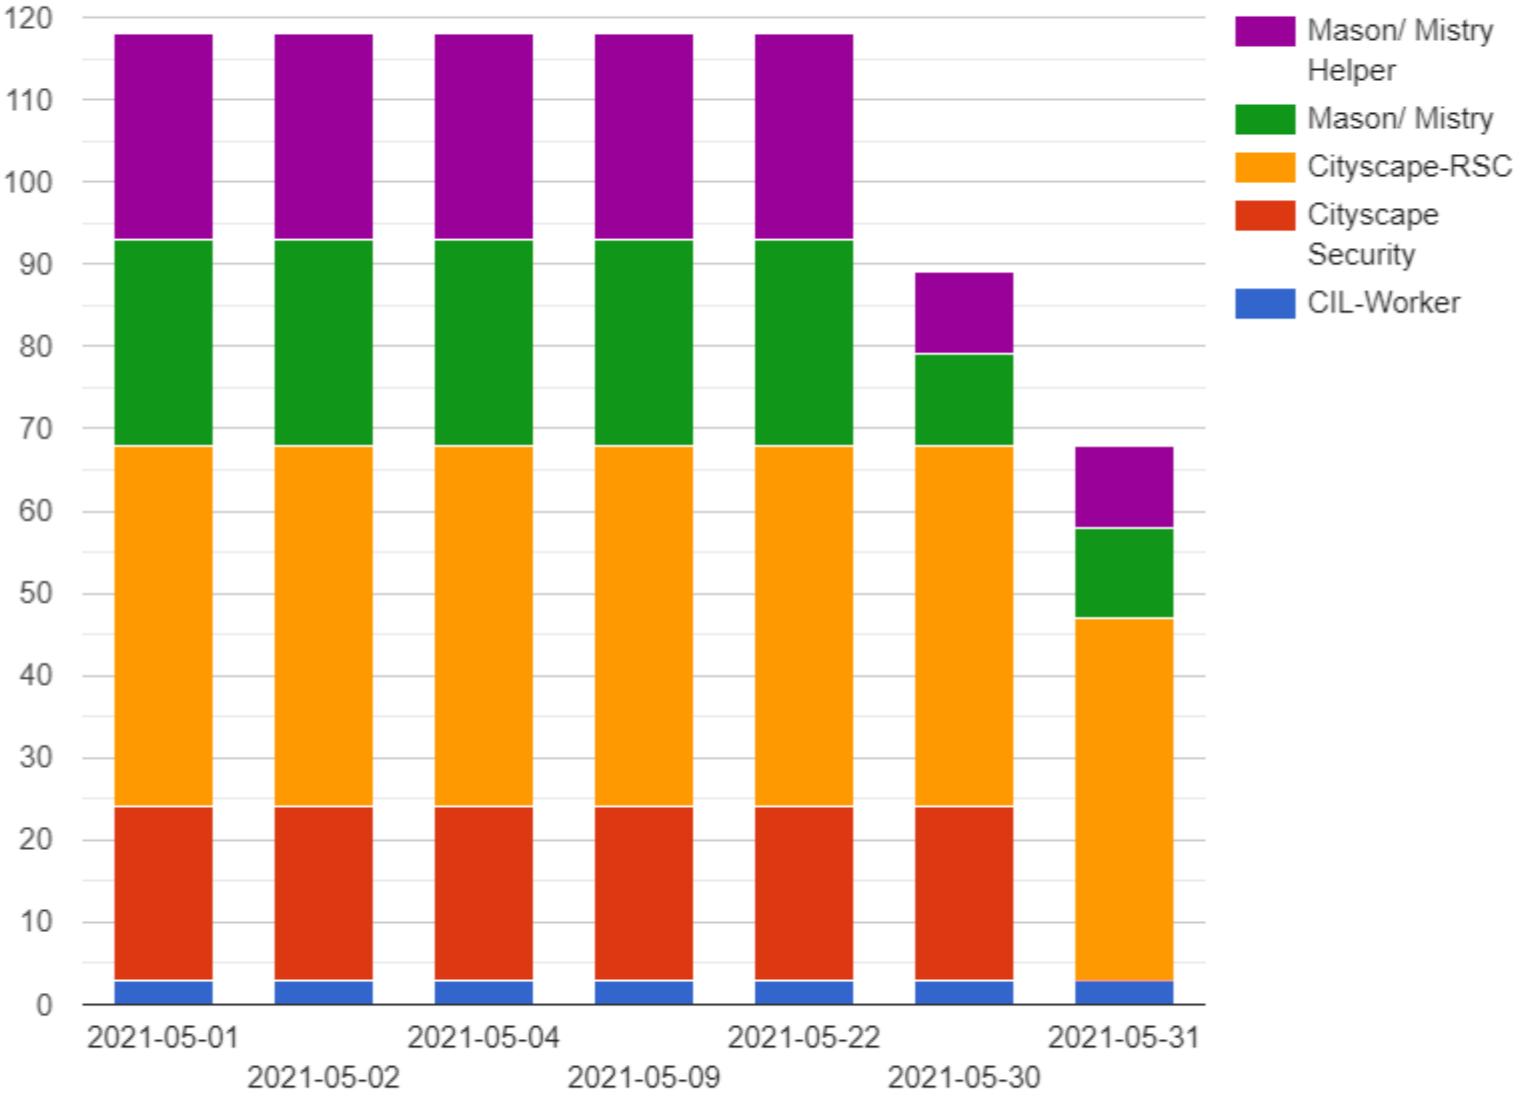

DAILY PROGRESS

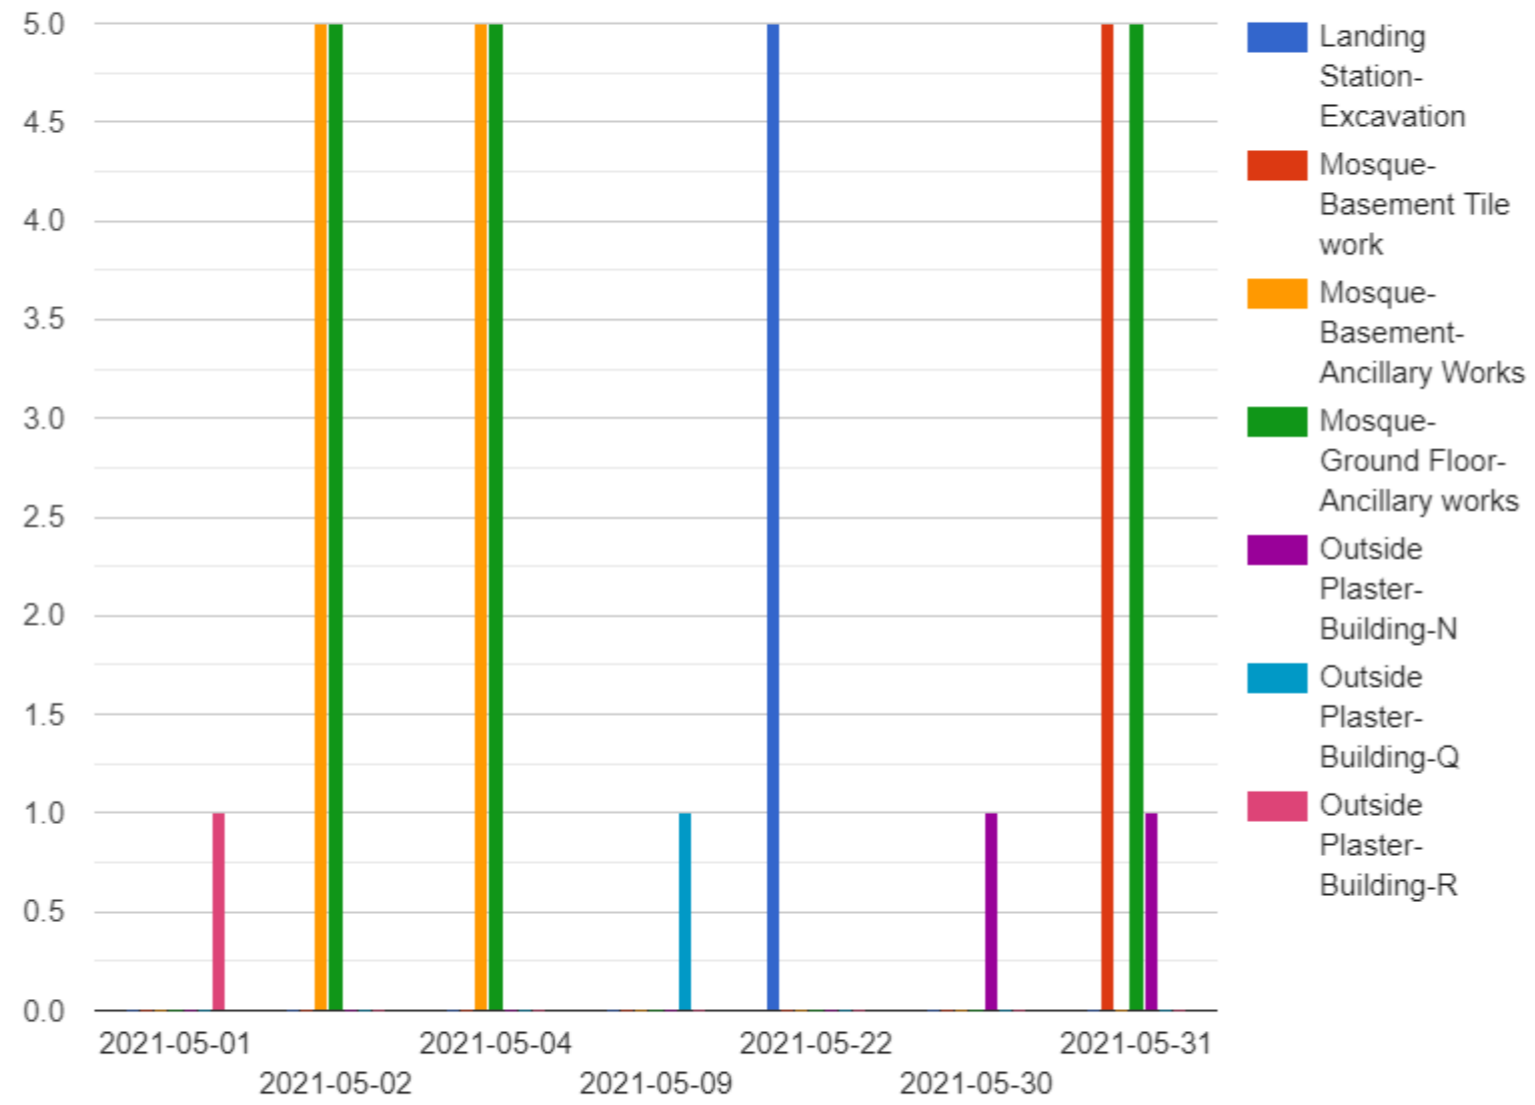

Project:	River Front Satellite City	Project Code:	56	Date:	11-April-2021
Client:	Sikder Group	Report	021	Day	Thu
Contractor:	Cityscape International Ltd.			Climate	Sunny
					27-34C

Manpower

SN	Description	Nos.
01	Cityscape-RSC	24
03	CIL-Worker	3
26	Cityscape Security	10
27	Mason/ Mistry	25
28	Mason/ Mistry Helper	25
TOTAL		87

Progress This Day

WBS	Task	Total Qty	Today Done(%)	Total Done(%)	Start	Finish
07.05.3	Mosque-Ground Floor-Stair	6nos	53	83	22-03-21	15-04-21
07.06.1	Mosque-Basement Tile work	790m2	35	35	10-04-21	19-04-21

Site Photographs



Mosque-Esatside Stair Case



Mosque-Basement Tiles Work

Site Description

Site Instruction

Entry by:


Planning Engineer

Generated by:

www.bel3c.com, Developed by: Engr. Md. Sanaul Haque

WORK PLAN AND PROGRESS

WORK PLAN AND PROGRESS OF RIVER FRONT SATELLITE CITY

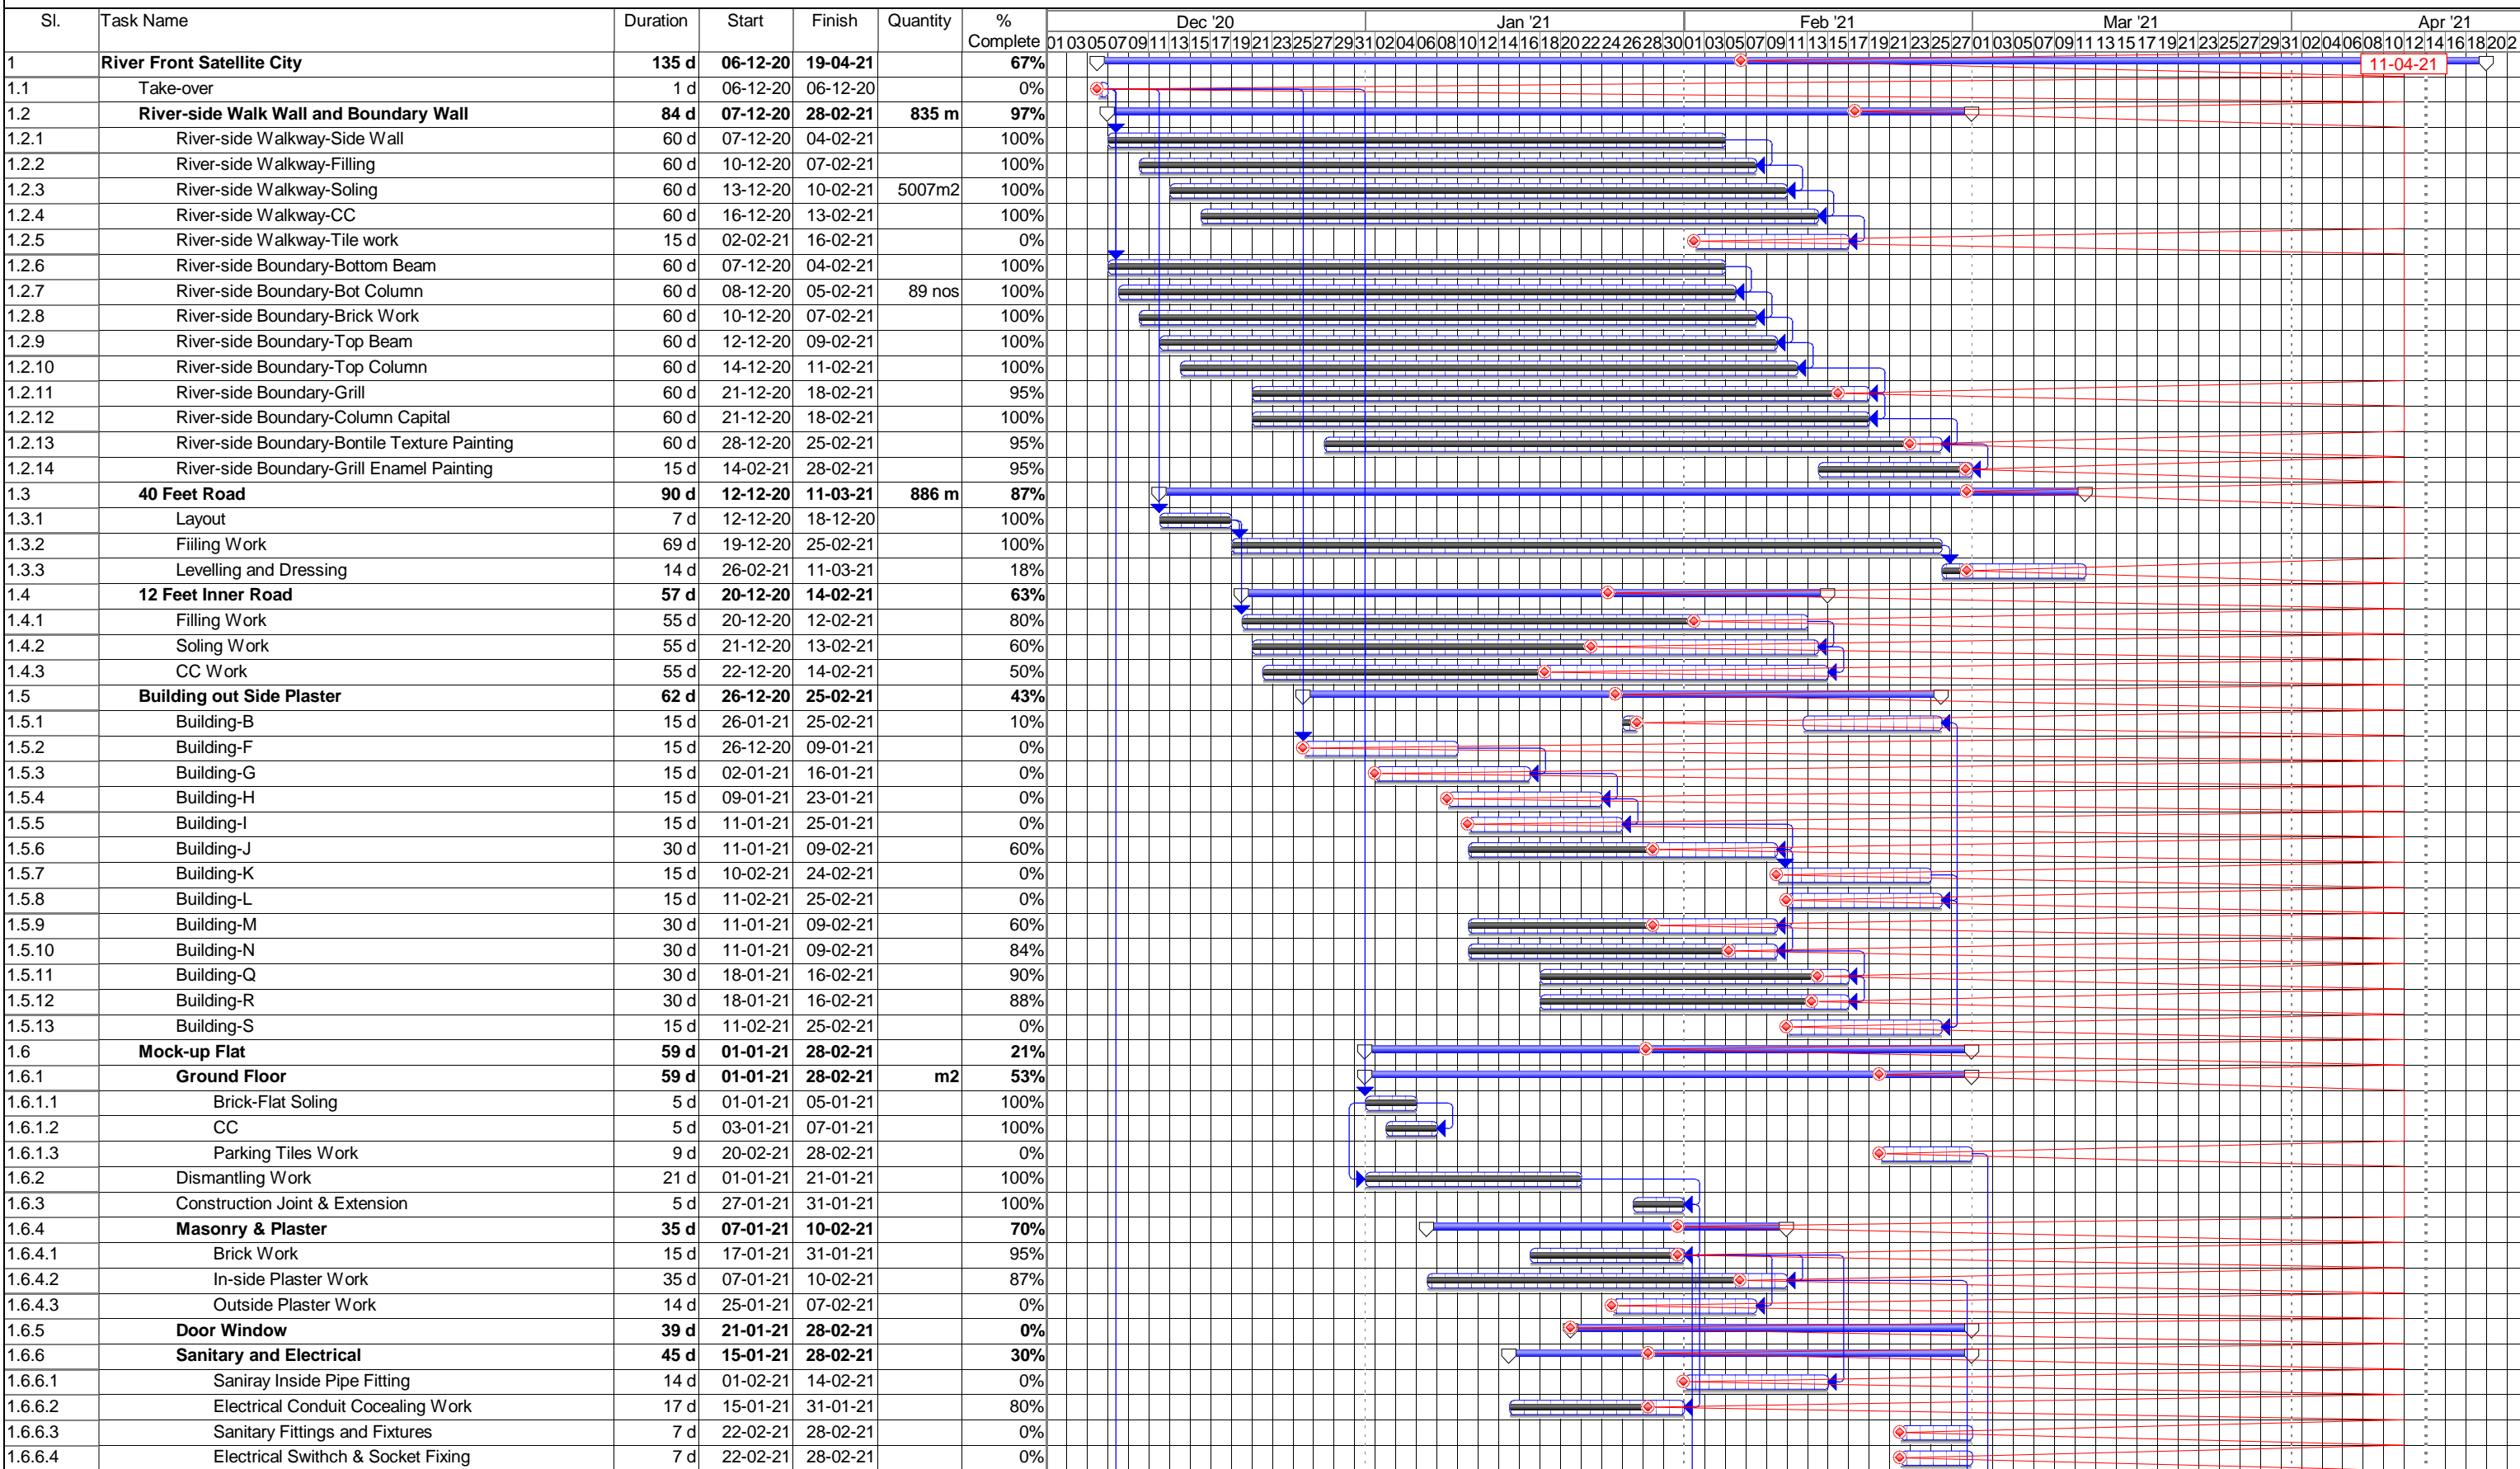

Date: 14-04-21 15.35
Sheet: 1 / 2

Task		Progress		Rolled Up Task		Rolled Up Progress		Group By Summary	
Critical Task		Summary		Rolled Up Critical Task		Project Summary			

WORK PLAN AND PROGRESS OF RIVER FRONT SATELLITE CITY



Sl.	Task Name	Duration	Start	Finish	Quantity	% Complete	Dec '20												Jan '21												Feb '21												Mar '21												Apr '21																																																																							
							01	03	05	07	09	11	13	15	17	19	21	23	25	27	29	31	01	02	04	06	08	10	12	14	16	18	20	22	24	26	28	30	01	03	05	07	09	11	13	15	17	19	21	23	25	27	01	03	05	07	09	11	13	15	17	19	21	23	25	27	29	31	01	02	04	06	08	10	12	14	16	18	20	22	24	26	28	30																																										
1.6.7	Tile Work	38 d	22-01-21	28-02-21		0%																																																													[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]											
1.6.8	Stair Railing	15 d	01-02-21	15-02-21		0%																																																													[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]											
1.6.9	Lime Terracing/ Roof Treatment	15 d	14-02-21	28-02-21		0%																																																													[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]											
1.6.10	Inside Painting	30 d	28-01-21	26-02-21		0%																																																													[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]											
1.6.11	Electro Mechanical Works	22 d	07-02-21	28-02-21		0%																																																													[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]											
1.6.12	Landscaping	20 d	09-02-21	28-02-21		0%																																																													[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]											
1.6.13	Snaging and Finshing Touch	7 d	22-02-21	28-02-21		0%																																																													[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]											
1.6.14	Handover	1 d	28-02-21	28-02-21		0%																																																													[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]											
1.7	New Mosque	134 d	07-12-20	19-04-21		86%	[Progress Bar]																																																												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]											
1.7.1	Pile Work	25 d	07-12-20	31-12-20		100%	[Progress Bar]																																																												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]											
1.7.2	Excavation and Pile Head Breaking	40 d	23-12-20	31-01-21		100%	[Progress Bar]																																																												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]											
1.7.3	Mat Concreting	20 d	20-01-21	08-02-21		100%	[Progress Bar]																																																												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]											
1.7.4	Basement	41 d	09-02-21	21-03-21		100%	[Progress Bar]																																																												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]											
1.7.4.1	Retaining wall, Column, Lift Core, Stair	29 d	09-02-21	09-03-21		100%	[Progress Bar]																																																												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]											
1.7.4.2	Ground Floor Slab	12 d	10-03-21	21-03-21		100%	[Progress Bar]																																																												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]											
1.7.5	Ground Floor	25 d	22-03-21	15-04-21		90%	[Progress Bar]																																																												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]											
1.7.5.1	Column	12 d	22-03-21	02-04-21		100%	[Progress Bar]																																																												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]											
1.7.5.2	Roof Slab	7 d	03-04-21	09-04-21	790 m2	100%	[Progress Bar]																																																												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]											
1.7.5.3	Stair-6 nos	25 d	22-03-21	15-04-21	6 nos	83%	[Progress Bar]																																																												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]											
1.7.6	Finishing Works	10 d	10-04-21	19-04-21		5%	[Progress Bar]																																																												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]											
1.7.6.1	<i>Basement Tiles</i>	<i>10 d</i>	<i>10-04-21</i>	<i>19-04-21</i>		<i>5%</i>	[Progress Bar]																																																												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]											
1.7.7	20 ft Connectrion Road	14 d	01-04-21	14-04-21		5%	[Progress Bar]																																																												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]											
1.7.7.1	Sand Filling	14 d	01-04-21	14-04-21		5%	[Progress Bar]																																																												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]												[Task Bar]											

Task		Progress		Rolled Up Task		Rolled Up Progress		Group By Summary	
Critical Task		Summary		Rolled Up Critical Task		Project Summary			

PROGRESS PHOTO

Site Photographs



Inner Road CC Work on 27-01-21



Scaffolding for Outside Plaster-Buildin on 27-01-21



Building-J outside plastering on 28-01-21



Riverside walkway CC work on 28-01-21



Building- outside plastering on 29-01-21



Scaffolding for outside plastering Build on 29-01-21



Riverside Bontile Rectification & Lighti on 01-02-21



Lanscape Lighting on 01-02-21



Boundary Grill Painting on 05-02-21



Out-side Plaster Work on 05-02-21



Riverside Boundary Fencing on 08-02-21



Building Outside Painting on 08-02-21



40 ft Road Levelling and dressing on 10-02-21



River Side Boundary Fencing on 10-02-21



on 18-02-21



on 18-02-21

Project was closed 11-17 Feb 2021 due to Honourable Z.H. Sikder death



Mock-up-Exterior Sand Stone Fixing on 25-02-21



Electrical Conduit Conesealing on 25-02-21



40 ft Road Dressing and Levelling on 28-02-21



12 ft Road Filling on 28-02-21



40 ft Road Dressing and Levelling on 01-03-21



Building Outside Plastering on 01-03-21



Building Outside Plastering on 08-03-21



Riverside Boundary Fencing on 08-03-21



Breifing instruction before Concreting on 21-03-21



Mosque Ground Floor Slab Concreting on 21-03-21



Cityscape Security Training on 24-03-21



Mosque GF Column 2nd Lift Re-bar Work on 24-03-21



Mosque-GF Column Work on 25-03-21



Mosque-GF-Stair Case Foundation Work on 25-03-21



Mosque 1st Floor Slab Shuttering on 27-03-21



Mosque Ground Floor Stair Concreting on 27-03-21



Mosque 1st Floor Slab Shuttering on 28-03-21



Mosque Ground Floor Stair Concreting on 28-03-21



Mosque-20ft Connecting Road-Filling on 31-03-21



2021/3/31 18:39

Mosque-Night Shift Work on 31-03-21



Mosque 1st Floor Slab Re-bar Work on 03-04-21



Mosque Building in Construction on 03-04-21



Mosque 1st Floor Slab Concreting on 06-04-21



Mosque 1st Floor Slab Concreting on 06-04-21



Mosque-Esatside Stair Case on 11-04-21



Mosque-Basement Tiles Work on 11-04-21



on 12-04-21



Mosque-Basement-Tile Work on 12-04-21



Mosque under Construction on 13-04-21



Mosque-Basement-Tile Work on 13-04-21



Mosque-Basment Plaster Work on 14-04-21



Mosque-Ground Floor Ancillary Works on 14-04-21



Out-side Plastering on 15-04-21



Mosque in Construction on 15-04-21



Mosque-Basement-Tile Work on 16-04-21



Mosque-Basement-Anclary Work on 16-04-21



Out-side Plastering on 17-04-21



Mosque-Basement-Ancliary Work on 17-04-21



Out-side Plastering on 19-04-21



Mosque-1st Floor Column Re-bar Work on 19-04-21



Out-side Plastering on 20-04-21



Out-side Plaster Work on 20-04-21



Out-side Plastering on 22-04-21



Mosque-Ground Floor-Roof Slab de-shutter on 22-04-21



Mosque-Gr.Floor Roof De-shuttering on 24-04-21



Mosque Building in Construction on 24-04-21



Mosque-Stair Case on 25-04-21



1st Floor Roof-De-shuttering on 25-04-21



Mosque-1st Floor-Column Shuttering on 26-04-21



Mosque-Basement-Anclary Work on 26-04-21



Out-side Plastering on 28-04-21



Drop Wall Shuttering on 28-04-21



Drop Wall Shuttering on 01-05-21



Out-side Plaster Work on 01-05-21



Out-side Plastering on 02-05-21



Mosque-Gr./1st Floor-Ancillary Works on 02-05-21



Mosque-Gr/1st Floor-Anciliary works on 04-05-21



Out-side Plaster Work on 04-05-21



Bulding-Q-Out-side Plastering on 09-05-21



Bulding-Q-Out-side Plastering on 09-05-21



Landing Station-Excavation on 22-05-21



Landing Station-Excavation on 22-05-21

Project Closed 10-21 May due to Eid-ul Fitre Vacation



on 30-05-21



on 30-05-21



Mosque-Basement-Tile Work on 31-05-21



Mosque-Ground Floor-Ancillary Works on 31-05-21
