



MONTHLY PROGRESS REPORT

From 1-February-2021 to 28-February-2021

Project Code:	32	Name:	Sikder Center
Client:	Multiplex Holding Ltd.	Contractor:	Cityscape International Ltd.

Monthly Progress

WBS	Task	Total Qty	Upto Last Month(%)	This Month(%)	Total Done(%)	Schedule Start	Schedule Finish	Actual Finish
04	5-7F-Patent Stone Floor		0	100	100	05-12-20	12-12-20	28-02-21
15	15-19F-Duct Wall Plaster		0	100	100	02-12-20	07-12-20	28-02-21
21	4-12F-Tolilet Counter Slab RCC		0	100	100	05-12-20	15-12-20	05-02-21
24	4-8F-Est Plaster-Partial North		40	60	100	08-12-20	15-12-20	10-02-21
26	13F-Safety Tray Removing		80	20	100	02-12-20	15-12-20	01-02-21
27	7F-Safety Tray Removing		40	25	65	12-12-20	15-12-20	28-02-21

Site Photographs



Toolbox Meeting-Work at Height on 01-02-21

Site Description

Site Instruction



13F-External Safety Tray Removing on 01-02-21



Front Side Opening Soon on 05-02-21

Site Description

Site Instruction




Round Stair Skirting Plaster finished fo on 05-02-21



Duct upstand Blockwork on 10-02-21

Site Description

Site Instruction

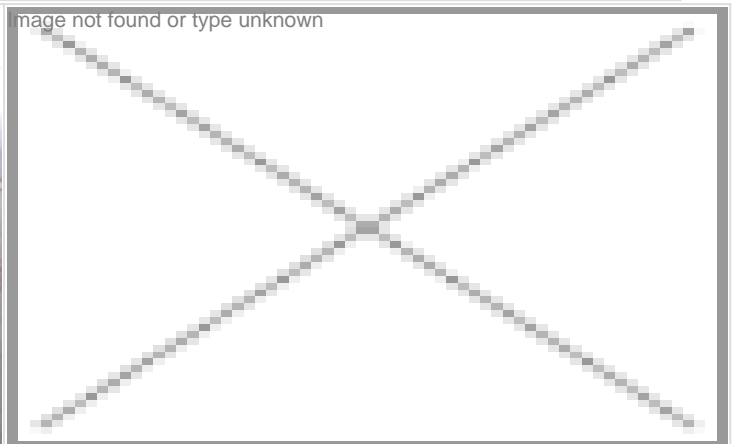

11F Toilet Conterslab Shutter Level Mark on 10-02-21



Rubish shifting to BTT, Purbachal on 28-02-21

Toolbox meeting-Electrical Hazard on 28-02-21

Site Desription	
Site Instruction	
Entry by:	Generated by:
Planning Engieer	www.bel3c.com, Developed by: Engr. Md. Sanaul Haque
