

WEEKLY PROJECT REPORT-035



Picture Taken : 16 May 2012

AS ON 16 MAY 2012

PROJECT SUMMARY AS ON: 16 MAY 2012

- Program is 70 days delayed from master program as on 16th May 2012. Still delay time is increasing and 7 days more lag in 8th floor roof slab casting. But it should be controlled.
- Still no signature by MEP in Work Inspection Request (WIR) before slab casting.
- Manpower is slightly increased as before.
- Tool Box Meeting (Safety Meeting) with picture, Safety Award picture and Safety violation notice are attached.

WEEKLY CHECK-LIST FOR **PROGRAM** AS ON: 16-05-2012



Name of Sub-Contractor:	Sohel Enterprise
--------------------------------	------------------

WBS					
Task Name	9th floor roof slab casting				
Schedule Finish	02/03/2012	Actual Finish:	11/05/2012	Time Lag:	70
Causes of Delay					

WBS					
Task Name	9th floor roof slab and beam shuttering complete				
Actual Start		Actual Finish:	10/05/2012	Time Lag:	
Causes of Delay					

WBS					
Task Name					
Actual Start		Actual Finish:		Time Lead/Lag:	
Causes of Delay					

WBS					
Task Name					
Actual Start		Actual Finish:		Time Lead/Lag:	
Causes of Delay					

WBS					
Task Name					
Actual Start		Actual Finish:		Time Lead/Lag:	
Causes of Delay					

Remarks: (Penalty/ Award) to be filled by Project Incharge

Suuggestion/ Advice:

9th floor roof slab casting is 70 days delayed from master program which is 7 days more delay than previous slab.

 Consultant


 Chief Engineer

Project Incharge

Chief Engineer

Director

Delay of Roof Slab Casting

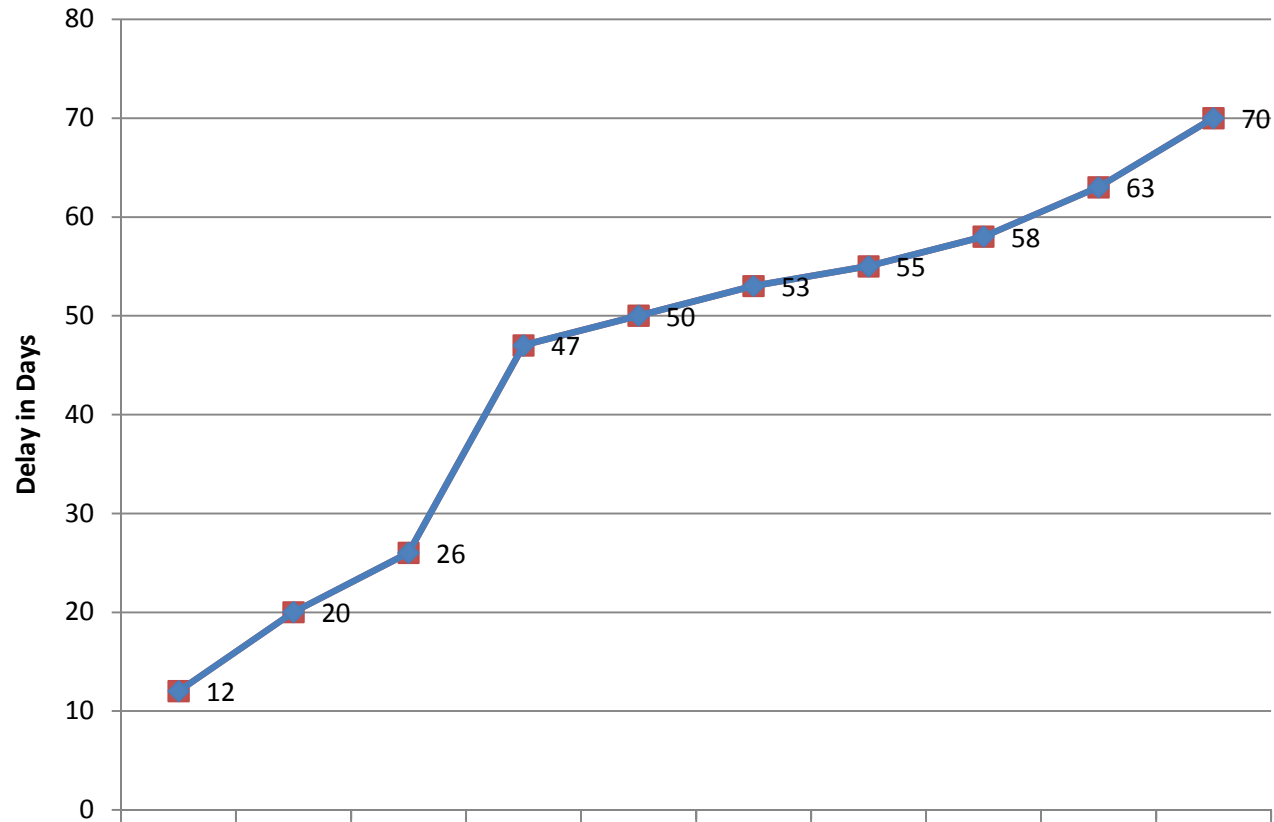

Actual Finish

Schedule Finish

29/08/11	02/10/11	28/10/11	09/12/11	07/01/12	31/01/12	24/02/12	18/03/12	13/04/12	11/05/12
17/8/11	12/9/11	2/10/11	23/10/11	18/11/11	9/12/11	31/12/11	20/1/12	10/2/12	2/3/12
Ground Floor	1st Floor	2nd Floor	3rd Floor	4th Floor	5th Floor	6th Floor	7th Floor	8th Floor	9th Floor

Ekushey Bhaban-Superstructure-Progress

Sl.	Task Name	Duration	Start	Finish	Actual Finish	% Compl	Mar '12					Apr '12				May '12									
							12/02	19/02	26/02	04/03	11/03	18/03	25/03	01/04	08/04	15/04	22/04	29/04	06/05	13/05	20/05				
1	Ekushey Bhaban	442 d	28/07/11	18/11/12	NA	5%	16/05/12																		
1.1	Superstructure	300 d	28/07/11	14/06/12	NA	70%																			
1.1.1	Ground Floor	20 d	28/07/11	17/08/11	29/08/11	100%																			
1.1.2	1st Floor	20 d	18/08/11	12/09/11	02/10/11	100%																			
1.1.3	2nd Floor	20 d	13/09/11	02/10/11	28/10/11	100%																			
1.1.4	3rd Floor	20 d	03/10/11	23/10/11	09/12/11	100%																			
1.1.5	4th Floor	20 d	24/10/11	18/11/11	07/01/12	100%																			
1.1.6	5th Floor	20 d	19/11/11	09/12/11	31/01/12	100%																			
1.1.7	6th Floor	20 d	10/12/11	31/12/11	24/02/12	100%																			
1.1.8	7th Floor	20 d	01/01/12	20/01/12	18/03/12	100%																			
1.1.9	8th Floor	20 d	21/01/12	10/02/12	18/04/12	100%																			
1.1.10	9th Floor	20 d	11/02/12	02/03/12	11/05/12	100%																			
1.1.10.1	Layout Work	1 d	11/02/12	11/02/12	NA	100%																			
1.1.10.2	Column (17 nos): Lift-1	4 d	12/02/12	15/02/12	NA	100%																			
1.1.10.3	Column (17 nos): Lift-2	4 d	16/02/12	19/02/12	NA	100%																			
1.1.10.4	Lift Core: Lift-1	5 d	12/02/12	16/02/12	NA	100%																			
1.1.10.5	Lift Core: Lift-2	4 d	17/02/12	20/02/12	NA	100%																			
1.1.10.6	Stair Case (2 nos)-Flight-1	8 d	13/02/12	20/02/12	NA	100%																			
1.1.10.7	Stair Case (2 nos)-Flight-2	8 d	24/02/12	02/03/12	NA	100%																			
1.1.10.8	Roof Slab	10 d	22/02/12	02/03/12	11/05/12	100%																			
1.1.10.8.1	Formwork	5 d	22/02/12	26/02/12	NA	100%																			
1.1.10.8.2	Re-bar	3 d	27/02/12	29/02/12	NA	100%																			
1.1.10.8.3	MEP Work	2 d	29/02/12	01/03/12	NA	100%																			
1.1.10.8.4	Inspection	1 d	01/03/12	01/03/12	NA	100%																			
1.1.10.8.5	Concrete	1 d	02/03/12	02/03/12	11/05/12	100%																			
1.1.11	10th Floor	20 d	03/03/12	23/03/12	NA	18%																			
1.1.11.1	Layout Work	1 d	03/03/12	03/03/12	NA	100%																			
1.1.11.2	Column (17 nos): Lift-1	4 d	04/03/12	07/03/12	NA	100%																			
1.1.11.2.1	Re-bar	1 d	04/03/12	04/03/12	NA	100%																			
1.1.11.2.2	Formwork	2 d	05/03/12	06/03/12	NA	100%																			
1.1.11.2.3	Concrete	1 d	07/03/12	07/03/12	NA	100%																			
1.1.11.3	Column (17 nos): Lift-2	4 d	08/03/12	11/03/12	NA	0%																			
1.1.11.3.1	Re-bar	1 d	08/03/12	08/03/12	NA	0%																			
1.1.11.3.2	Formwork	2 d	09/03/12	10/03/12	NA	0%																			
1.1.11.3.3	Concrete	1 d	11/03/12	11/03/12	NA	0%																			
1.1.11.4	Lift Core: Lift-1	5 d	04/03/12	08/03/12	NA	70%																			
1.1.11.4.1	Re-bar	2 d	04/03/12	05/03/12	NA	100%																			
1.1.11.4.2	Formwork	2 d	06/03/12	07/03/12	NA	50%																			
1.1.11.4.3	Concrete	1 d	08/03/12	08/03/12	NA	50%																			
1.1.11.5	Lift Core: Lift-2	4 d	09/03/12	12/03/12	NA	0%																			

Project: Ekushey Bhaban - Superstruc Date: 02/08/12	Task Critical Task Progress	Summary Rolled Up Task Rolled Up Critical Task	Rolled Up Progress Project Summary Group By Summary	
--	-----------------------------------	--	---	----------

WEEEKLY CHECK-LIST FOR **QUALITY** AS ON: 16-05-2012



Name of Sub-contractor:	Sohel Enterprise
-------------------------	------------------

Remarks on Shuttering: (Attach Photograph) to be filled by Project Incharge

Remarks on Re-bar Work: (Attach Photograph) to be filled by Project Incharge

Remarks on Concreting : (Attach Photograph) to be filled by Project Incharge

Suggestion/ Advice:

WIR attached. But MEP did not sign it.

Consultant

Chief Engineer

Project Incharge

Chief Engineer

Director

R & D 0.0, Date of Issue : Nov, 2010 Doc No. CIL R & D WIR 002	CITYSCAPE INTERNATIONAL LIMITED	
--	--	--

WORK INSPECTION REQUEST (To submit by Contractor 48 hours before Concreting)		
Description of Work : <u>10th floor (Beam + Slab) casting</u>		
Location/ Grid : <u>A to E and 01 to 05</u>	Level : <u>+104</u>	Date of Concreting : <u>11/05/12</u>
(A Drawing with Marking/ Higlighting must be submitted)		Time of Concreting : <u>06:00 AM</u>
Submitted By:		
Company : <u>Rasem Tech Limited Sokel Enterprise</u>		Signature :
Name : <u>Mrs. Forluz Rahaman</u>		
Designation : <u>Cont'</u>	Date : <u>10/05/12</u>	Time :

WORK INSPECTION REPORT		
Reienforcement <input checked="" type="checkbox"/> OK	Formwork <input checked="" type="checkbox"/> OK	Proping/Supporting <input checked="" type="checkbox"/> OK
Comments :		
Inspected By		
Company : <u>Cityscape International Limited</u>		Signature :
Name : <u>MD. Mohiuddin</u>		
Designation : <u>Site Engineer</u>	Date :	Time : <u>8:40 pm</u>

MEP CLEARANCE		
Not Applicable <input type="checkbox"/>	Completed <input type="checkbox"/>	Not Completed <input type="checkbox"/>
Clearanced By		
Company : <u>Cityscape International Limited</u>		Signature :
Name :		
Designation :	Date :	Time :

APPROVAL FOR CONCRETING		
Comments : <u>Check Rebar spacing / Leveling clean</u>		
Approved <input type="checkbox"/>	Approved with Comments <input checked="" type="checkbox"/>	Not Approved <input type="checkbox"/>
Inspected By		
Company : <u>Cityscape International Limited</u>		Signature :
Name : <u>[Signature]</u>		
Designation : <u>CE</u>	Date : <u>[Signature]</u>	Time : <u>[Signature]</u>

WEEKLY CHECK-LIST FOR **SAFETY** AS ON: 16-05-2012



Name of Sub-Contractor:	Sohel enterprise.
--------------------------------	-------------------

List of Safety Materials issued:

Safety Shoe	145	pairs
Helmet	223	nos.
T-shirt	263	nos.

Inducution:

Total Labour:		Inducted:	113			
Tool Box Meeting (Weekly Safety Meeting) no.:					Date:	

Safety Violation: (Attach Photograph)

Warning	No. of Persons
1st Warning :	12
2nd Warning with Fine:	3
Termination:	

Safety Award: (Attach Photograph)

Induction ID:		Trade	Cleaner
Name:			

Accidents/ Injury:

--

House Keeping

--

Remarks: to be filled by Project Incharge

--

Suggestion/ Advice:

Tool Box Meeting notice with picture, Safety Award picture and Safety vioalation notice are attached.	

	Consultant

	Chief Engineer

Project Incharge

Chief Engineer

Director

তারিখ: এপ্রিল ২৯, ২০১২

প্রতি

সোহেল এন্টারপ্রাইজ

স্বাধিকারী: মোঃ আব্দুর রহমান

বিষয়: সেফটি নিয়ম ভঙ্গ করা প্রসঙ্গে

জনাব,

অত্যন্ত দুঃখের সাথে জানানো যাচ্ছে যে, আপনার কর্মচারী প্রায়শ সেফটি নিয়ম ভঙ্গ করে চলছে। আজ একজন হেলমেট এর বেল্ট না পড়ে কাজ করার জন্য তা উপর থেকে নীচে পড়ে যায়। এরকম কাজের জন্য কোন ক্ষয়ক্ষতি হলে তার দায়িত্ব আপনাকে নিতে হবে।

এর পর থেকে কোন কর্মচারী নিয়ম ভঙ্গ করলে তাকে প্রোজেক্ট থেকে বের করে দিতে হবে।

নিবেদক

মীর রুহুল আমিন

সিটিস্কেপ ইন্টারন্যাশনাল লিমিটেড

একুশে ভবন



CITYSCAPE INTERNATIONAL LIMITED

Gulshan Point (5th Floor), 7/A Gulshan South Avenue, Gulshan-1, Dhaka-1212
www.cityscapebd.com ; Phone: 88029881867-8

Date: May 02, 2012

Ref:

WEEKLY SAFETY (TOOL BOX) MEETING

With a view to build awareness and effectiveness on Health, Safety and Environment issue among workers and staff, management is arranging a weekly safety (tool box) meeting. Detail of the program is given below:

Date	Time	Venue
May 03, 2012	2.00 pm	Construction Site (Assembly Point)
Discussion:	Safe Work Practice and safety award program	
Resource Person	Eng. Mir Ruhul Amin (Health & Safety Engineer- Electro Mechanical) Engr. Mohiuddin (Site Engineer)	

All nominated members are hereby requested to attend the session in scheduled time.

HSE Engineer

Manager R&D

Copy to:

1. Managing Director (For kind information only)
2. Director, Business Operation (For kind information only)
3. Chief Engineer
4. Eng. Mohiuddin (Site Engineer)



CITYSCAPE INTERNATIONAL LIMITED

Gulshan Point (5th Floor), 7/A Gulshan South Avenue, Gulshan-1, Dhaka-1212
www.cityscapebd.com ; Phone: 88029881867-8

Weekly Safety (Tool Box) Meeting

Venue: Ekushey Bhaban

Date: May 3, 2012

Time: 2.30 pm

Resource Person: Eng. Mir Ruhul Amin (HSE Engr.)



Safety award



Tool Box Meeting

WEEKLY CHECK-LIST FOR **MANPOWER** AS ON: 16-05-2012



Name of Sub-Contractor:	Sohel Enterprise
--------------------------------	------------------

Shuttering Work:

Manpower	Required No.	Present No.	Remarks
Shutter Mistry		124	
Shutter Helper		120	

Re-bar Work:

Manpower	Required No.	Present No.	Remarks
Re-bar Fabricator		28	
Helper		28	

Concrete Work:

Manpower	Required No.	Present No.	Remarks
Mason		6	
Labour		7	

Housekeeping

Manpower	Required No.	Present No.	Remarks
Labour		28	

Over All Remarks by Project Incharge

Concrete volume =118.5 m3

Suggestion/ Advice

Manpower is slightly increased than before. Manpower Histogram attached.

Consultant

Chief Engineer

Project Incharge

Chief Engineer

Director

MANPOWER HISTOGRAM

