

# Ekushey Bhaban Program-Progress (Ver-3.0)

Sl.	Task Name	Baseline Finish	Duration	Start	Finish	% Complete	Jan '11					Feb '11							
							01/01	08/01	15/01	22/01	29/01	05/02	12/02	19/02	26/02				
1	<b>EKUSHEY BHABAN</b>	12/09/12	927.86 d	25/01/10	19/09/12	18%													
1.1	<b>PRELIMINARIES</b>	21/08/12	911.86 d	25/01/10	28/08/12	87%													
1.1.1	MOBILIZATION-1-TEMPORARY OFFICE-SH	16/04/10	82 d	25/01/10	16/04/10	100%													
1.1.2	MOBILIZATION-2 -INFRASTRUCTURE	25/08/10	15 d	11/08/10	25/08/10	100%													
1.1.3	MOBILIZATION-3-GENERATOR & TOWER C	30/08/10	33 d	29/07/10	30/08/10	100%													
1.1.4	PREPARATION FOR STRUCTURAL CONST	31/12/10	115 d	21/08/10	28/12/10	100%													
1.1.5	MOBILIZATION-4-TOWER CRANE	25/10/11	32 d	28/09/11	30/10/11	0%													
1.1.6	MOBILIZATION-5-LIFTING HOIST	24/05/12	7 d	22/05/12	29/05/12	0%													
1.1.7	DEMOBILIZATION	21/08/12	78 d	07/06/12	28/08/12	0%													
1.2	<b>SUB-STRUCTURE</b>	13/05/11	380.86 d	18/04/10	18/05/11	62%													
1.2.1	<b>PART-1</b>	15/08/10	120 d	18/04/10	15/08/10	100%													
1.2.2	<b>PART-2</b>	12/05/11	220.86 d	02/10/10	18/05/11	54%													
1.2.2.1	<b>EXCAVATION</b>	31/12/10	57 d	02/10/10	05/12/10	100%													
1.2.2.2	<b>Mat Foundation</b>	07/02/11	39.17 d	03/11/10	20/12/10	100%													
1.2.2.3	<b>BASEMENT-3</b>	24/03/11	50.69 d	20/12/10	08/02/11	55%													
1.2.2.3.1	<b>LIFT-1</b>	03/03/11	39.69 d	20/12/10	28/01/11	83%													
1.2.2.3.1.1	<b>Retaining Wall</b>	23/02/11	34 d	20/12/10	23/01/11	98%													
1.2.2.3.1.1.1	Brick Wall	09/02/11	15 d	20/12/10	04/01/11	100%													
1.2.2.3.1.1.2	Plaster	10/02/11	1 d	03/01/11	04/01/11	100%													
1.2.2.3.1.1.3	Water Proofing	17/02/11	3 d	04/01/11	07/01/11	98%													
1.2.2.3.1.1.4	Re-bar Work	20/02/11	6 d	07/01/11	13/01/11	98%													
1.2.2.3.1.1.5	Form Work	21/02/11	5 d	13/01/11	18/01/11	98%													
1.2.2.3.1.1.6	Concreting	22/02/11	2 d	19/01/11	21/01/11	98%													
1.2.2.3.1.1.7	De-shuttering	23/02/11	1 d	22/01/11	23/01/11	70%													
1.2.2.3.1.2	<b>Water Reservoir</b>	17/02/11	14 d	11/01/11	24/01/11	90%													
1.2.2.3.1.2.1	<b>Vertical Wall</b>	13/02/11	11 d	11/01/11	21/01/11	100%													
1.2.2.3.1.2.1.1	Re-bar Work	10/02/11	3 d	11/01/11	13/01/11	100%													
1.2.2.3.1.2.1.2	Form Work	11/02/11	3 d	14/01/11	16/01/11	100%													
1.2.2.3.1.2.1.3	Concrete	12/02/11	3 d	17/01/11	19/01/11	100%													
1.2.2.3.1.2.1.4	De Shuttering	13/02/11	2 d	20/01/11	21/01/11	100%													
1.2.2.3.1.2.2	<b>Top Slab</b>	17/02/11	4 d	21/01/11	24/01/11	68%													
1.2.2.3.1.2.2.1	Form Work	15/02/11	2 d	21/01/11	22/01/11	90%													
1.2.2.3.1.2.2.2	Re-bar Work	16/02/11	2 d	22/01/11	23/01/11	80%													
1.2.2.3.1.2.2.3	Concrete	17/02/11	1 d	24/01/11	24/01/11	0%													
1.2.2.3.1.3	<b>Column</b>	15/02/11	13 d	12/01/11	25/01/11	87%													
1.2.2.3.1.3.1	Re-Bar Work	09/02/11	5 d	12/01/11	17/01/11	100%													
1.2.2.3.1.3.2	Form Work	11/02/11	3 d	17/01/11	20/01/11	85%													
1.2.2.3.1.3.3	Concrete	13/02/11	3 d	20/01/11	23/01/11	85%													
1.2.2.3.1.3.4	De-shuttering	15/02/11	2 d	23/01/11	25/01/11	60%													

Project Engineer

Project Incharge

# Ekushey Bhaban Program-Progress (Ver-3.0)


Sl.	Task Name	Baseline Finish	Duration	Start	Finish	% Complete	Jan '11				Feb '11							
							01/01	08/01	15/01	22/01	29/01	05/02	12/02	19/02	26/02			
1.2.2.3.1.4	<b>Shear Wall</b>	<b>19/02/11</b>	<b>38.69 d</b>	<b>20/12/10</b>	<b>27/01/11</b>	<b>54%</b>												
1.2.2.3.1.4.1	Re-Bar Work	10/02/11	3 d	20/12/10	22/01/11	65%												
1.2.2.3.1.4.2	Form Work	13/02/11	3 d	21/01/11	24/01/11	20%												
1.2.2.3.1.4.3	Concrete	16/02/11	2 d	23/01/11	25/01/11	20%												
1.2.2.3.1.4.4	De-shuttering	19/02/11	3 d	24/01/11	27/01/11	100%												
1.2.2.3.1.5	<b>Stair - 1</b>	<b>11/02/11</b>	<b>4 d</b>	<b>21/01/11</b>	<b>24/01/11</b>	<b>69%</b>												
1.2.2.3.1.5.1	<b>1st Flight</b>	<b>11/02/11</b>	<b>4 d</b>	<b>21/01/11</b>	<b>24/01/11</b>	<b>69%</b>												
1.2.2.3.1.5.1.1	Brick Work	08/02/11	1 d	21/01/11	21/01/11	100%												
1.2.2.3.1.5.1.2	Form Work	09/02/11	1 d	22/01/11	22/01/11	60%												
1.2.2.3.1.5.1.3	Re-bar Work	10/02/11	1 d	23/01/11	23/01/11	60%												
1.2.2.3.1.5.1.4	Concrete	11/02/11	1 d	24/01/11	24/01/11	54%												
1.2.2.3.1.6	<b>Ramp</b>	<b>27/02/11</b>	<b>2 d</b>	<b>22/01/11</b>	<b>23/01/11</b>	<b>0%</b>												
1.2.2.3.1.6.1	Form Work	26/02/11	1 d	22/01/11	22/01/11	0%												
1.2.2.3.1.6.2	Re-Bar	27/02/11	1 d	23/01/11	23/01/11	0%												
1.2.2.3.1.7	<b>Roof Slab</b>	<b>03/03/11</b>	<b>1 d</b>	<b>27/01/11</b>	<b>28/01/11</b>	<b>0%</b>												
1.2.2.3.1.7.1	Form Work	26/02/11	0 d	27/01/11	27/01/11	0%												
1.2.2.3.1.7.2	Re-bar	28/03/11	0 d	27/01/11	27/01/11	0%												
1.2.2.3.1.7.3	MEP Work	01/03/11	0 d	27/01/11	27/01/11	0%												
1.2.2.3.1.7.4	Inspection	02/03/11	0 d	27/01/11	27/01/11	0%												
1.2.2.3.1.7.5	Concrete	03/03/11	1 d	27/01/11	28/01/11	0%												
1.2.2.3.2	<b>LIFT-2</b>	<b>24/03/11</b>	<b>24.69 d</b>	<b>15/01/11</b>	<b>08/02/11</b>	<b>11%</b>												
1.2.2.3.2.1	<b>Retaining Wall</b>	<b>17/03/11</b>	<b>13 d</b>	<b>15/01/11</b>	<b>28/01/11</b>	<b>24%</b>												
1.2.2.3.2.1.1	<i>Brick Wall</i>	<i>05/03/11</i>	<i>8 d</i>	<i>15/01/11</i>	<i>23/01/11</i>	<i>50%</i>												
1.2.2.3.2.1.2	Plaster	06/03/11	0 d	23/01/11	23/01/11	0%												
1.2.2.3.2.1.3	Water Proofing	13/03/11	1 d	22/01/11	23/01/11	0%												
1.2.2.3.2.1.4	Re-bar Work	14/03/11	2 d	22/01/11	24/01/11	0%												
1.2.2.3.2.1.5	Form Work	15/03/11	2 d	23/01/11	25/01/11	0%												
1.2.2.3.2.1.6	Concreting	16/03/11	2 d	24/01/11	26/01/11	0%												
1.2.2.3.2.1.7	De-shuttering	17/03/11	2 d	26/01/11	28/01/11	0%												
1.2.2.3.2.2	<b>Column</b>	<b>08/03/11</b>	<b>5 d</b>	<b>23/01/11</b>	<b>28/01/11</b>	<b>5%</b>												
1.2.2.3.2.2.1	Form Work	06/03/11	2 d	23/01/11	25/01/11	0%												
1.2.2.3.2.2.2	Re-Bar Work	05/03/11	1 d	23/01/11	24/01/11	35%												
1.2.2.3.2.2.3	Concrete	07/03/11	2 d	24/01/11	26/01/11	0%												
1.2.2.3.2.2.4	De-shuttering	08/03/11	2 d	26/01/11	28/01/11	0%												
1.2.2.3.2.3	<b>Shear Wall</b>	<b>09/03/11</b>	<b>7 d</b>	<b>24/01/11</b>	<b>31/01/11</b>	<b>8%</b>												
1.2.2.3.2.3.1	Re-Bar Work	06/03/11	3 d	24/01/11	27/01/11	30%												
1.2.2.3.2.3.2	Form Work	07/03/11	3 d	25/01/11	28/01/11	0%												
1.2.2.3.2.3.3	Concrete	08/03/11	3 d	26/01/11	29/01/11	0%												
1.2.2.3.2.3.4	De-shuttering	09/03/11	3 d	28/01/11	31/01/11	0%												

Project Engineer

Project Incharge

## Ekushey Bhaban Program-Progress (Ver-3.0)

Sl.	Task Name	Baseline Finish	Duration	Start	Finish	% Complete	Jan '11					Feb '11					
							01/01	08/01	15/01	22/01	29/01	05/02	12/02	19/02	26/02		
1.2.2.3.2.4	<b>Stair - 1</b>	06/03/11	3 d	25/01/11	27/01/11	0%											
1.2.2.3.2.4.1	<b>2nd Flight</b>	06/03/11	3 d	25/01/11	27/01/11	0%											
1.2.2.3.2.4.1.1	Brick Work	04/03/11	1 d	25/01/11	25/01/11	0%											
1.2.2.3.2.4.1.2	Form Work	05/03/11	1 d	26/01/11	26/01/11	0%											
1.2.2.3.2.4.1.3	Re-bar Work	06/03/11	1 d	27/01/11	27/01/11	0%											
1.2.2.3.2.5	<b>Ramp</b>	06/03/11	3 d	28/01/11	31/01/11	0%											
1.2.2.3.2.5.1	Form Work	04/03/11	1 d	28/01/11	29/01/11	0%											
1.2.2.3.2.5.2	Re-Bar	05/03/11	1 d	29/01/11	30/01/11	0%											
1.2.2.3.2.5.3	Concrete	06/03/11	1 d	30/01/11	31/01/11	0%											
1.2.2.3.2.6	<b>Roof Slab</b>	24/03/11	8 d	31/01/11	08/02/11	0%											
1.2.2.3.2.6.1	Form Work	19/03/11	2 d	31/01/11	02/02/11	0%											
1.2.2.3.2.6.2	Re-bar	21/03/11	3 d	02/02/11	05/02/11	0%											
1.2.2.3.2.6.3	MEP Work	22/03/11	1 d	05/02/11	06/02/11	0%											
1.2.2.3.2.6.4	Inspection	23/03/11	1 d	06/02/11	07/02/11	0%											
1.2.2.3.2.6.5	Concrete	24/03/11	1 d	07/02/11	08/02/11	0%											
1.2.2.4	<b>BASEMENT-2</b>	17/04/11	51 d	28/01/11	20/03/11	9%											
1.2.2.5	<b>BASEMENT-1</b>	12/05/11	82 d	25/02/11	18/05/11	0%											
1.3	<b>SUPER STRUCTURE</b>	02/06/12	370 d	18/05/11	07/06/12	0%											
1.3.1	<b>GROUND FLOOR</b>	07/06/11	25 d	18/05/11	12/06/11	0%											
1.3.2	<b>1ST FLOOR</b>	02/07/11	25 d	12/06/11	07/07/11	0%											
1.3.3	<b>2ND FLOOR</b>	27/07/11	25 d	07/07/11	01/08/11	0%											
1.3.4	<b>3RD FLOOR</b>	21/08/11	25 d	01/08/11	03/09/11	0%											
1.3.5	<b>4TH FLOOR</b>	23/09/11	25 d	03/09/11	28/09/11	0%											
1.3.6	<b>5TH FLOOR</b>	18/10/11	25 d	28/09/11	23/10/11	0%											
1.3.7	<b>6TH FLOOR</b>	20/11/11	25 d	23/10/11	25/11/11	0%											
1.3.8	<b>7TH FLOOR</b>	15/12/11	25 d	25/11/11	20/12/11	0%											
1.3.9	<b>8TH FLOOR</b>	09/01/12	25 d	20/12/11	14/01/12	0%											
1.3.10	<b>9TH FLOOR</b>	03/02/12	25 d	14/01/12	08/02/12	0%											
1.3.11	<b>10TH FLOOR</b>	28/02/12	25 d	08/02/12	04/03/12	0%											
1.3.12	<b>11TH FLOOR</b>	24/03/12	25 d	04/03/12	29/03/12	0%											
1.3.13	<b>12TH FLOOR</b>	18/04/12	25 d	29/03/12	23/04/12	0%											
1.3.14	<b>13TH FLOOR</b>	13/05/12	25 d	23/04/12	18/05/12	0%											
1.3.15	<b>MACHINE FLOOR</b>	02/06/12	20 d	18/05/12	07/06/12	0%											
1.4	<b>FINISHING WORK</b>	02/08/12	509 d	01/03/11	07/08/12	0%											
1.4.1	<b>BASEMENT-3</b>	01/07/11	77 d	01/03/11	17/05/11	0%											
1.4.2	<b>BASEMENT-2</b>	25/07/11	77 d	10/04/11	26/06/11	0%											
1.4.3	<b>BASEMENT-1</b>	19/08/11	77 d	08/06/11	24/08/11	0%											
1.4.4	<b>GROUND FLOOR</b>	06/09/11	62 d	03/07/11	11/09/11	0%											
1.4.5	<b>1ST FLOOR</b>	22/09/11	53 d	28/07/11	27/09/11	0%											

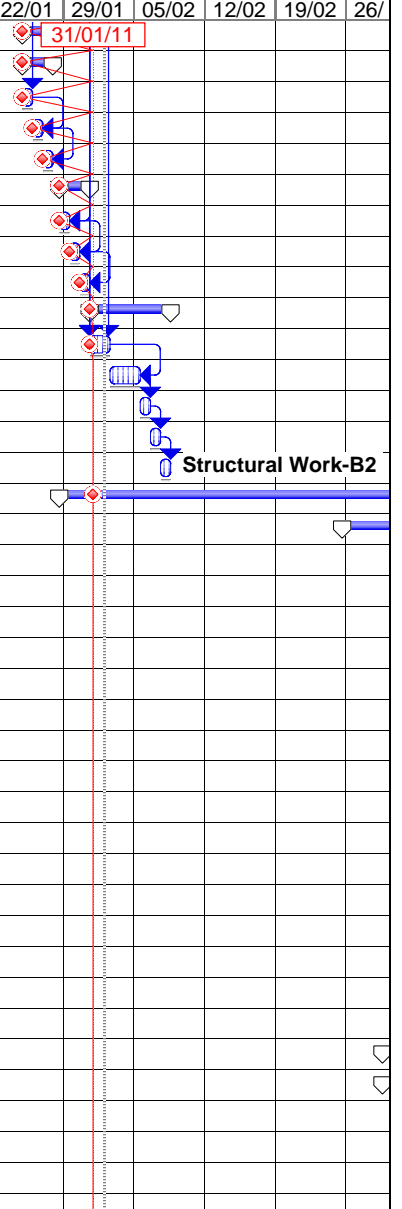

Project Engineer

Project Incharge
