



## MONTHLY PROGRESS REPORT

From 1-January-2022 to 31-January-2022

Project Code:	17	Name:	Shimanto Conference Center					
Client:	Border Guard Bangladesh			Contractor:	Sarker Steel Ltd.			

### Monthly Progress

WBS	Task	Total Qty	Upto Last Month(%)	This Month(%)	Total Done(%)	Schedule Start	Schedule Finish	Actual Finish
1.3.1.1	Brick Work-Ground Floor	1340m2	95	5	100	01-05-21	18-08-21	31-01-22
1.3.1.3	Brick Work-1st Floor	1210m2	95	5	100	28-05-21	04-09-21	31-01-22
1.3.2.2	Plaster-Ground Floor	2680m2	95	5	100	09-05-21	20-08-21	31-01-22
1.3.2.4	Plaster-1st Floor	2420m2	92	3	95	29-08-21	12-09-21	31-01-22
1.3.2.5	Plaster-1st Floor Mezzanine	1560m2	92	3	95	10-09-21	16-09-21	31-01-22
1.3.3	Tiles Work		60	10	70	10-05-21	26-09-21	31-01-22
2.3.1.1	Interior-False Ceiling-GF		95	5	100	09-09-21	08-10-21	05-01-22
2.3.1.2	Interior-False Ceiling-1st Floor	0	0	70	70	16-09-21	15-10-21	31-01-22
2.5.2	Generator		5	75	80	15-09-21	27-10-21	31-01-22
2.7	Road and Landscaping		90	10	100	10-08-21	18-10-21	05-01-22
2.8	Outside Sanitary and Plumbing Work		85	15	100	22-08-21	30-10-21	05-01-22

## Site Photographs



First floor ceiling work on 05-01-22




Interior ceiling on 05-01-22

Site Description

Work stopped 19-26 Dec 2021 due to Inauguration Ceremony

Site Instruction

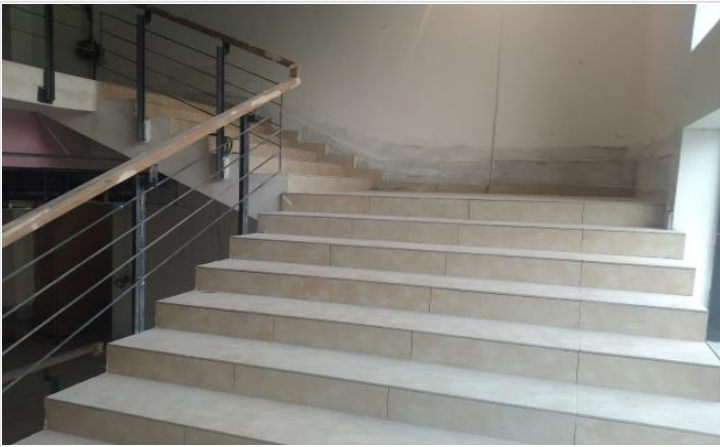

Tiles work on 31-01-22



Interior work on 31-01-22

Site Description

Site Instruction

Entry by:

Planning Engineer

Generated by:

www.bel3c.com, Developed by: Engr. Md. Sanaul Haque
