



MONTHLY PROGRESS REPORT

From 1-April-2024 to 23-April-2024

Project Code:	21	Name:	New Hope Animal Nutrition Plant Bogura
Client:	New Hope	Contractor:	Sarker Steel Ltd.

Monthly Progress

WBS	Task	Total Qty	Upto Last Month(%)	This Month(%)	Total Done(%)	Schedule Start	Schedule Finish	Actual Finish
3.2.5.2.8	Dormitory-1st Floor-False Ceiling-Partit	sum	0	100	100	29-12-23	04-01-24	26-02-24
3.2.5.3.1	Dormitory-2nd Floor-Brickwork	111m2	0	100	100	08-01-24	17-01-24	23-04-24
3.2.5.3.2	Dormitory-2nd Floor-Door Frame fixing	0nos	0	100	100	18-01-24	20-01-24	23-04-24
3.2.5.3.3	Dormitory-2nd Floor-Window Grill Fixing	0nos	0	100	100	18-01-24	20-01-24	23-04-24
3.2.5.3.4	Dormitory-2nd Floor-Inside Plastering	468m2	0	100	100	12-01-24	21-01-24	23-04-24
3.2.5.3.5	Dormitory-2nd Floor-Tiles Fitting	0m2	0	100	100	20-01-24	28-01-24	23-04-24
3.2.5.3.6	Dormitory-2nd Floor-Door-Window fixing	0nos	0	95	95	27-01-24	29-01-24	23-04-24
3.2.5.3.7	Dormitory-2nd Floor-Inside Painting	m2	0	30	30	18-01-24	31-01-24	23-04-24
3.2.5.3.8	Dormitory-2nd Floor-False Ceiling-Partit		0	80	80	25-01-24	31-01-24	05-04-24
3.2.5.5	Dormitory-Outside Plastering	0m2	10	90	100	29-12-23	22-01-24	23-04-24
3.2.5.6	Dormitory-Waterproof-Rooftop		0	100	100	08-01-24	22-01-24	08-04-24
3.2.5.7	Dormitory-Outside Painting	m2	0	30	30	12-01-24	31-01-24	23-04-24
3.2.5.8	Dormitory-Stair Railing		0	100	100	25-01-24	31-01-24	23-04-24
3.2.6.3	Dormitory-2nd Floor-Water-Electrical	0	0	90	90	15-01-24	29-01-24	23-04-24
4.1	Road--Sub-grade Compaction	4817m2	75	25	100	11-07-23	03-01-24	05-04-24
4.2	Sub-base-Car Road-400m	4817m2	75	25	100	06-08-23	10-01-24	05-04-24
4.3	Road-Sub-base-Pedestrian	0m2	0	80	80	19-11-23	17-01-24	23-04-24
4.4	RCC-Car Road	4817m2	4	96	100	26-12-23	24-01-24	05-04-24

WBS	Task	Total Qty	Upto Last Month(%)	This Month(%)	Total Done(%)	Schedule Start	Schedule Finish	Actual Finish
6.1	Hydropower-Main Workshop	0	0	90	90	08-12-23	28-01-24	08-04-24
6.2	Production Buldg-Hydropower installation	1sum	0	90	90	18-12-23	28-01-24	08-04-24
6.4.2	Sub-station-Wall Electric Pipe Work	0m	0	100	100	16-12-23	23-12-23	08-04-24
6.4.3	Electrical Cable/Wiring	0m	0	100	100	23-12-23	22-01-24	08-04-24

Site Photographs



Road-Re-bar work on 05-04-24

Road-RCC on 05-04-24

Site Description

RCC-Car Road Handover

Site Instruction




Electrical Work on 08-04-24

Electrical Work on 08-04-24

Site Description

Site Instruction

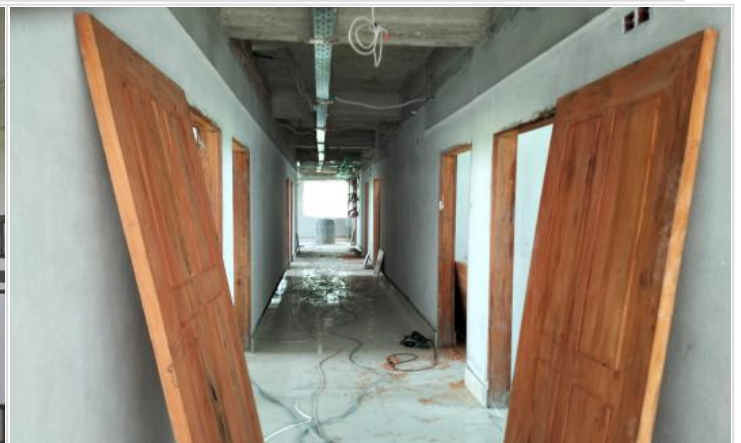

Dormitory-2nd Floor Painting on 23-04-24

Dormitor-2nd Floor-Corridor on 23-04-24

Site Description

Project closed from 09 to 16 April, 2024 due to Eid-ul Fitre

Site Instruction

Entry by:

Planning Engineer

Generated by:

www.bel3c.com, Developed by: Engr. Md. Sanaul Haque
