



DAILY PROGRESS REPORT

Project:	Shimanto Conference Center	Project Code:	17	Date:	31-January-2022
Client:	Border Guard Bangladesh	Report	142	Day	Monday
Contractor:	Sarker Steel Ltd.			Climate	Sunny
					11-22C


Manpower

SN	Description	Nos.
01	Sarker Staff	3
04	AC-Newton-Staff	1
05	AC-Newton-Worker	10
TOTAL		14

Progress This Day

WBS	Task	Total Qty	Today Done(%)	Total Done(%)	Schedule Start	Schedule Finish
1.3.1.1	Brick Work-Ground Floor	1340m2	5	100	01-05-21	18-08-21
1.3.1.3	Brick Work-1st Floor	1210m2	5	100	28-05-21	04-09-21
1.3.2.2	Plaster-Ground Floor	2680m2	5	100	09-05-21	20-08-21
1.3.2.4	Plaster-1st Floor	2420m2	3	95	29-08-21	12-09-21
1.3.2.5	Plaster-1st Floor Mezzanine	1560m2	3	95	10-09-21	16-09-21
1.3.3	Tiles Work		10	70	10-05-21	26-09-21
2.3.1.2	Interior-False Ceiling-1st Floor	0	70	70	16-09-21	15-10-21
2.5.2	Generator		20	80	15-09-21	27-10-21

Site Photographs

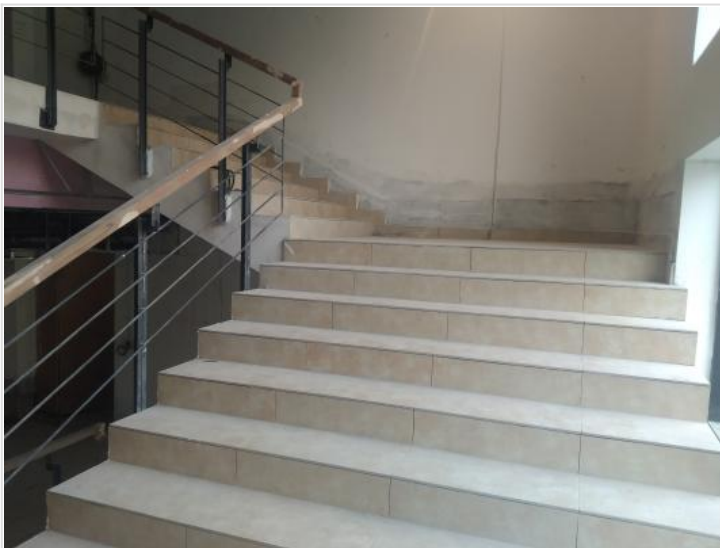

Tiles work



Interior work

Site Description

Site Instruction

Entry by:

Generated by:

