



## WEEKLY PROGRESS REPORT

From 16-November-2024 to 22-November-2024

Project Code:	31	Name:	New Hope Agrotech-Munshiganj					
Client:	New Hope Agrotech BD Ltd.			Contractor:	Sarker Steel Ltd.			

### Weekly Progress

WBS	Task	Total Qty	Upto Last Week(%)	This Week(%)	Total Done(%)	Schedule Start	Schedule Finish	Actual Finish
04.06	Basement Wall	3nos	86	14	100	30-10-24	18-11-24	16-11-24
04.08	Anchor Bolt setting	84nos	81	19	100	09-11-24	18-11-24	18-11-24
04.09	Foundation Beam	32gap	69	31	100	07-11-24	21-11-24	18-11-24
04.11	Foundation (Tank) Slab	139m2	0	21	21	19-11-24	28-11-24	22-11-24
04.14	Embedded Steel Parts	1740kg	0	50	50	21-11-24	28-11-24	21-11-24
04.15	Tank wall water proofing membrain-SBS	195m2	0	22	22	17-11-24	19-11-24	22-11-24
05.01	Steel-Shop Drawing	0	70	30	100	15-10-24	14-11-24	19-11-24
05.02	Shop drawing Approval	0	50	50	100	14-11-24	21-11-24	21-11-24
05.03.1	Production-1st Floor	55ton	5	85	90	21-11-24	29-11-24	02-11-24

## Site Photographs



Wall concreting on 16-11-24

Site Description

Site Instruction



Foundation beam concreting on 16-11-24




Foundation beam bottom shuttering on 17-11-24

Site Description

Site Instruction




Foundation beam rebar work on 17-11-24

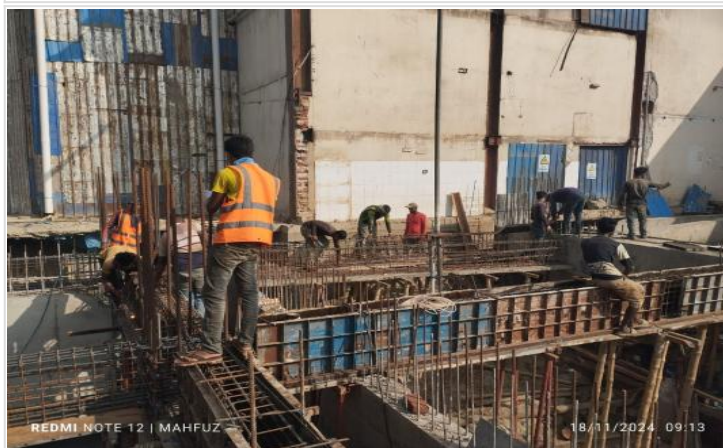

Anchor bolt setting on 18-11-24

Site Description

Site Instruction

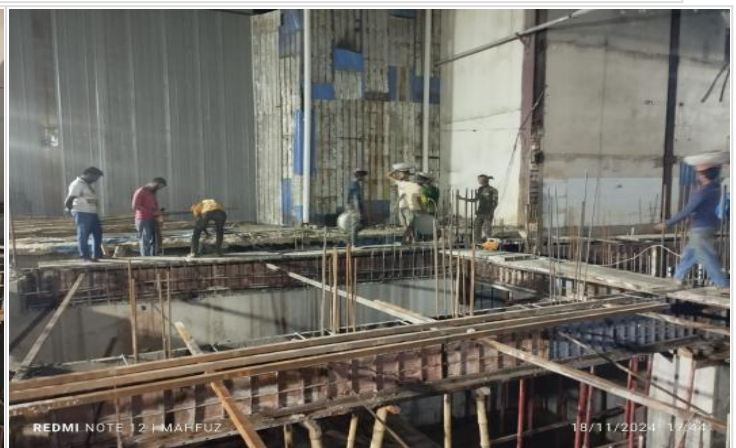

Foundation beam concreting on 18-11-24



Tank slab shuttering on 19-11-24

Tank slab shuttering on 19-11-24

Site Description

Site Instruction



Tank slab shuttering on 20-11-24

Tank slab shuttering on 20-11-24

Site Description

Site Instruction



Embedded steel parts mobilized on 21-11-24

Tank slab shuttering on 21-11-24

Site Description

Site Instruction



Tank slab shuttering on 22-11-24

Tank wall water proofing membrain SBS fi on 22-11-24

Site Description	
Site Instruction	
Entry by: Planning Engineer	Generated by: www.bel3c.com, Developed by: Engr. Md. Sanaul Haque
