



TOTAL PROGRESS REPORT

From 22-December-2022 to 6-March-2023

Project Code:	61	Name:	Cityscape Tower Level-15 Bar						
Client:	Cityscape	Contractor:	Cityscape International Ltd.						
Total Duration:	74	days	Total Working Days:	15	Total Manpower:	129			
Planning Progress =	65.9%	Actual Progress=	54.6%	SPI=	0.83	Behind Schedule			

Total Progress

WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)	Not Yet
01	Glass Work	01	90	22-12-22	21-01-23	22-12-22	06-03-23	-44	Completed
02	Carpentry Mock-up	1sum	100	22-12-22	23-12-22	22-12-22	26-12-22	-3	
03	Bar Counter	1sum	50	22-12-22	06-01-23	22-12-22	26-01-23	-20	Completed
04	Washroom Brickwork	1sum	90	22-12-22	27-12-22	22-12-22	03-01-23	-7	Completed
05	Floor Finsh-NCF	1sum	100	26-12-22	31-12-22	03-01-23	12-02-23	-43	
06	Wall Paneling	1sum	5	08-02-23	09-03-23	08-02-23	08-02-23	29	

Site Photographs



Carpentry Mock-up on 22-12-22



Brick work demolition on 22-12-22



on 23-12-22



on 23-12-22



on 26-12-22



on 26-12-22



Glass Work on 31-12-22



Wash Room Brick work on 31-12-22



Interior works on 03-01-23



Floor Finishing-NCF on 03-01-23



Fixing Glass on 09-01-23



Fixing Glass on 09-01-23



on 14-01-23



on 14-01-23




on 17-01-23



on 17-01-23



on 26-01-23

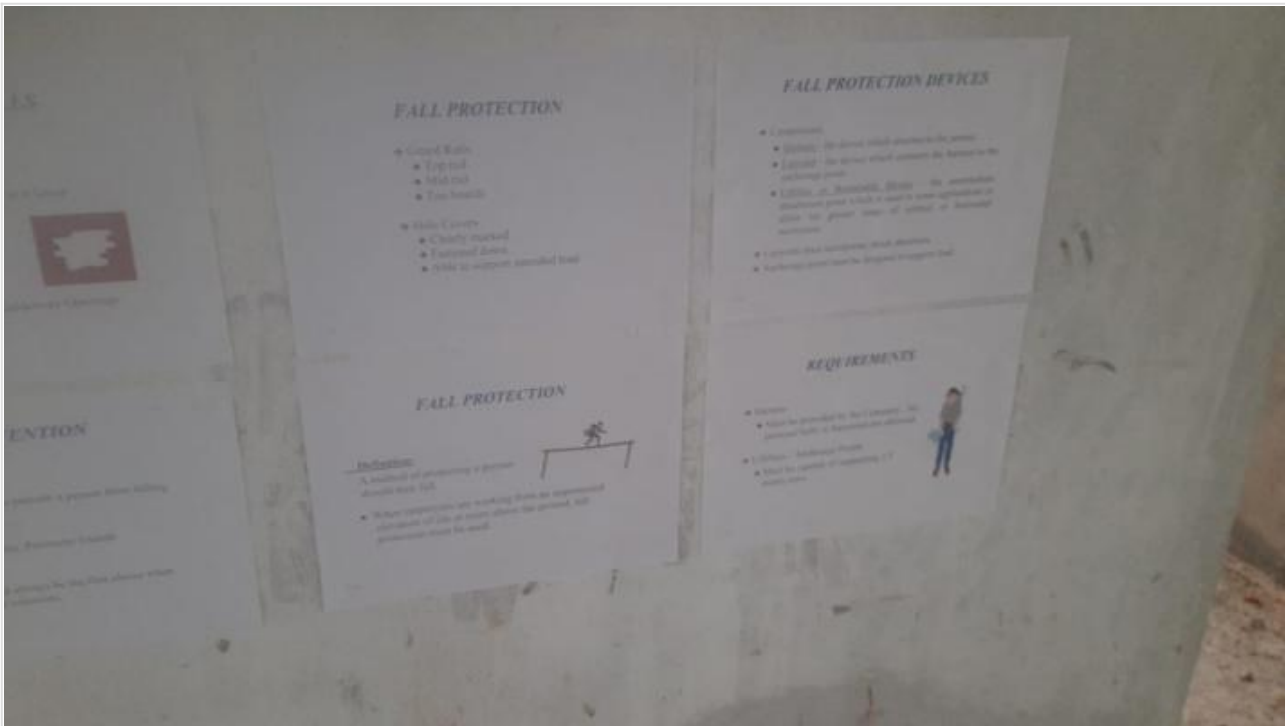

Safety Instruction on 26-01-23



on 31-01-23



on 31-01-23



on 05-02-23



on 05-02-23



Wall Paneling on 08-02-23



Wall Paneling on 08-02-23



L-15-Floor Neat Cement Finishing on 12-02-23



L-15-Floor Neat Cement Finishing on 12-02-23









L-15-South side glass fixing on 06-03-23

Generated by: www.bel3c.com, Developed by: Engr. Md. Sanaul Haque
