

**CONSTRUCTION OF 150000 TONS LIVESTOCK AND
POULTRY FEED FACTORY IN BOGRURA, RAJSHAI,
BANGLADESH**

PROJECT COMPLETION REPORT



23 APRIL 2024

Generated by: Sarker Steel Ltd.

TABLE OF CONTENTS

- TOTAL PROGRESS
- TOTAL MANPOWER CHART
- CUMMULATIVE PROGRESS CHART
- SCHEDULE LEAD-LAG CHART
- LAST MONTH PROGRESS
- LAST MONTH MANPOWER HISTOGRAM
- LAST MONTH PROGRESS CHART
- DAILY PROGRESS REPORT
- WORK PLAN AND PROGRESS
- PROGRESS PHOTO



TOTAL PROGRESS REPORT

From 9-January-2023 to 23-April-2024

Project Code:	21	Name:	New Hope Animal Nutrition Plant Bogura			
Client:	New Hope	Contractor:	Sarker Steel Ltd.			
Total Duration:	470	days	Total Working Days:	223	Total Manpower:	8279
Planning Progress =	96.4%	Actual Progress=	94%	SPI=	0.98	Behind Schedule

Total Progress

WBS	Task	Total Qty	Total Done(%)	Schedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)	Not Yet
1.1	Mobilization-Shed	1sum	100	09-01-23	20-01-23	09-01-23	22-01-23	-2	
1.2	Mobilization-Labor	1sum	100	14-01-23	17-01-23	14-01-23	17-01-23	0	
1.3	Mobilization-Materials	1sum	100	21-01-23	22-01-23	21-01-23	21-01-23	1	
1.4	Mobilization-Equipment	1sum	100	27-01-23	28-01-23	29-01-23	29-01-23	-1	
1.5	Electricity Connection	01	100	31-01-23	06-02-23	31-01-23	06-02-23	0	
1.6	Tube-well Sinking	1no.	100	01-02-23	01-02-23	01-02-23	01-02-23	0	
1.7	Mud Tank Making	2nos	100	01-02-23	12-02-23	02-02-23	12-02-23	0	
2	Pile Layout and Survey	1sum	100	01-02-23	02-02-23	01-02-23	03-02-23	-1	
3.1.1	Comp.Bldg-Pile Boring, Concreting	69nos	100	09-02-23	10-03-23	09-02-23	17-03-23	-7	
3.1.2	Comp Bldg-Load Test-Integrity Test	1sum	100	11-04-23	13-04-23	06-04-23	14-04-23	-1	
3.1.3.1	Comp Bldg-Pile head Breaking	69nos	100	18-03-23	27-03-23	16-03-23	06-04-23	-10	
3.1.3.2	Comp Bldg-Pile Cap	20nos	100	21-03-23	30-03-23	05-04-23	18-04-23	-19	
3.1.3.3	Comp Bldg-Foundation Beam	266m	100	31-03-23	13-04-23	19-04-23	16-05-23	-33	
3.1.4.1.1	Comp Bldg-GF-Column	20nos	100	24-05-23	01-06-23	22-05-23	02-06-23	-1	
3.1.4.1.2.1	Comp Bldg-GF-Stair-1st Flight	1nos	100	28-05-23	01-06-23	01-06-23	05-06-23	-4	
3.1.4.1.2.2	Comp Bldg-GF-Stair-2nd Flight	1nos	100	04-06-23	10-06-23	22-06-23	27-06-23	-17	
3.1.4.1.3.1	Comp-1st Floor Slab-Formwork	613m2	100	01-06-23	06-06-23	01-06-23	22-06-23	-16	
3.1.4.1.3.2	Comp-1st Floor Slab-Re-bar Work	613m2	100	07-06-23	09-06-23	02-06-23	22-06-23	-13	
3.1.4.1.3.3	Comp-1st Floor Slab-Electrical	613m2	100	08-06-23	09-06-23	22-06-23	22-06-23	-13	

WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)	Not Yet
3.1.4.1.3.4	Comp-1st Floor Slab Concreting	613m2	100	10-06-23	10-06-23	27-06-23	27-06-23	-17	
3.1.4.2.1	Comp Bldg-1st Floor-Column	20nos	100	12-06-23	18-06-23	06-07-23	19-07-23	-31	
3.1.4.2.2.1	Comp-1st Floor-Stair-1st Flight	1no.	100	12-06-23	18-06-23	06-07-23	16-07-23	-28	
3.1.4.2.2.2	Comp-1st Floor-Stair-2nd Flight	1no.	100	20-06-23	26-06-23	17-07-23	04-08-23	-39	
3.1.4.2.3.1	Comp-2nd Floor Slab-Formwork	613m2	100	19-06-23	24-06-23	16-07-23	31-07-23	-37	
3.1.4.2.3.2	Comp-2nd Floor Slab-Re-bar Work	613m2	100	25-06-23	26-06-23	17-07-23	02-08-23	-37	
3.1.4.2.3.3	Comp-2nd Floor Slab-Electrical Work	613m2	100	25-06-23	26-06-23	04-08-23	04-08-23	-39	
3.1.4.2.3.4	Comp-2nd Floor Slab-Concreting	613m2	100	26-06-23	26-06-23	04-08-23	04-08-23	-39	
3.1.4.3.1	Comp-Top Floor-Column	4nos	100	08-07-23	09-07-23	21-08-23	27-08-23	-49	
3.1.4.3.2	Comp-Top Floor Roof Slab	0m2	100	10-07-23	11-07-23	03-09-23	16-09-23	-67	
3.1.4.3.3	Comp Parapet-Brick Wall	153m2	100	08-07-23	10-07-23	14-08-23	22-09-23	-74	
3.1.5.1.1	Comp-GF-Brickwork	111m3	100	25-06-23	11-07-23	21-07-23	08-09-23	-59	
3.1.5.1.2	Comp-GF-Window Grill	0nos	100	12-07-23	14-07-23	03-09-23	21-09-23	-69	
3.1.5.1.3	Comp-GF-Plaster work	1364m2	100	11-07-23	15-07-23	18-08-23	21-09-23	-68	
3.1.5.1.4	Comp-Khoa-sand Cushion in Floor	613m2	100	11-07-23	15-07-23	14-08-23	25-09-23	-72	
3.1.5.1.5	Comp-GF-Floor Concreting	613m2	100	10-07-23	16-07-23	16-09-23	02-11-23	-109	
3.1.5.1.6	Comp-GF-Tiles Fitting	790m2	100	17-07-23	23-07-23	25-10-23	02-02-24	-194	
3.1.5.1.7	Comp-GF-Door Shutter-Window fixing	0nos	100	22-07-23	24-07-23	02-02-24	02-02-24	-193	
3.1.5.1.8	Comp-GF-False Ceiling		100	10-07-23	24-07-23	02-02-24	02-02-24	-193	
3.1.5.1.9	Comp-GF-Painting		100	25-11-23	19-12-23	02-02-24	02-02-24	-45	
3.1.5.2.1	Comp-1st Floor-Brickwork	111m3	100	26-07-23	01-08-23	22-08-23	22-09-23	-52	
3.1.5.2.2	Comp-1st Floor-Plaster Work	1364m2	100	01-08-23	05-08-23	03-09-23	02-02-24	-181	
3.1.5.2.3	Comp-1st Floor-Tile Fixing	613m2	100	04-08-23	10-08-23	02-02-24	02-02-24	-176	
3.1.5.2.4	Comp-1st Floor-Door Shutter Window fixin	0nos	100	09-08-23	11-08-23	02-02-24	02-02-24	-175	
3.1.5.2.5	Comp-1st Floor-False Ceiling		100	28-07-23	11-08-24	02-02-24	02-02-24	191	

WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)	Not Yet
3.1.5.2.6	Comp-1st Floor-Painting		100	02-12-23	26-12-23	02-02-24	02-02-24	-38	
3.1.5.3	Comp-Outside Plastering	m2	100	28-07-23	11-08-23	08-10-23	02-11-23	-83	
3.1.6.1.1	Comp-GF-Sanitary Pipe Work	1sum	100	12-07-23	21-12-23	19-07-23	02-02-24	-43	
3.1.6.1.2	Comp-GF-Plumbing work	1sum	100	12-07-23	18-07-23	31-10-23	02-02-24	-199	
3.1.6.1.3	Comp-GF-Electrical Pipe Work	1sum	100	12-07-23	18-07-23	27-07-23	23-08-23	-36	
3.1.6.1.4	Comp-GF-Power Distribution Board	nos	100	19-07-23	25-07-23	26-10-23	02-02-24	-192	
3.1.6.1.5	Comp-GF-Cable Tray	80m	100	19-07-23	25-07-23	29-09-23	29-09-23	-66	
3.1.6.1.6	Comp-GF-Electric Cable/wiring	1Sum	100	13-07-23	19-07-23	13-10-23	31-10-23	-104	
3.1.6.1.7	Comp-GF-Sanitary Fixer installi	1Sum	100	21-12-23	27-12-23	02-02-24	02-02-24	-37	
3.1.6.1.8	Comp-GF-Electric switch-socket fix	1Sum	100	25-12-23	27-12-23	02-02-24	02-02-24	-37	
3.1.6.2.1	Comp-1st Floor-Sanitary Pipe Work	1Sum	100	04-08-23	08-08-23	03-09-23	02-02-24	-178	
3.1.6.2.2	Comp.1st Floor-Plumbing work	1sum	100	04-08-23	08-08-23	31-10-23	02-02-24	-178	
3.1.6.2.3	Comp.1st Floor-Electrical Pipe work		100	04-08-23	08-08-23	03-09-23	31-10-23	-84	
3.1.6.2.4	Comp-1st Floor-Power Distribution Board	nos	100	05-08-23	11-08-23	26-10-23	02-02-24	-175	
3.1.6.2.5	Comp-1st Floor-Cable Tray	80m	100	05-08-23	11-08-23	25-10-23	31-10-23	-81	
3.1.6.2.6	Comp.1st Floor-Electrical Cable/wiring	1sum	100	07-08-23	09-08-23	31-10-23	31-10-23	-83	
3.1.6.2.7	Comp.1st Floor-Sanitary fixer installati	1sum	100	21-12-23	27-12-23	02-02-24	02-02-24	-37	
3.1.6.2.8	Comp-1st Floor-Elect switch-socket	1sum	100	25-12-23	27-12-23	02-02-24	02-02-24	-37	
3.2.1	Canteen Dormitory-Pile Boring, Concretin	38nos	100	12-03-23	26-03-23	25-03-23	13-04-23	-18	
3.2.2	Canteen Dormitory-Load Test-Integrity Te	1sum	100	30-04-23	30-04-23	19-05-23	19-05-23	-19	

WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)	Not Yet
3.2.3.1	Canteen Dormitory-Pilehead Breaking	38nos	100	01-05-23	10-05-23	02-05-23	23-05-23	-13	
3.2.3.2	Canteen Dormitory-Pile Cap	12nos	100	20-05-23	29-05-23	11-05-23	29-05-23	0	
3.2.3.3	Canteen Dormitory-Short Column	12nos	100	30-05-23	01-06-23	01-06-23	13-06-23	-12	
3.2.3.4	Canteen Dormitory-Grade Beam	164m	100	02-06-23	08-06-23	01-06-23	13-06-23	-5	
3.2.4.1.1	Canteen Dormitory-GF-Column	12nos	100	18-06-23	26-06-23	20-06-23	27-06-23	-1	
3.2.4.1.2.1	Canteen Dormitory-GF-Stair-1st Flight	1no.	100	09-07-23	13-07-23	08-07-23	02-08-23	-20	
3.2.4.1.2.2	Canteen Dormitory-GF-Stair-2nd Flight	1no.	100	20-07-23	26-07-23	04-08-23	10-08-23	-15	
3.2.4.1.3.1	Canteen Dormitory-1st Floor Slab-Form	240m2	100	12-07-23	21-07-23	21-07-23	06-08-23	-16	
3.2.4.1.3.2	Canteen Dormitory-1st Floor Slab-Rebar	240m2	100	22-07-23	25-07-23	02-08-23	06-08-23	-12	
3.2.4.1.3.3	Canteen Dormitory-1st Floor Slab-Electri	240m2	100	23-07-23	25-07-23	07-08-23	09-08-23	-15	
3.2.4.1.3.4	Canteen Dormitory-1st Floor Slab-Concret	240m2	100	26-07-23	26-07-23	10-08-23	10-08-23	-15	
3.2.4.2.1	Canteen Dormitory-1st Floor-Column	12nos.	100	13-08-23	19-08-23	18-08-23	01-09-23	-13	
3.2.4.2.2.1	Canteen Dormitory-1st Floor-Stair-1st Fl	1no,	100	13-08-23	19-08-23	23-08-23	30-08-23	-11	
3.2.4.2.2.2	Canteen Dormitory-1st Floor-Stair-2nd Fl	1no.	100	26-08-23	01-09-23	01-09-23	16-09-23	-15	
3.2.4.2.3.1	Canteen Dormitory-2nd Floor-Form Work	240m2	100	20-08-23	27-08-23	03-09-23	08-09-23	-12	
3.2.4.2.3.2	Canteen Dormitory-2nd Floor-Slab-Rebar	240m2	100	28-08-23	01-09-23	04-09-23	09-09-23	-8	
3.2.4.2.3.3	Canteen Dormitory-2nd Floor Slab-Electri	240m2	100	31-08-23	01-09-23	16-09-23	16-09-23	-15	

WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)	Not Yet
3.2.4.2.3.4	Canteen Dormitory-2nd Floor Slab- Concret	240m2	100	01-09-23	01-09-23	16-09-23	16-09-23	-15	
3.2.4.3.1	Dormitory-2nd Floor-Column	12nos	100	04-09-23	02-11-23	04-10-23	03-11-23	-1	
3.2.4.3.2.1	Dormitory-2nd Floor-Stair-1st Flight	1no.	100	27-10-23	02-11-23	23-12-23	23-04-24	-173	
3.2.4.3.2.2	Dormitory-2nd Floor-Stair-2nd Flight	1no.	100	04-12-23	10-12-23	23-12-23	23-04-24	-135	
3.2.4.3.3.1	Dormitory-3rd Floor Slab- Formwork	240m2	100	03-11-23	10-11-23	08-11-23	18-12-23	-38	
3.2.4.3.3.2	Dormitory-3rd Floor Slab-Re- bar Work	240m2	100	06-12-23	10-12-23	18-12-23	18-12-23	-8	
3.2.4.3.3.3	Dormitory-3rd Floor Slab- Electrical Pipe	240m2	100	09-12-23	10-12-23	18-12-23	18-12-23	-8	
3.2.4.3.3.4	Dormitory-3rd Floor Slab- Concreting	240m2	100	10-12-23	10-12-23	23-12-23	23-04-24	-135	
3.2.5.1.1	Canteen Dormitory-GF Brickwork	111m2	100	31-07-23	16-08-23	20-09-23	18-10-23	-63	
3.2.5.1.2	Canteen Dormitory-GF- Door Frame fixing	0nos	100	11-12-23	17-12-23	26-02-24	26-02-24	-71	
3.2.5.1.3	Canteen Dormitory-GF- Window Grill Fixing	0nos	100	11-12-23	17-12-23	26-02-24	26-02-24	-71	
3.2.5.1.4	Canteen Dormitory-GF- Inside Plastering	468m2	178	16-08-23	20-08-23	27-10-23	26-02-24	-190	
3.2.5.1.5	Canteen Dormitory-GF- Khoa-sand cushion	240m2	140	16-08-23	20-08-23	09-11-23	26-02-24	-190	
3.2.5.1.6	Canteen Dormitory-GF- Concereting	240m2	100	16-08-23	21-08-23	26-02-24	26-02-24	-189	
3.2.5.1.7	Canteen Dormitory-GF- Tiles	240m2	100	05-12-23	19-12-23	26-02-24	26-02-24	-69	
3.2.5.1.8	Canteen Dormitory-GF- Door-Window fixing	0nos	100	18-12-23	20-12-23	26-02-24	26-02-24	-68	
3.2.5.1.9	Dormatory-GF- Painting		100	06-12-24	20-12-24	26-02-25	26-02-25	-68	
3.2.5.2.1	Canteen Dormitory-1st Floor-Brickwork	111m2	100	09-10-23	15-10-23	06-10-23	20-10-23	-5	


WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)	Not Yet
3.2.5.2.2	Canteen Dormitory-1st Floor-Door Frame f	0nos	100	18-12-23	20-10-23	26-02-24	26-02-24	-129	
3.2.5.2.3	Canteen Dormitory-1st Floor-Window Grill	0nos	100	18-12-23	20-12-23	26-02-24	26-02-24	-68	
3.2.5.2.4	Canteen Dormitory-1st Floor-Plaster work	0m2	100	15-10-23	21-12-23	26-02-24	26-02-24	-67	
3.2.5.2.5	Canteen Dormitory-1st Floor-Tile work	0m2	100	20-12-23	03-01-24	26-02-24	26-02-24	-54	
3.2.5.2.6	Canteen Dormitory-1st Floor-Door-window	0nos	100	02-01-24	04-01-24	26-02-24	26-02-24	-53	
3.2.5.2.7	Dormitory-1st Floor-Painting		100	21-12-24	04-01-25	26-02-24	26-02-25	-53	
3.2.5.2.8	Dormitory-1st Floor-False Ceiling-Partit	sum	100	29-12-23	04-01-24	23-04-24	26-02-24	-53	
3.2.5.3.1	Dormitory-2nd Floor-Brickwork	111m2	100	08-01-24	17-01-24	23-04-24	23-04-24	-97	
3.2.5.3.2	Dormitory-2nd Floor-Door Frame fixing	0nos	100	18-01-24	20-01-24	23-04-24	23-04-24	-94	
3.2.5.3.3	Dormitory-2nd Floor-Window Grill Fixing	0nos	100	18-01-24	20-01-24	23-04-24	23-04-24	-94	
3.2.5.3.4	Dormitory-2nd Floor-Inside Plastering	468m2	100	12-01-24	21-01-24	23-04-24	23-04-24	-93	
3.2.5.3.5	Dormitory-2nd Floor-Tiles Fitting	0m2	100	20-01-24	28-01-24	23-04-24	23-04-24	-86	
3.2.5.3.6	Dormitory-2nd Floor-Door-Window fixing	0nos	95	27-01-24	29-01-24	23-04-24	23-04-24	-85	Completed
3.2.5.3.7	Dormitory-2nd Floor-Inside Painting	m2	30	18-01-24	31-01-24	23-04-24	23-04-24	-83	Completed
3.2.5.3.8	Dormitory-2nd Floor-False Ceiling-Partit		80	25-01-24	31-01-24	05-04-24	05-04-24	-65	Completed
3.2.5.4	Dormitory-Parapet Brick Wall	0m2	100	14-12-23	28-12-23	26-02-24	26-02-24	-60	
3.2.5.5	Dormitory-Outside Plastering	0m2	100	29-12-23	22-01-24	26-02-24	23-04-24	-92	
3.2.5.6	Dormitory-Waterproof-Rooftop		100	08-01-24	22-01-24	08-04-24	08-04-24	-77	
3.2.5.7	Dormitory-Outside Painting	m2	30	12-01-24	31-01-24	23-04-24	23-04-24	-83	Completed

WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)	Not Yet
3.2.5.8	Dormitory-Stair Railing		100	25-01-24	31-01-24	05-04-24	23-04-24	-83	
3.2.6.1.1	Canteen Dormitory-GF-Sanitary Pipe work	1sum	100	17-08-23	23-08-23	07-11-23	26-02-24	-187	
3.2.6.1.2	Canteen Dormitory-GF-Plumbing work	1sum	100	22-12-23	28-12-23	26-02-24	26-02-24	-60	
3.2.6.1.3	Canteen Dormitory-GF-Electrical Pipe Wor	1sum	100	17-08-23	23-08-23	31-10-23	31-10-23	-69	
3.2.6.1.4	Dormitory-GF-Power Distribution Board	nos	100	22-12-23	28-12-23	26-02-24	26-02-24	-60	
3.2.6.1.5	Dormitory-GF-Cable Tray	m	100	20-08-23	26-08-23	26-02-24	26-02-24	-184	
3.2.6.1.6	Canteen Dormitory-GF-Electrical Cable wi	1sum	100	22-12-23	28-12-23	26-02-24	26-02-24	-60	
3.2.6.1.7	Canteen Dormitory-GF-Sanitary Fixer inst	1sum	100	04-01-24	10-01-24	26-02-24	26-02-24	-47	
3.2.6.1.8	Canteen Dormitory-GF-Electrical Switch-s	1sum	100	08-01-24	10-01-24	26-02-24	26-02-24	-47	
3.2.6.2.1	Dormitory-1st Floor-Sanitary Pipe Work	1sum	100	16-10-23	22-10-23	26-02-24	26-02-24	-127	
3.2.6.2.2	Dormitory-1st Floor-Plumbing Work	1sum	100	29-12-23	04-01-24	26-02-24	26-02-24	-53	
3.2.6.2.3	Dormitory-1st Floor-Electrical Pipe Work	1sum	100	29-12-23	04-01-24	07-11-23	26-02-24	-53	
3.2.6.2.4	Dormitory-1st Floor-Power Distribution B	0	100	05-01-24	07-01-24	26-02-24	26-02-24	-50	
3.2.6.2.5	Dormitory-1st Floor-Cable Tray	1sum	100	01-01-24	07-01-24	26-02-24	26-02-24	-50	
3.2.6.2.6	Dormitory-1st Floor-Electric Wiring/Cabl	1sum	100	08-01-24	14-01-24	26-02-24	26-02-24	-43	
3.2.6.2.7	Dormitory-1st Floor-Sanitary Fixer	0	100	05-01-24	05-01-24	26-02-24	26-02-24	-52	
3.2.6.2.8	Dormitory-1st Floor-Electrical Switch-So	0	100	04-01-24	05-01-24	26-02-24	26-02-24	-52	
3.2.6.3	Dormitory-2nd Floor-Water-Electrical	0	90	15-01-24	29-01-24	23-04-24	23-04-24	-85	Completed


WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)	Not Yet
3.3.1	Gate House-Pile Boring, Concreting	6nos	100	28-03-23	29-03-23	19-03-23	21-03-23	8	
3.3.2	Gate House-Pile Integrity Test	1nos	100	17-04-23	19-04-23	14-04-23	14-04-23	5	
3.3.3.1	Gate House-Pile Cap	6nos	100	03-05-23	07-05-23	08-05-23	12-05-23	-5	
3.3.3.2	Gate House-Foundation Beam	50m	100	08-05-23	17-05-23	15-05-23	18-05-23	-1	
3.3.4	Gate House-Brick Work	35m3	100	28-05-23	10-06-23	28-05-23	20-06-23	-10	
3.3.5	Gate House-Column	6nos	100	11-06-23	17-06-23	06-06-23	19-06-23	-2	
3.3.6	Gate House-Roof Slab	93m2	100	18-06-23	25-06-23	25-06-23	11-07-23	-16	
3.3.7.1	Gate House-Door Frame fixing	4nos	100	12-08-23	14-08-23	20-08-23	20-08-23	-6	
3.3.7.2	Gate House-Paster Work	234m2	100	11-08-23	15-08-23	26-07-23	20-08-23	-5	
3.3.7.3	Gate House-Khoa-sand cushion in floor	93m2	100	14-08-23	16-08-23	02-08-23	02-08-23	14	
3.3.7.4	Gate House-Floor concreting	93m2	100	17-08-23	19-08-23	01-09-23	01-09-23	-13	
3.3.7.5	Gate House-Tiles fitting	93m2	100	20-08-23	24-08-23	26-09-23	04-10-23	-41	
3.3.7.6	Gate House-Door Shutter, Window fixing	11nos	100	25-08-23	26-08-23	27-10-23	03-11-23	-69	
3.3.7.7	Gate House-Painting	m2	100	09-10-23	15-10-23	08-11-23	10-11-23	-26	
3.3.8.1	Gate House-Electrical Pipe Work	1sum	100	12-08-23	16-08-23	19-07-23	21-07-23	26	
3.3.8.2	Gate House-Electric cable/wiring	0sum	100	23-08-23	24-08-23	13-10-23	13-10-23	-50	
3.3.8.3	Gate House-Electrical Switch Socket Fixi	0sum	100	25-08-23	26-08-23	13-11-23	13-11-23	-79	
4.1	Road--Sub-grade Compaction	4817m2	100	11-07-23	03-01-24	20-07-23	05-04-24	-93	
4.2	Sub-base-Car Road-400m	4817m2	100	06-08-23	10-01-24	22-07-23	05-04-24	-86	
4.3	Road-Sub-base-Pedestrain	0m2	80	19-11-23	17-01-24	23-04-24	23-04-24	-97	Completed
4.4	RCC-Car Road	4817m2	100	26-12-23	24-01-24	15-10-23	05-04-24	-72	
4.5	RCC-Pedstrain	0m2	0	02-01-24	31-01-24		30-11--10		Started
5.1	Outdoor-Electrical-Power Cable	2916m	100	11-07-23	15-12-23	04-10-23	26-02-24	-73	

WBS	Task	Total Qty	Total Done(%)	Shedule Start	Schedule Finish	Actual Start	Actual Finish	Lead-Lag(day)	Not Yet
5.2	Outdoor-Water Supply Pipe	0	100	16-12-23	14-01-24	26-02-24	26-02-24	-43	
5.3	Outdoor-Sewerage	0	100	16-12-23	14-01-24	26-02-24	26-02-24	-43	
6.1	Hydropower-Main Workshop	0	90	08-12-23	28-01-24	08-04-24	08-04-24	-71	Completed
6.2	Production Buldg-Hydropower installation	1sum	90	18-12-23	28-01-24	08-04-24	08-04-24	-71	Completed
6.3	Hydropower-Boiler Room	0	0	08-12-23	28-01-24		30-11--10	0	Started
6.4.1	Substation-Roof Slab Electric Pipe Work		100	11-10-23	13-10-23	22-07-23	22-07-23	83	
6.4.2	Sub-station-Wall Electric Pipe Work	0m	100	16-12-23	23-12-23	08-04-24	08-04-24	-107	
6.4.3	Electrical Cable/Wiring	0m	100	23-12-23	22-01-24	08-04-24	08-04-24	-77	
6.4.4	Sub-station-Switch Socket Fixing	1sum	0	15-01-24	21-01-24		30-11--10	0	Started
7	NewHope-Handover	0	0	31-01-24	31-01-24		30-11--10	0	Started


DAILY MANPOWER

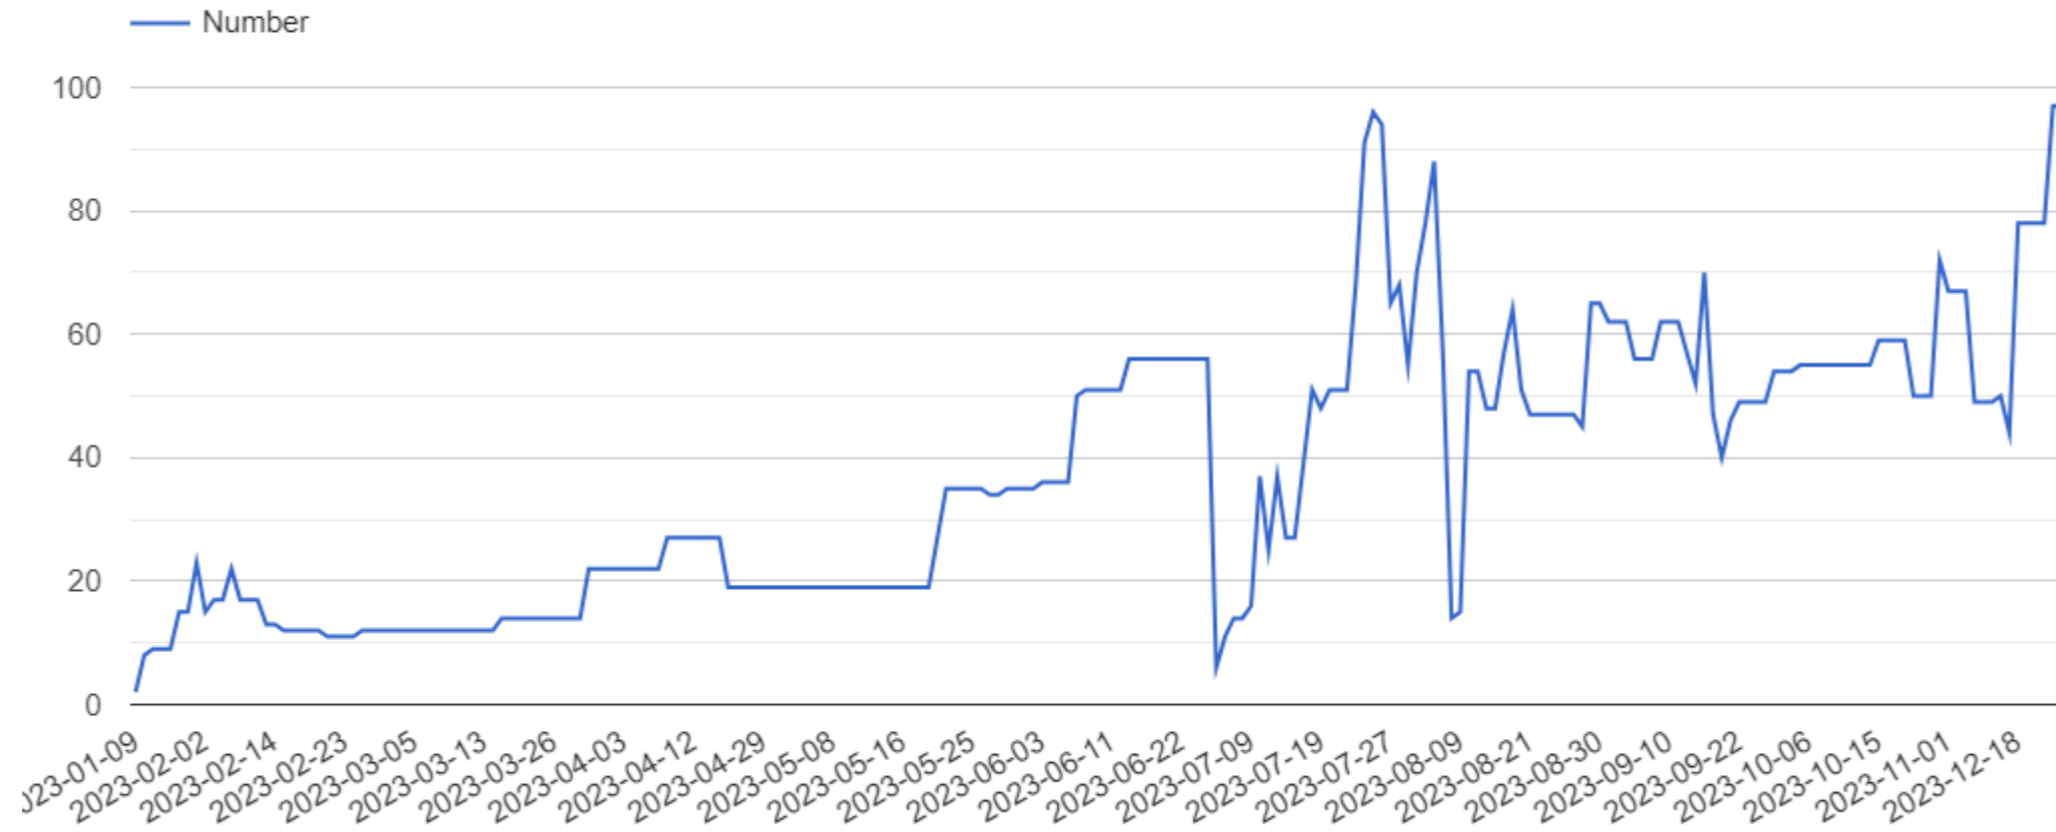


CUMMULATIVE ACTUAL WORK PROGRESS

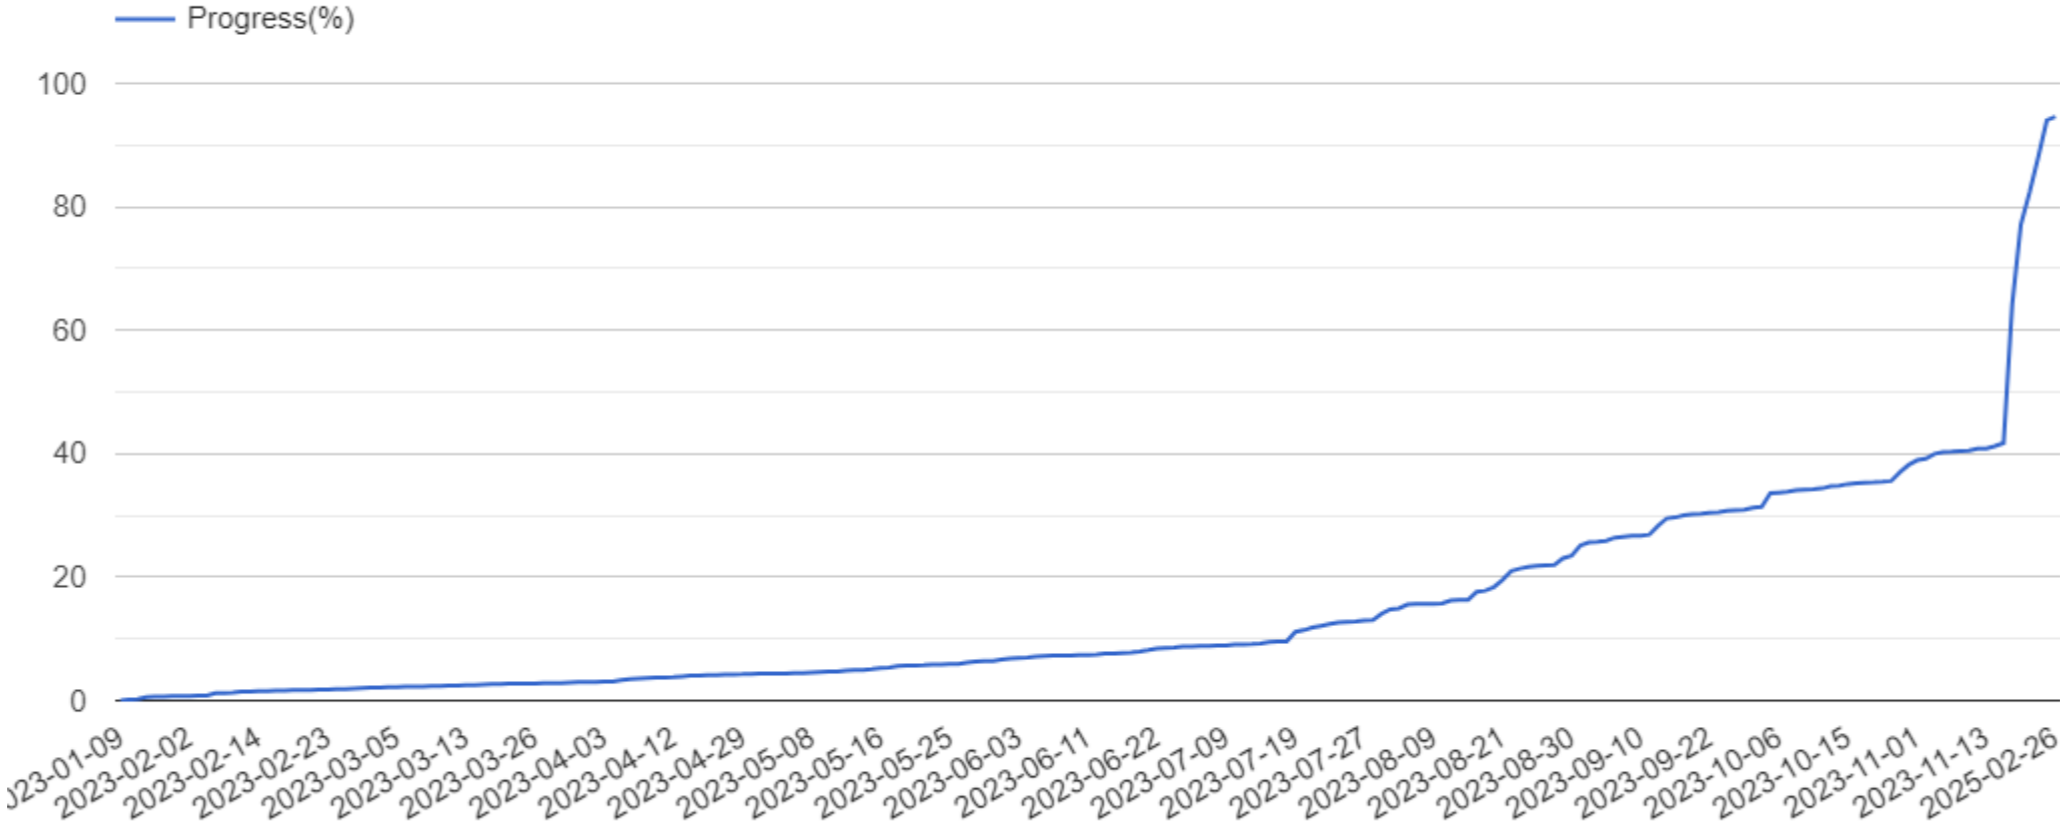


CUMMULATIVE PLAN WORK PROGRESS

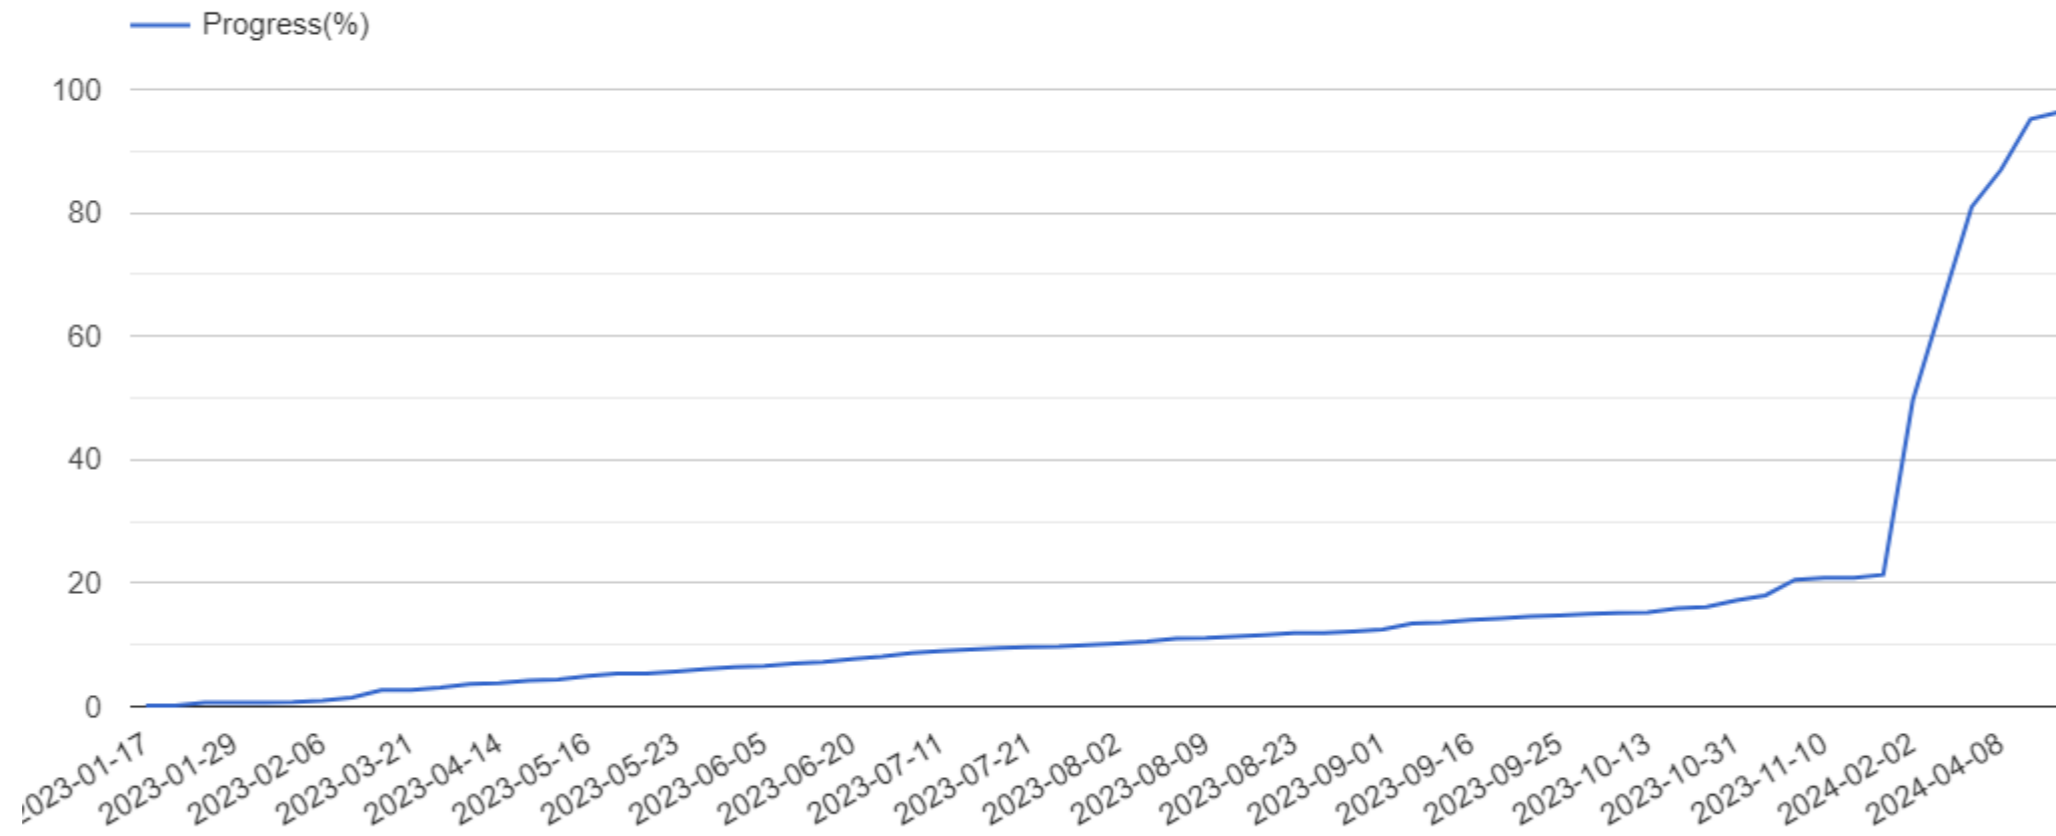

CUMMULATIVE WORK PROGRESS

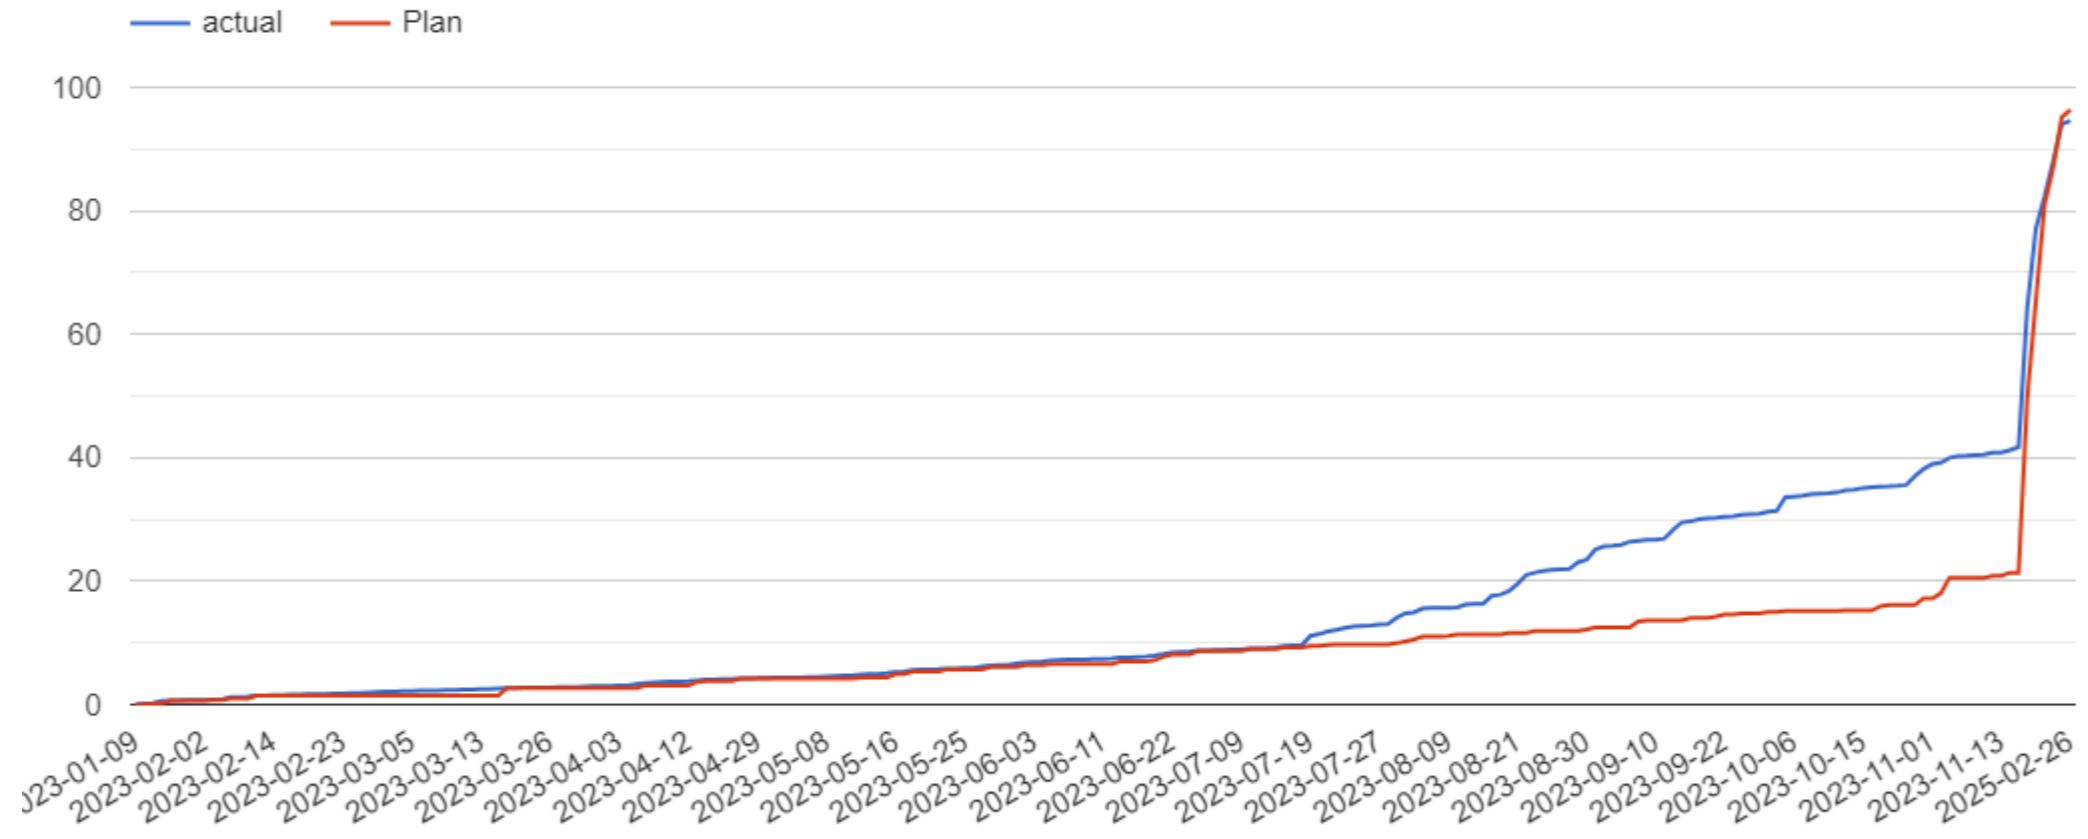

SCHEDULE AHEAD-BEHIND

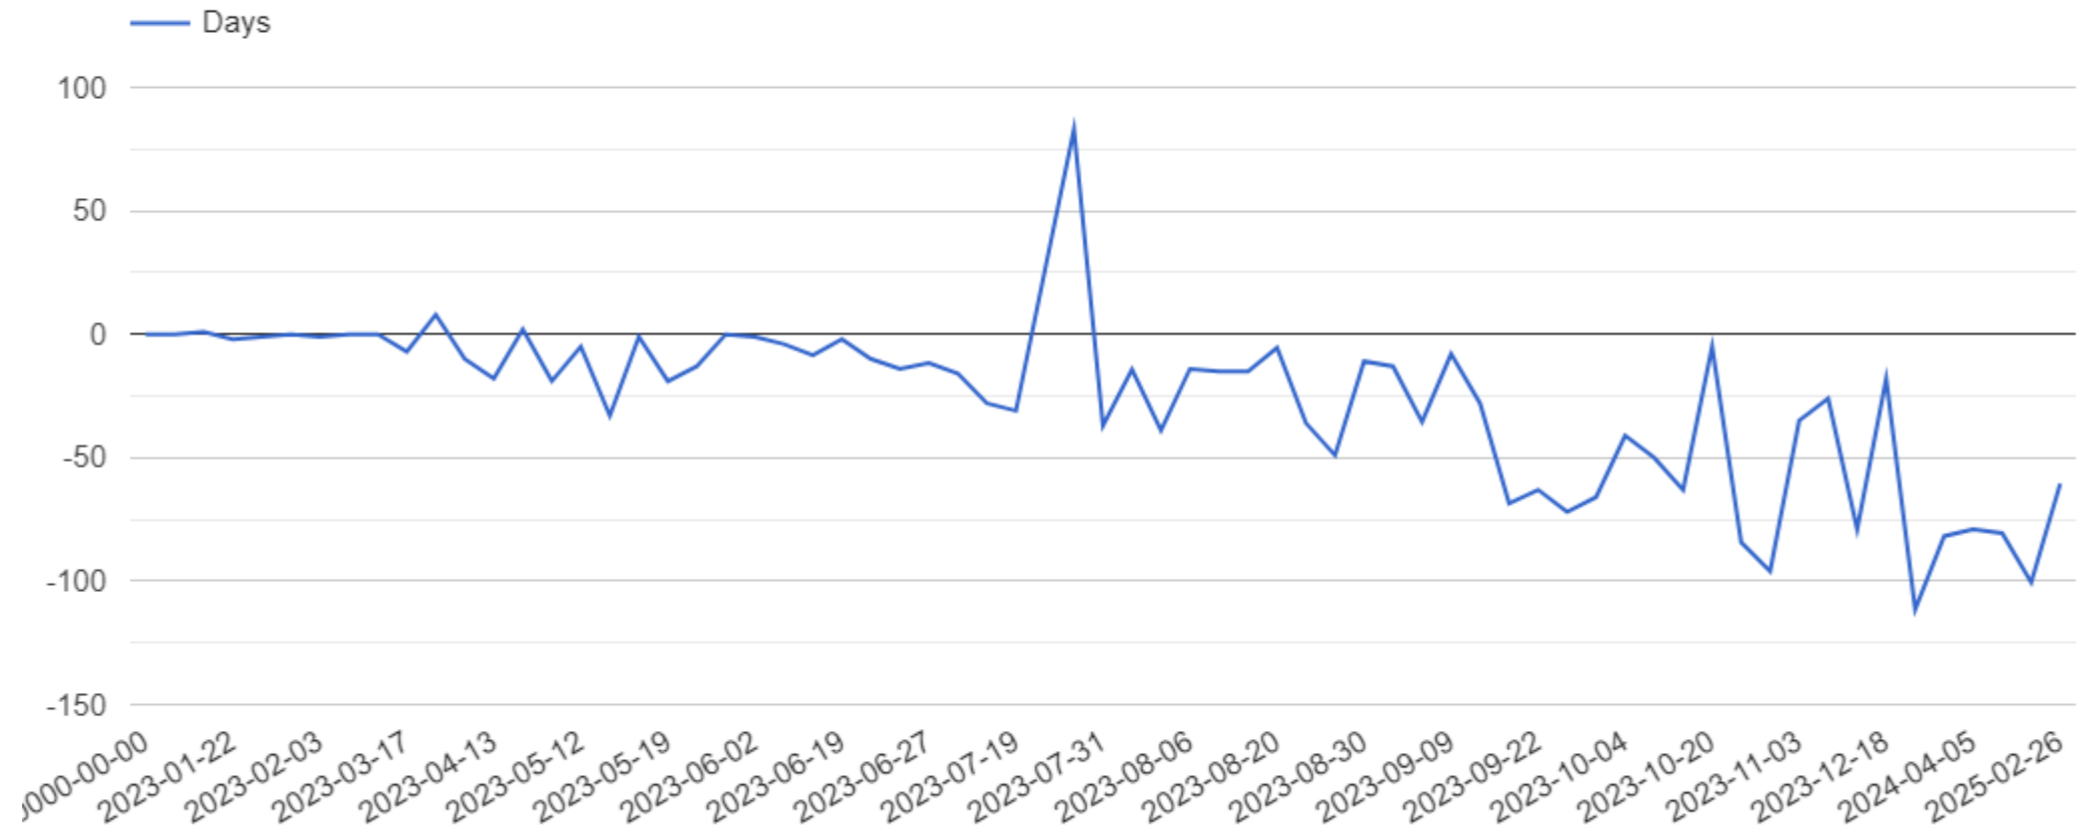

MONTHLY REPORT
DAILY REPORT



MONTHLY PROGRESS REPORT

From 1-April-2024 to 23-April-2024

Project Code:	21	Name:	New Hope Animal Nutrition Plant Bogura					
Client:	New Hope		Contractor:	Sarker Steel Ltd.				


Monthly Progress

WBS	Task	Total Qty	Upto Last Month(%)	This Month(%)	Total Done(%)	Schedule Start	Schedule Finish	Actual Finish
3.2.5.2.8	Dormitory-1st Floor-False Ceiling-Partit	sum	0	100	100	29-12-23	04-01-24	26-02-24
3.2.5.3.1	Dormitory-2nd Floor-Brickwork	111m2	0	100	100	08-01-24	17-01-24	23-04-24
3.2.5.3.2	Dormitory-2nd Floor-Door Frame fixing	0nos	0	100	100	18-01-24	20-01-24	23-04-24
3.2.5.3.3	Dormitory-2nd Floor-Window Grill Fixing	0nos	0	100	100	18-01-24	20-01-24	23-04-24
3.2.5.3.4	Dormitory-2nd Floor-Inside Plastering	468m2	0	100	100	12-01-24	21-01-24	23-04-24
3.2.5.3.5	Dormitory-2nd Floor-Tiles Fitting	0m2	0	100	100	20-01-24	28-01-24	23-04-24
3.2.5.3.6	Dormitory-2nd Floor-Door-Window fixing	0nos	0	95	95	27-01-24	29-01-24	23-04-24
3.2.5.3.7	Dormitory-2nd Floor-Inside Painting	m2	0	30	30	18-01-24	31-01-24	23-04-24
3.2.5.3.8	Dormitory-2nd Floor-False Ceiling-Partit		0	80	80	25-01-24	31-01-24	05-04-24
3.2.5.5	Dormitory-Outside Plastering	0m2	10	90	100	29-12-23	22-01-24	23-04-24
3.2.5.6	Dormitory-Waterproof-Rooftop		0	100	100	08-01-24	22-01-24	08-04-24
3.2.5.7	Dormitory-Outside Painting	m2	0	30	30	12-01-24	31-01-24	23-04-24
3.2.5.8	Dormitory-Stair Railing		0	100	100	25-01-24	31-01-24	23-04-24
3.2.6.3	Dormitory-2nd Floor-Water-Electrical	0	0	90	90	15-01-24	29-01-24	23-04-24
4.1	Road--Sub-grade Compaction	4817m2	75	25	100	11-07-23	03-01-24	05-04-24
4.2	Sub-base-Car Road-400m	4817m2	75	25	100	06-08-23	10-01-24	05-04-24
4.3	Road-Sub-base-Pedestrian	0m2	0	80	80	19-11-23	17-01-24	23-04-24
4.4	RCC-Car Road	4817m2	4	96	100	26-12-23	24-01-24	05-04-24


WBS	Task	Total Qty	Upto Last Month(%)	This Month(%)	Total Done(%)	Schedule Start	Schedule Finish	Actual Finish
6.1	Hydropower-Main Workshop	0	0	90	90	08-12-23	28-01-24	08-04-24
6.2	Production Buldg-Hydropower installation	1sum	0	90	90	18-12-23	28-01-24	08-04-24
6.4.2	Sub-station-Wall Electric Pipe Work	0m	0	100	100	16-12-23	23-12-23	08-04-24
6.4.3	Electrical Cable/Wiring	0m	0	100	100	23-12-23	22-01-24	08-04-24

MANPOWER HISTOGRAM

- Civil-Labor
- Civil-Mason/ Mistry
- Equipment Operator
- Other Labor
- Plumber/Electrician
- SSL-Labor-Night
- SSL-Mason/Mistry-Night
- SSL-Staff
- SSL-Tile Worker

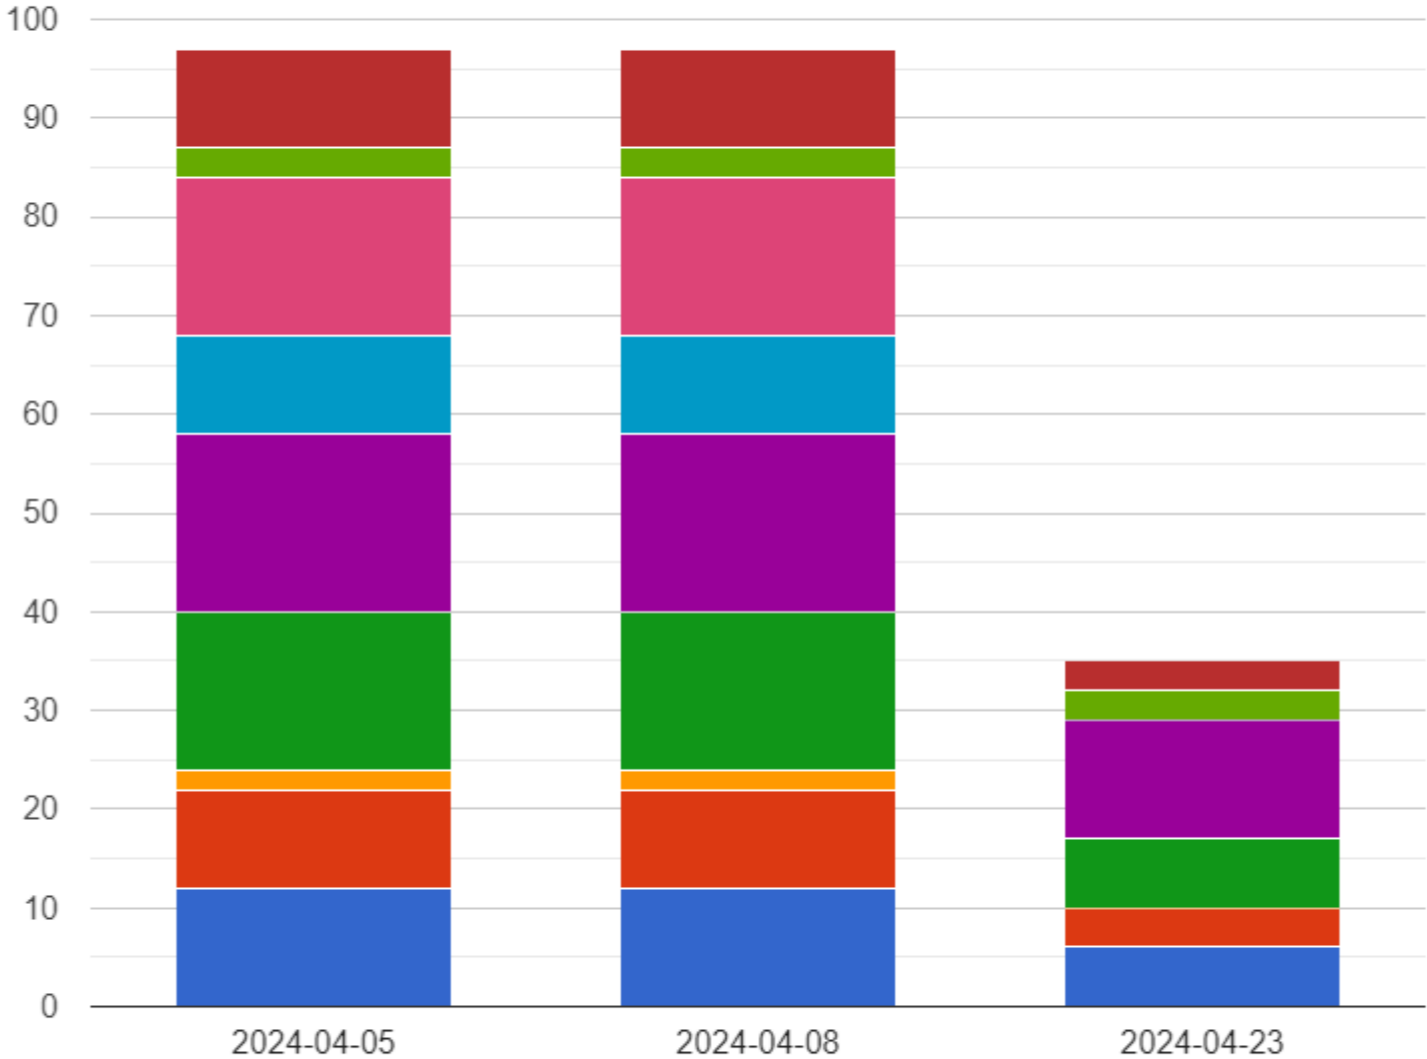

DAILY PROGRESS

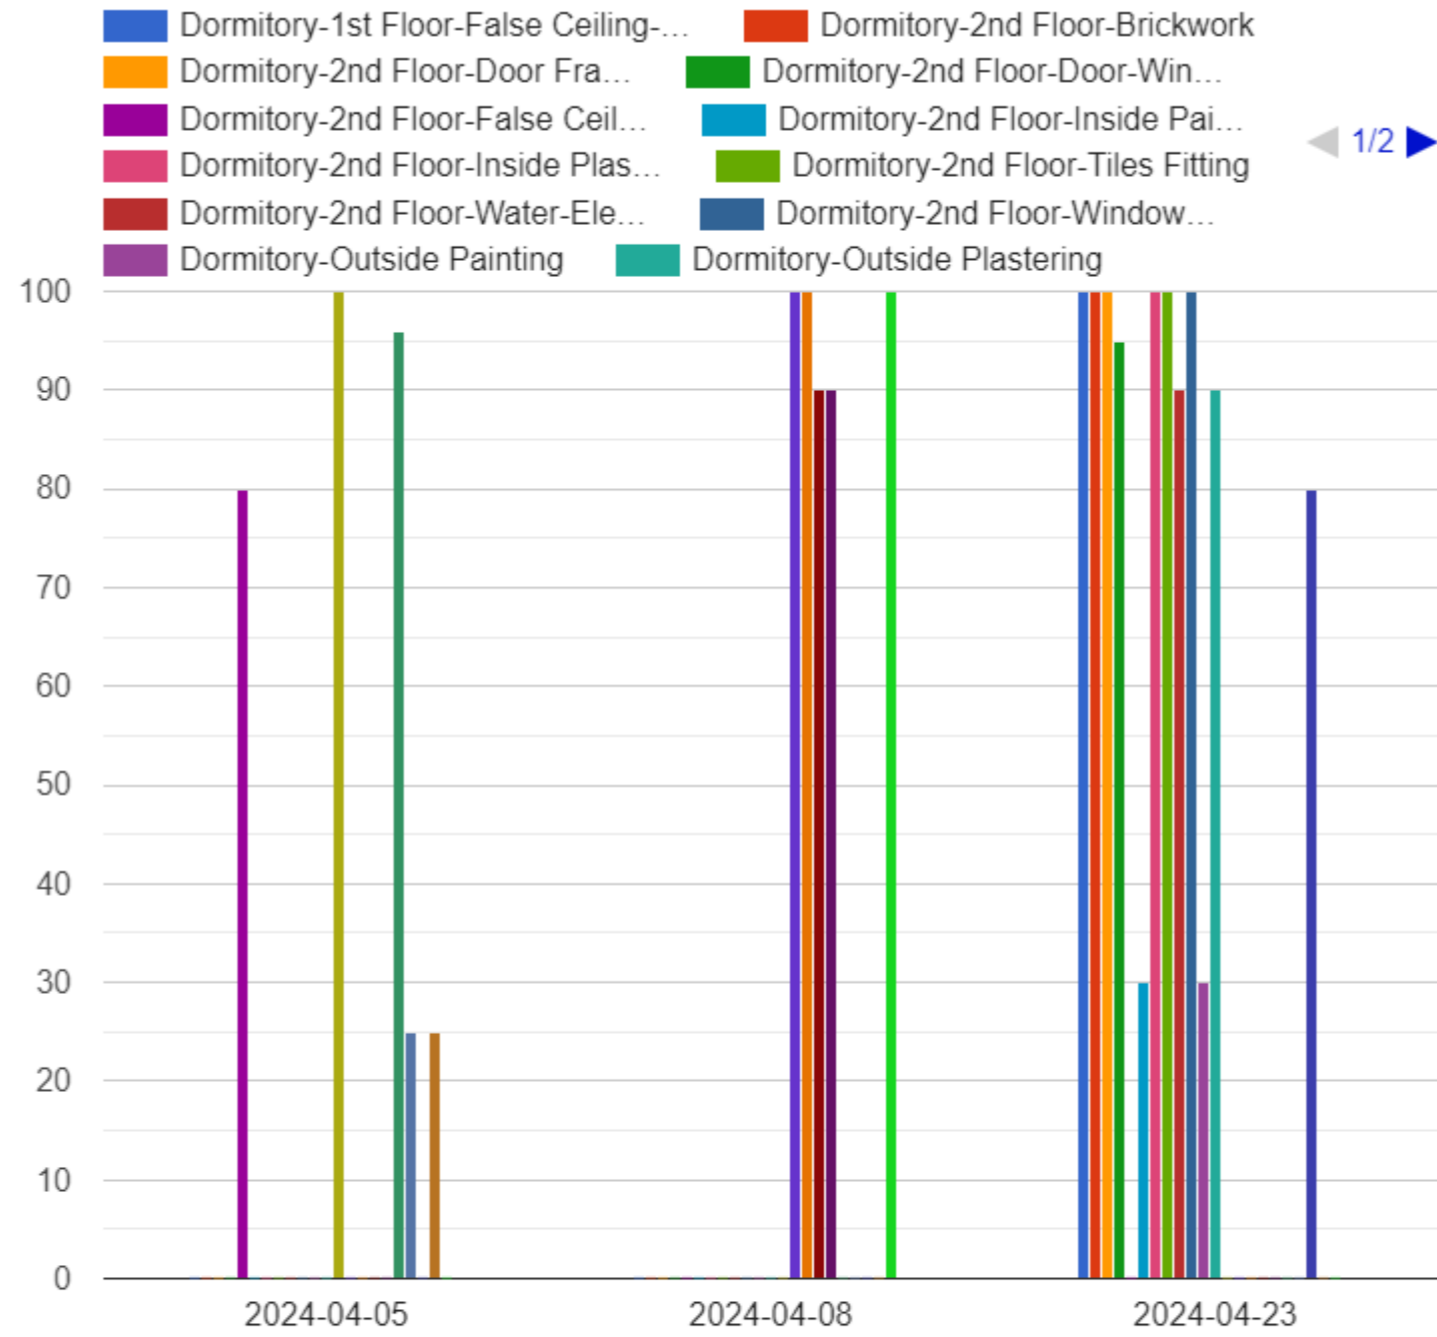



DAILY PROGRESS REPORT

Project:	New Hope Animal Nutrition Plant Bogura	Project Code:	21	Date:	23-April-2024
Client:	New Hope	Report	223	Day	Tuesday
Contractor:	Sarker Steel Ltd.			Climate	Sunny
					28-38C

Manpower

SN	Description	Nos.
01	SSL-Staff	3
02	Civil-Mason/ Mistry	4
03	Civil-Labor	6
05	Other Labor	7
08	Plumber/Electrician	12
10	SSL-Tile Worker	3
TOTAL		35

Progress This Day

WBS	Task	Total Qty	Today Done(%)	Total Done(%)	Schedule Start	Schedule Finish
3.2.5.2.8	Dormitory-1st Floor-False Ceiling-Partit	sum	100	100	29-12-23	04-01-24
3.2.5.3.1	Dormitory-2nd Floor-Brickwork	111m2	100	100	08-01-24	17-01-24
3.2.5.3.2	Dormitory-2nd Floor-Door Frame fixing	0nos	100	100	18-01-24	20-01-24
3.2.5.3.3	Dormitory-2nd Floor-Window Grill Fixing	0nos	100	100	18-01-24	20-01-24
3.2.5.3.4	Dormitory-2nd Floor-Inside Plastering	468m2	100	100	12-01-24	21-01-24
3.2.5.3.5	Dormitory-2nd Floor-Tiles Fitting	0m2	100	100	20-01-24	28-01-24
3.2.5.3.6	Dormitory-2nd Floor-Door-Window fixing	0nos	95	95	27-01-24	29-01-24
3.2.5.3.7	Dormitory-2nd Floor-Inside Painting	m2	30	30	18-01-24	31-01-24
3.2.5.5	Dormitory-Outside Plastering	0m2	90	100	29-12-23	22-01-24
3.2.5.7	Dormitory-Outside Painting	m2	30	30	12-01-24	31-01-24
3.2.6.3	Dormitory-2nd Floor-Water-Electrical	0	90	90	15-01-24	29-01-24
4.3	Road-Sub-base-Pedestrian	0m2	80	80	19-11-23	17-01-24

Site Photographs



Dormitory-2nd Floor Painting

Dormitor-2nd Floor-Corridor

Site Description	
Project closed from 09 to 16 April, 2024 due to Eid-ul Fitre	
Site Instruction	
Entry by:	Generated by:
Planning Engineer	www.bel3c.com, Developed by: Engr. Md. Sanaul Haque

WORK PLAN AND PROGRESS

Work Plan(Rev-2.0) and Progress for Construction of 150,000 Tons Livestock and Poultry Feed Factory in Bogura, Rajshahi, Bangladesh



WBS	Task Name	Duration	Start	Finish	% Complete	2023																
						Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr
1.3.2.4.1.3.3	Electrical Pipe Fixing	3 d	23/07/23	25/07/23	100%																	
1.3.2.4.1.3.4	Concreting	1 d	26/07/23	26/07/23	100%																	
1.3.2.4.2	1st Floor	20 d	13/08/23	01/09/23	100%																	
1.3.2.4.2.1	Column	7 d	13/08/23	19/08/23	100%																	
1.3.2.4.2.2	Stair Case	20 d	13/08/23	01/09/23	100%																	
1.3.2.4.2.2.1	1st Flight	7 d	13/08/23	19/08/23	100%																	
1.3.2.4.2.2.2	2nd Flight	7 d	26/08/23	01/09/23	100%																	
1.3.2.4.2.3	Roof Beam-Slab	13 d	20/08/23	01/09/23	100%																	
1.3.2.4.2.3.1	Formwork	8 d	20/08/23	27/08/23	100%																	
1.3.2.4.2.3.2	Re-bar Work	5 d	28/08/23	01/09/23	100%																	
1.3.2.4.2.3.3	Electrical Pipe Fixing	2 d	31/08/23	01/09/23	100%																	
1.3.2.4.2.3.4	Concreting	1 d	01/09/23	01/09/23	100%																	
1.3.2.4.3	2nd Floor	98 d	04/09/23	10/12/23	100%																	
1.3.2.4.3.1	Column	60 d	04/09/23	02/11/23	100%																	
1.3.2.4.3.2	Stair Case	45 d	27/10/23	10/12/23	100%																	
1.3.2.4.3.2.1	1st Flight	7 d	27/10/23	02/11/23	100%																	
1.3.2.4.3.2.2	2nd Flight	7 d	04/12/23	10/12/23	100%																	
1.3.2.4.3.3	Roof Beam-Slab	38 d	03/11/23	10/12/23	100%																	
1.3.2.4.3.3.1	Formwork	8 d	03/11/23	10/11/23	100%																	
1.3.2.4.3.3.2	Re-bar Work	5 d	06/12/23	10/12/23	100%																	
1.3.2.4.3.3.3	Electrical Pipe Fixing	2 d	09/12/23	10/12/23	100%																	
1.3.2.4.3.3.4	Concreting	1 d	10/12/23	10/12/23	100%																	
1.3.2.5	Masonry and Finishing Work	185 d	31/07/23	31/01/24	91%																	
1.3.2.5.1	Ground Floor	143 d	31/07/23	20/12/23	100%																	
1.3.2.5.1.1	Brick Work	17 d	31/07/23	16/08/23	100%																	
1.3.2.5.1.2	Door Frame Fixing	7 d	11/12/23	17/12/23	100%																	
1.3.2.5.1.3	Window Grill Fixing	7 d	11/12/23	17/12/23	100%																	
1.3.2.5.1.4	Plaster Work	5 d	16/08/23	20/08/23	100%																	
1.3.2.5.1.5	Khoa-sand Cushion in Floor	5 d	16/08/23	20/08/23	100%																	
1.3.2.5.1.6	Floor Concreting	6 d	16/08/23	21/08/23	100%																	
1.3.2.5.1.7	Tiles Fitting	15 d	05/12/23	19/12/23	100%																	
1.3.2.5.1.8	Door shutter and Window fixing	3 d	18/12/23	20/12/23	100%																	
1.3.2.5.1.9	Inside Painting	15 d	06/12/23	20/12/23	100%																	
1.3.2.5.2	1st Floor	88 d	09/10/23	04/01/24	100%																	
1.3.2.5.2.1	Brick Work	7 d	09/10/23	15/10/23	100%																	
1.3.2.5.2.2	Door Frame Fixing	3 d	18/12/23	20/12/23	100%																	
1.3.2.5.2.3	Window Grill Fixing	3 d	18/12/23	20/12/23	100%																	
1.3.2.5.2.4	Plaster Work	5 d	15/10/23	21/12/23	100%																	
1.3.2.5.2.5	Tiles Fitting	15 d	20/12/23	03/01/24	100%																	
1.3.2.5.2.6	Door shutter and Window fixing	3 d	02/01/24	04/01/24	100%																	
1.3.2.5.2.7	Inside Painting	15 d	21/12/23	04/01/24	100%																	
1.3.2.5.2.8	False Ceiling and Toilet Partition	7 d	29/12/23	04/01/24	100%																	
1.3.2.5.3	2nd Floor	24 d	08/01/24	31/01/24	81%																	
1.3.2.5.3.1	Brick Work	10 d	08/01/24	17/01/24	100%																	
1.3.2.5.3.2	Door Frame Fixing	3 d	18/01/24	20/01/24	100%																	
1.3.2.5.3.3	Window Grill Fixing	3 d	18/01/24	20/01/24	100%																	
1.3.2.5.3.4	Inside Plaster Work	10 d	12/01/24	21/01/24	100%																	
1.3.2.5.3.5	Tiles Fitting	9 d	20/01/24	28/01/24	100%																	
1.3.2.5.3.6	Door shutter and Window fixing	3 d	27/01/24	29/01/24	95%																	
1.3.2.5.3.7	Inside Painting	14 d	18/01/24	31/01/24	30%																	

Task Progress Rolled Up Task Rolled Up Progress Group By Summary

Critical Task Summary Rolled Up Critical Task Project Summary

PROGRESS PHOTO

Site Photographs



Brick un-loading on 09-01-23



Brick mobilized for shed on 09-01-23



Unloading Materials on 14-01-23



Materials for Shed on 14-01-23



Shed making on 17-01-23



shed making on 17-01-23



Re-bar mobilized on 21-01-23



Re-bar mobilized on 21-01-23



Shed completed on 22-01-23



Shed completed on 22-01-23



Piling Rig mobilized on 29-01-23



Piling Rig Mobilized on 29-01-23



Electrical DB Setting on 31-01-23



Pile Rig Installing on 31-01-23



Pile Point Layout and Survey on 01-02-23



Deep tube well sinking on 01-02-23



Exaction for Pile mud tank on 02-02-23



Pile re-bar spacer block making on 02-02-23



Pile Rig setting on 03-02-23



Excavation for Pile Mud Tank on 03-02-23



Brick-work around Pile point on 05-02-23



Pile Re-bar Work on 05-02-23



Electricity Connection on 06-02-23



Mud Tank making on 06-02-23



Mud Tank-1 Completed on 08-02-23



Inspection before Pile driving on 08-02-23



Pile Driving Starting on 09-02-23



Pile Concreting on 09-02-23



Mud Tank-2 Completed on 12-02-23



Pile Re-bar Work on 12-02-23



Pile boring work on 13-02-23



Ready mix concreting of pile on 13-02-23



Pile boring work on 14-02-23



Ready mix concreting of pile on 14-02-23



Pile boring work-CB(5+2) out of 69 nos p on 15-02-23



Ready mix concreting of pile on 15-02-23



Com. Bldg. 9th pile boring on 16-02-23



Ready mix concreting of pile on 16-02-23



Com. Bldg. 12th pile boring on 17-02-23



Ready mix concreting of pile on 17-02-23



Com. Bldg. 14th pile boring on 18-02-23



Ready mix concreting of pile on 18-02-23



Com. Bldg. 15th pile boring on 19-02-23



Ready mix concreting of pile on 19-02-23



Com. Bldg. 17th Pile Boring on 21-02-23



Ready mix concreting of pile on 21-02-23

Yesterday no pile bored due to RMC non-availability

BBS no operator, Farida plant disturbed



Com. Bldg. 20th Pile Boring on 22-02-23



Ready mix concreting of pilewort on 22-02-23



Com. Bldg. 22nd pile boring on 23-02-23



Ready mix concreting of pile on 23-02-23



Com. Bldg. 24th pile boring on 24-02-23



Ready mix concreting of pile on 24-02-23



Com. Bldg. 27th pile boring on 25-02-23



Ready mix concreting of pile on 25-02-23



Com. Bldg. 30th pile boring on 26-02-23



Ready mix concreting of pile on 26-02-23



Com. Bldg. 33 pile boring on 27-02-23



Ready mix concreting of pile on 27-02-23



Com. Bldg. 36 Pile Boring on 28-02-23



Ready mix concreting of pile on 28-02-23



Com. Bldg. 39 pile boring on 02-03-23



Ready mix concreting of pile on 02-03-23



Com. Bldg. 41 Pile Boring on 03-03-23



Ready mix concreting of pile on 03-03-23



Com. Bldg. 44 pile boring on 05-03-23



Ready mix concreting of pile on 05-03-23



Com. Bldg. 45 Pile Boring on 06-03-23



Re-bar arrived at site on 06-03-23

Today Less pile bored due to winch m/c. Problem.



Com. Bldg. 46 Pile Boring on 07-03-23



Ready mix concreting of pile on 07-03-23



Com. Bldg. 49 Pile Boring on 08-03-23



Ready mix concreting of pile on 08-03-23



Com. Bldg. 50 Pile Boring on 09-03-23



Ready mix concreting of pile on 09-03-23



Com. Bldg. 52 Pile Boring on 10-03-23



Ready mix concreting of pile on 10-03-23



Com. Bldg. 55 pile boring on 11-03-23



Ready mix concreting of pile on 11-03-23



Com. Bldg. 57 Pile Boring on 12-03-23



Ready mix concreting of pile on 12-03-23



Com. Bldg. 60 Pile Boring on 13-03-23



Ready mix concreting of pile on 13-03-23



Com. Bldg. 63 Pile Boring on 14-03-23



Ready mix concreting of pile on 14-03-23



Com. Bldg. 66 Pile Boring on 16-03-23



Ready mix concreting of pile on 16-03-23

Yesterday no pile driving due to RMC supplier payment



Com. Bldg. 69 Pile Boring on 17-03-23



Ready mix concreting of pile on 17-03-23



Guard House 2nd pile Boring on 19-03-23



Guard House pile concreting by RMC on 19-03-23



Guard House 6th pile Boring on 21-03-23



Ready mix concreting of pile on 21-03-23



Earth cutting for Pile head breaking on 24-03-23



Pile head breaking on 24-03-23



Cantg. Dor. Bldg. 2nd pile boring on 25-03-23



Ready mix concreting of pile on 25-03-23



Dorm. Bldg. 4th pile boring on 26-03-23



Ready mix concreting of pile on 26-03-23



Pile head breaking on 27-03-23



Pile cap earth cutting on 27-03-23



Earth cutting for Pile head breaking on 28-03-23



Pile head breaking on 28-03-23



Dorm. Bldg. 7th pile boring on 29-03-23



MD Sir went to bogura for NH site visit on 29-03-23



Earth cutting and pile head breaking on 30-03-23



Dorm. Bldg. 10th pile concreting on 30-03-23



Dorm. Bldg. 12th pile boring on 31-03-23



Ready mix concreting of pile on 31-03-23



Dorm. Bldg. 14th pile boring on 01-04-23



Ready mix concreting of pile on 01-04-23



Dorm. Bldg. 16th pile boring on 02-04-23



Ready mix concreting of pile on 02-04-23



Dorm. Bldg. 17th pile concreting on 03-04-23



Pile head finishing for test on 03-04-23



Pile cap cc work on 04-04-23



Pile cap bottom cc casting. on 04-04-23



Dorm. Bldg. 19th pile concreting on 05-04-23



Pile cap CC work on 05-04-23



Pile cap cc complete of com. Bldg. on 06-04-23



Dorm. Bldg. 22nd pile casting on 06-04-23



Dorm. Bldg. 26th pile concreting on 07-04-23



Pile head finishing for test on 07-04-23



Dorm. Bldg. 30th pile boring on 08-04-23



Ready mix concreting of pile on 08-04-23



Com. Bldg. Pile Rebar work on 09-04-23



Dorm. Bldg. 32nd pile concreting on 09-04-23



Dorm. Bldg. 34th pile concreting on 10-04-23



Com. Bldg. Pile cap work on 10-04-23



Dorm. Bldg. 37th pile boring on 12-04-23



Ready mix concreting on 12-04-23



Com. Bldg. Pile cap casting on 13-04-23



Dorm. Bldg 38th pile casting on 13-04-23

pile test finish

Dorm. Bldg pile work finish



Pile cap work on 14-04-23



Pile cap rebar work on 14-04-23



Pile Cap rebar binding on 15-04-23



Pile Cap concreting. on 15-04-23



Comp. Bldg. Pile cap casting on 16-04-23



Pile Cap concreting. on 16-04-23



Pile cap casting on 17-04-23



Com. Bldg. Pile cap casting on 17-04-23



Pile cap concreting on 18-04-23



Com. Bldg. 20th pile cap casting complet on 18-04-23



Comp. Bldg. Back filling on 19-04-23



Back filling and levelling dressing. on 19-04-23



C.C work at GB Bottom of comp. Bldg. on 29-04-23



Comp. Bldg. C.C concreting on 29-04-23

19-28 April work stopped due to Eid Vacation



Comp. Bldg. CC casting at GB Bottom on 30-04-23



C.C concreting on 30-04-23



Dorm. Bldg. Earth cutting for PH Breakin on 02-05-23



Comp. Bldg. C.C concreting on 02-05-23

Yesterday work stopped due to May day



Comp. Bldg. GB Re-bar work on 03-05-23



GB Re-bar work on 03-05-23



Re-bar work for GB of comp. Bldg. on 04-05-23



GB Re-bar work on 04-05-23



Comp. Bldg. GB Re-bar work on 05-05-23



MD Sir visit to site on 05-05-23



Comp. GB Shuttering on 06-05-23



Earth cutting for dorm. Bldg. on 06-05-23



Dorm. Bldg. Pile head breaking on 07-05-23



Comp. GB Shuttering on 07-05-23



Comp. Bldg. GB Shuttering work on 08-05-23



Gate pile Cap cc work on 08-05-23



G. House Pile cap work on 09-05-23



Pile head finishing for test on 09-05-23



Dorm. Bldg. pile head breaking on 10-05-23



Pile head breaking on 10-05-23



Pile cap bottom cc work of Dorm. Bldg on 11-05-23



Pile cap CC work on 11-05-23



Comp. Bldg. GB casting work on 12-05-23



Gate house pile cap casting on 12-05-23



Com. GB Shuttering on 13-05-23



Re-bar work on 13-05-23



Comp. Bldg. GB Shuttering work on 14-05-23



GB Shuttering work on 14-05-23



Dorm Bldg pile head breaking on 15-05-23



Com Bldg GB Shuttering on 15-05-23



Comp. Bldg. GB casting work on 16-05-23



GB Concreting on 16-05-23



Dorm Bldg pile cap bottom cc casting on 17-05-23



CC Casting on 17-05-23



Guard House GB Casting on 18-05-23



GB Casting on 18-05-23



Pile load test on 19-05-23



Pile integrity test on 19-05-23



Civil worker on 21-05-23



Sand filling on 21-05-23



Civil worker on 22-05-23



Dorm. Bldg. Pile cap rebar binding on 22-05-23



Dorm Bldg pile cap rebar binding on 23-05-23



Pile cap rebar work on 23-05-23



Comp. Bldg. Column shuttering on 24-05-23



Dorm. Bldg. Pile cap rebar binding on 24-05-23



Dorm. Bldg pile cap work on 25-05-23



Comp. Bldg column work on 25-05-23



Dorm. Bldg pile cap work on 26-05-23



Comp. Bldg column shuttering on 26-05-23



Dorm. Bldg pile cap casting on 28-05-23



Comp. Bldg column casting on 28-05-23



Dorm. Bldg. pile cap casting on 29-05-23



Pile Cap concreting. on 29-05-23



Comp. Bldg. Column casting on 30-05-23



Gate house Brick work on 30-05-23



Civil worker on 31-05-23



Comp. Bldg. Column shutter on 31-05-23



Comp. Bldg. Slab beam line shuttering on 01-06-23



Gate house Brick work on 01-06-23



Comp. Bldg. Stair shuttering on 02-06-23



Gate house Brick work on 02-06-23

Due to RMC plant disturbed Comp bldg column could not finish yesterday



Comp. Bldg. Slab beam line shuttering on 03-06-23



Dorm. Bldg. GB Bottom CC work on 03-06-23



Comp. Bldg. Slab beam line shuttering on 04-06-23



Dorm. Bldg. Rebar work for GB on 04-06-23



Comp. Bldg. Slab beam shuttering on 05-06-23



1st flight stair casting on 05-06-23



Comp. Bldg. Slab and beam shuttering on 06-06-23



Gate house Brick work on 06-06-23



Dorm. Bldg GB Rebar work on 07-06-23



Comp. Bldg. Slab beam shuttering on 07-06-23



Comp. Bldg. Slab and beam shuttering on 08-06-23



Dorm. GB work on 08-06-23



Comp. Bldg. Slab beam shuttering on 09-06-23



Dorm. Bldg. GB shuttering on 09-06-23



Dorm. Bldg GB shutter and rebar work on 10-06-23



Comp. Bldg. Slab beam shuttering on 10-06-23



Comp. Bldg. Slab beam shuttering on 11-06-23



Comp. Bldg. Rebar work on 11-06-23



Comp. Bldg. Slab beam shuttering on 12-06-23



Dorm. Bldg. GB shuttering on 12-06-23



Dorm. Bldg. GB Casting on 13-06-23



Round column New steel
shutter Making (12ft
long) for office building
porch column

Com. Bldg. Slab shuttering on 13-06-23



Comp. Bldg. Slab beam shuttering on 15-06-23



Gate house work on 15-06-23



Comp. Bldg. Slab beam shuttering and Reb on 16-06-23



Gate house column shuttering work on 16-06-23



Gate House column casting on 18-06-23



Dorm. Bldg. Column casting on 18-06-23



Comp. Bldg. Slab beam shuttering and rod on 19-06-23



Gate house work on 19-06-23



Comp. Bldg. Slab shuttering and Rod bind on 20-06-23



Dorm. Bldg. Column casting on 20-06-23



Comp. Bldg. Slab Ready for Concrete on 22-06-23



Comp. Bldg. Slab shutter and Rebar work on 22-06-23



Dorm. Bldg. Column Casting on 23-06-23



Gate House Lintel casting on 23-06-23



Gate House Slab shuttering and rod bindi on 25-06-23



Gate House work on 25-06-23



Com. Bldg. 1st floor slab casting on 27-06-23



Comp. Bldg. Slab casting complete on 27-06-23



Comp. Bldg. 1st floor column Rebar work on 04-07-23



Gate House work on 04-07-23

Project was closed 6 days due to Eid vacation



Comp Bldg-1st floor Column Re-bar work on 06-07-23



Comp Bldg-1st floor Column Re-bar work on 06-07-23



Comp. Bldg. 1st floor column work on 07-07-23



Comp. Bldg. 1st floor column rebar work on 07-07-23



Civil Manpower on 08-07-23



shutter opening on 08-07-23



Civil worker on 09-07-23



Shuttering work on 09-07-23



Gate House Slab casting on 11-07-23



Gate House Slab Casting complete on 11-07-23



Comp. Bldg. Slab shutter opening on 12-07-23



Comp. Bldg. 1st floor column casting on 12-07-23



Comp. Bldg. 1st floor column work on 13-07-23



Comp. Bldg 1st floor column casting on 13-07-23



Comp. Bldg. 1st floor column work on 14-07-23



Comp. Bldg 1st floor roof slab work on 14-07-23



Comp. Bldg. 1st flight stair casting on 16-07-23



Comp. Bldg 2nd floor shuttering on 16-07-23



Comp. Bldg. Slab beam shuttering on 17-07-23



Comp. Bldg. 2nd floor Slab beam shutteri on 17-07-23



Comp. Bldg. 2nd Floor Slab beam shutteri on 18-07-23



Dorm. Bldg. Sand filling on 18-07-23



Materials arrive at site for road on 19-07-23



Comp. Bldg. 2nd floor slab shuttering wo on 19-07-23



Dorm. Bldg. Floor levelling work on 20-07-23



Comp. Bldg. 2nd Slab beam shuttering on 20-07-23



Comp. Bldg. 2nd Floor Slab beam shuttering on 21-07-23



Comp. Bldg. GF Brick work on 21-07-23



BBS, Substation Roof
slab electric pipe conduit
working.

Sub-station-Electrical Pipe Work on 22-07-23



Road Sub-base work on 22-07-23

Substation Roof Slab Electrical pipe work delayed due to BBS not completed slab shuttering and re-bar work



Civil Manpower on 23-07-23



Road Sub-base work on 23-07-23



Dorm. Bldg. 1st floor shuttering work on 24-07-23



Comp. Bldg GF Brick work on 24-07-23



Comp. Bldg. on 25-07-23



Dormitory Bldg. on 25-07-23



Dorm. Bldg. 1st flight stair on 26-07-23



Comp. Bldg. 2nd floor work on 26-07-23



Foundation brick work at scale station on 27-07-23



Dorm. Bldg shuttering work on 27-07-23



Comp. Bldg. 2nd Floor rebar work on 28-07-23



Dorm. Bldg shuttering work on 28-07-23



Comp. Bldg Rebar work on 31-07-23



Road work on 31-07-23

Gate House Handover



Rebar binding of Scale on 02-08-23



Tie column work at brick wall on 02-08-23



Comp. 2nd floor slab concreting on 04-08-23



Comp. Bldg. concreting work complete on 04-08-23

Casting start on 04-08-2023 5:30PM and finish on 05-08-2023 5:02AM



Comp.Bldg GF Brick work on 06-08-23



Dormitory 1st Floor Re-bar work on 06-08-23



Comp-GF-Brick Work on 07-08-23



Due to Rain no work on 07-08-23

Due to Rain no work afternoon and night



No work due to rain on 08-08-23



Dormitory Slab Electrical Pipe Laying on 08-08-23



Dormitory Slab Electric Pipe Laying on 09-08-23



Comp.Bldg.GF Brick work on 09-08-23

Dormitory Slab Concreting not possible due to rain



Dormitory GF Stair 2nd flight concrete c on 10-08-23



Dormitory 1st Floor Slab concrete comple on 10-08-23



Weighing bridge re-bar work on 11-08-23



Road Sub-base work on 11-08-23



Comp-Parapet Brick-work on 14-08-23



Sub-base-Khoa unloading on 14-08-23



Comp-GF Column Concreting on 16-08-23



Road-Excavation-box cutting on 16-08-23

Project was closed on 15 Aug due to National Mourning day.



Sub-base Compaction on 17-08-23



Comp-Parapet Brick-work on 17-08-23



Comp-GF Brickwork on 18-08-23



Road-Sub-basework on 18-08-23



Comp-1st Floor-Shutter Removing on 20-08-23



Gate House-Door Frame Fixing on 20-08-23



Material stock for Road Sub-base on 21-08-23



Road-Sub-base work on 21-08-23



Comp-1st Floor-Brickwork on 22-08-23



Road-Box cutting on 22-08-23



Weighing Bridge Concreting on 23-08-23



Dormitory Column Concreting on 23-08-23



Comp. Bldg. 1st floor brick wall on 24-08-23



Road work on 24-08-23



Dormitory column casting on 25-08-23



Column casting work on 25-08-23



Comp. Bldg plaster work on 26-08-23



Dormitory bldg. Column casting on 26-08-23



Comp. Bldg Column casting on 27-08-23



Comp. Bldg. GF plaster work on 27-08-23



Comp. Bldg. Sanitary work on 29-08-23



Dorm. Bldg. 2nd floor shuttering on 29-08-23



Dorm. Bldg. 1st flight stair casting on 30-08-23



Road Sub-base work on 30-08-23



Gate House floor casting on 01-09-23



Road Sub-base work on 01-09-23



Dorm. Bldg. 2nd floor shuttering work on 03-09-23



Road work on 03-09-23



Comp. Bldg. 1st floor brick wall on 04-09-23



Dorm. Bldg. 2nd floor Shuttering work on 04-09-23



Dorm. Bldg. 2nd floor shuttering work on 06-09-23



Anchor bolt fitting at scale on 06-09-23



Dorm. Bldg. 2nd floor Rebar work on 07-09-23



Comp. Bldg 1st floor sanitary work on 07-09-23



Dorm. Bldg. 2nd floor rebar work on 08-09-23



Road Sub-base work on 08-09-23



Dorm. Bldg. 2nd floor rebar work on 09-09-23



Comp. Bldg. FF Brick work on 09-09-23



Comp. Bldg. 2nd Floor work on 10-09-23



Comp. Bldg. FF Brick work on 10-09-23



Comp. Bldg. Plaster work on 11-09-23



Comp. Bldg floor GF compaction on 11-09-23



Dorm. Bldg. 1st floor brick work on 13-09-23



Road work on 13-09-23



Comp. Bldg work on 15-09-23



Comp. GF Cushion concreting on 15-09-23



Dorm. Bldg. 2nd floor concreting work on 16-09-23



Comp. Bldg. Roof top concreting work on 16-09-23



Comp. Bldg FF plastr wok on 19-09-23



GF cushion wok on 19-09-23



Comp. Bldg. Plaster work on 20-09-23



Dormitory GF-Brick Work on 20-09-23



Dorm. Bldg GF Brick work on 21-09-23



Comp. Bldg 1st fplaster work on 21-09-23



Dorm. Bldg GF Brick work on 22-09-23



Dorm. Brick work on 22-09-23



Dorm.Bldg. GF brick work on 23-09-23



Dorm.Bldg brick work on 23-09-23



Dorm.Bldg. GF brick work on 25-09-23



Dorm. Bldg Brick work on 25-09-23



Gats house files work on 26-09-23



Weight scale concreting on 26-09-23



Comp. Bldg outside scaffolding on 28-09-23



Earth cutting power cable laying on 28-09-23



Comp. GF concreting on 29-09-23



Comp. Bldg. GF casting on 29-09-23



Earth cutting Electric line on 01-10-23



Comp. Roof top parapet work on 01-10-23



Dorm. Stair room column shuttering on 04-10-23



Dorm. 1st floor brick work on 04-10-23



Dorm. Bldg. on 06-10-23



Dorm. Bldg. 1st floor brick work on 06-10-23



Dorm. 1st floor brick work on 07-10-23



Dorm. Bldg Brick work on 07-10-23



Comp. Bldg. Prepared for Out side plaste on 08-10-23



Dorm. Bldg. Roof top column casting on 08-10-23



Comp. Bldg. Outside plaster work on 09-10-23



Comp. Bldg. GF casting on 09-10-23



Dorm. Bldg. Brick work on 10-10-23



Comp. Bldg. Outside plaster work on 10-10-23



Comp. Bldg. Outside plaster work on 11-10-23



Road work on 11-10-23



Comp. Bldg. Outside plaster work on 13-10-23



Dorm. Bldg. Roof top Column work on 13-10-23



Road work on 14-10-23



Comp. Bldg. Outside plaster work on 14-10-23



Comp. Bldg. Outside plaster work on 15-10-23



Road work on 15-10-23



Comp. Bldg. Outside plaster work on 16-10-23



Comp. Bldg. GF casting on 16-10-23



Comp. Bldg. Outside plaster work on 18-10-23



Road casting work on 18-10-23



Comp. Building-Outside Plastering on 20-10-23



Comp. Building-Outside Plastering on 20-10-23



Dorm. Bldg. 2nd floor column work on 25-10-23



Ceiling plaster on 25-10-23



Comp. Bldg. Door shutter work on 26-10-23



Comp. Bldg. on 26-10-23



Dormitory-GF-Ceiling Plastering on 27-10-23



Electrical Cable Received on 27-10-23



Gate House door fixed on 31-10-23



PPR Pipe Received on 31-10-23



Dorm. Bldg. Ceiling Plaster on 01-11-23



Comp. Bldg. GF Tiles work on 01-11-23



Dorm. Bldg. 2nd floor concreting work on 02-11-23



Dorm. Bldg. Plaster work on 02-11-23



Dorm. Bldg. 2nd floor column work on 03-11-23



Power cable laying work on 03-11-23



Dorm. Bldg. 2nd floor shuttering work on 06-11-23



Sanitary group cutting on 06-11-23



Gate House Thai work on 07-11-23



Dormitory canopy on 07-11-23



Dorm. Bldg. 3rd floor slab shuttering on 08-11-23



Gate roof top water proofing casting on 08-11-23



Dorm. Bldg. 3rd floor shuttering work on 09-11-23



Dorm. Bldg. GF sand khoa cushion on 09-11-23



Dorm. Bldg. GF Concreting on 10-11-23



Gate House Painting on 10-11-23



Dormitory-3rd Floor Slab Re-bar Work on 18-12-23



Dormitory-3rd Floor Slab Electrical Pipe on 18-12-23



Dormitory-3rd Floor Slab Concreting on 23-12-23



Dormitory-3rd Floor Slab Concreting on 23-12-23



Comp.Bldg. Front View on 02-02-24



Comp.Bldg. Roof Top on 02-02-24

Comprehensive Building Handover



Dormitory-Outside on 26-02-24



Dormitory-Inside-Toilet Area on 26-02-24

Dormitory-two story handover



Road-Re-bar work on 05-04-24



Road-RCC on 05-04-24

RCC-Car Road Handover



Electrical Work on 08-04-24



Electrical Work on 08-04-24



Dormitory-2nd Floor Painting on 23-04-24



Dormitor-2nd Floor-Corridor on 23-04-24

Project closed from 09 to 16 April, 2024 due to Eid-ul Fitre

Generated by: www.bel3c.com, Developed by: Engr. Md. Sanaul Haque
