# WEEKLY PROJECT REPORT-018



Picture Taken: 15 Jan 2012


#### PROJECT SUMMARY AS ON: 18 JAN 2012

- Program is 53 delayed from master program as on 16<sup>th</sup> Jan 2012.
- Manpower is decreased but production increased. So work-efficiency increased.
- Re-bar and Shutter Lifting Rope should be immediately replaced to avoid any accident.

#### WEEEKLY CHECK-LIST FOR **PROGRAM** AS ON: 18-01-12



Name of Sub-Contractor:			Sohel Enterprise			
WBS						
Task Name	All 5th floor	column (first lift) & SW1	(first lift) casting cor	nnlete		
Actual Start	7111 3111 11001	Actual Finish:	13/01/2012	Time Lag:		
Causes of Delay			abour are not skill.	Time Lug.		
WBS						
Task Name	5th floor C1	A, C2A & SW2, SW3 (first	lift) casting complet	:e		
Actual Start		Actual Finish:	16/01/2012	Time Lag:		
Causes of Delay						
WBS		$\neg$				
Task Name	all Eth floor	l column (2nd lift) & SW1 (	2nd lift) casting			
Actual Start	all Stil llool	Actual Finish:	17/01/2012	Time Lead/Lag:		
Causes of Delay		Actual Fillisti.	17/01/2012	Tillie Leau/Lag.		
Causes of Delay						
WBS						
Task Name	all 5th floor	column (2nd lift) & SW1 (	2nd lift) shuttering	complete		
Actual Start		Actual Finish:	16/01/2012	Time Lead/Lag:		
Causes of Delay		+	, , ,	, 51		
<u> </u>						
WBS						
Task Name						
Actual Start		Actual Finish:		Time Lead/Lag:		
Causes of Delay						
Remarks: (Penalty	y/ Award) to b	e filled by Project Incharg	ge			
,		, ,				
Suuggestion/ Adv	vice:					
53 days delayed fo	rom master nro	ogram as on 16 Jan 2012.				
33 days delayed ii	ioni master pro	ogram as on 10 Jan 2012.				
					Consultant	
				_		
					Chief Engineer	
Project Incharge		Chief Engineer	_	Director		

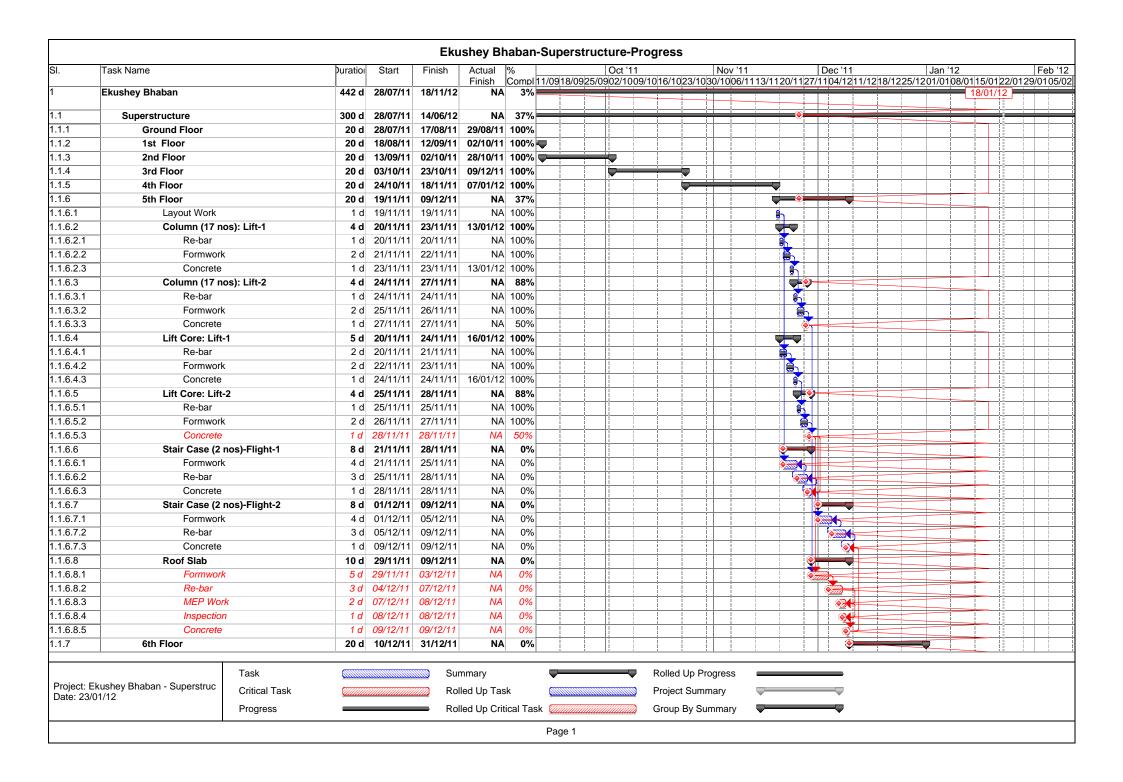

# WEEEKLY CHECK-LIST FOR ${f QUALITY}$ AS ON: 18-01-12



Name of Sub-contractor:	Sohel Enterpri	se
Remarks on Shuttering: (Attach Phot	ograph) to be filled by Project Incharge	
Remarks on Re-bar Work: (Attach Ph	notograph) to be filled by Project Incharge	2
Remarks on Concreting: (Attach Pho	otograph) to be filled by Project Incharge	
Suggestion/ Advice:		
Work Inspection Request before cond	croting attached	
Work inspection request before conc	reting attached.	
		Consultant
		Chief Engineer
Project Incharge	Chief Engineer	Director

Designation

## CITYSCAPE INTERNATIONAL LIMITED

Doc No. CIL R & D WIR 002	
WORK INSPECTION	REDUEST
Description of Work : 5th floors Column 1881 1st Lef-	+ - C5A, C1, C5, C1A, C1B, C1C, C2A, C6B,
Location/ Grid Atob, and 11-05 Level : +1	34 ) Date of Concreting : 13 . 01.
(A Drawing with Marking/Higlighting must be submitted)	Time of Concreting : 68:35
Submitted By:	
Company : Resem Tech Limited Shoke ( Company	teronise This
Name : Mr. Fazlur Rahumo	Signature Signature
	12:01-12 Time : 12:30
	12.50
WORK INSPECTION	REPORT
Reienforcement 6K Formwork	OK Proping/Supporting ✓ OK
Comments	6 11 1
Geood Atter	· Readition.
**	
Inspected By Company : Cityscape International Limited	
Could a real to the contract to a	Old later
Designation : Site was force Date : (	[3.0].[2 Time :
MEP CLEARAN	NCE
Not Applicable Completed	Not Completed
Clearannoed By	A A
Company : Cityscape International Limited	1
Name ;	Signature :
Designation : Date :	Time :
APPROVAL FOR COI	NCRETING
Comments :	
Approved   ✓ Approved with Comments	Not Approved
	Not Approved
Inspected By	1 , (
Company : Cityscape International Limbed	treat Policy
Name : Ul Ul lastu	Signature

Date

Time

## CITYSCAPE INTERNATIONAL LIMITED

	Ġ	ı	ı	
ð	ĕ	d	ä	

	WORK INSPECTION REQUE	ST
	(To submit by Contractor 48 hours before Co-	
	oor Column (GA +GA	) and shear Nath (sws + Swa) first
Location/ Grid by the 5 mul B		Date of Concreting : 16.01-12
(A Drawing linth Marking	Highling must be submitted	Time of Concreting : 10·17:000
Submitted By:		
Company : Rasem	Tech Limited Stuel Enterpris	(r) (m) /_
	elwr Rahman	- years
Designation : Cont	Date :15.01.1	Signature 1/2 Time 2.8% Dec
· Covid	Late .13.011	12 Time : 2,56 Pm
	WORK INSPECTION REPO	RT .
11.0120.01020.000.000		100000000000000000000000000000000000000
Reienforcement V OK	Formwork \( \sqrt{OK} \)	Proping/Supporting OK
Comments :	1/ 0 -: 0:	**
6	itood after Rectifica	ction
Inspected By Company Cityscan	e International Limited	
Name : English		Signature Software
		Cignature /
Designation : Site En	gimular Date : 16:01-1	2 Time : 17-61 12
Not Applicable	MEP CLEARANCE  Completed	Not Completed
Clearannoed By	N/A	
	e International Limited	
Name		-
Designation	Date	Signature :
	C-Sity .	Times
	APPROVAL FOR CONCRET	ING
Comments :		
Approved Approved Approved Approved By	proved with Comments	Not Approved
	pe International Limited	1 0 0
	sml	- Coffam
		Signature (AV T)
Designation : (T	Date : Doll	Time :

# 0.0, Date of Issue : Nov. 2010 CITYSCAPE INTERNATIONAL LIMITED

Doc No. CIL R & D WI	R 002		ALC ENVITED
The state of	Wo	RK INSPECTION REQUES	ST .
	(To subm	iff by Contractor 48 hours before Conc	creting)
Description of Work	5th floor AU		eA and GA RNd Lift-CA
Location/ Grid	A 18 G OUT	Level : 454	Date of Concreting : 19:61-12-
(A Dra	wing with Marking Highgan	ng must be submitted)	Time of Concreting : 1.50 DV/L
Submitted By:			
Company	; Resem Tech Lir	mitted Sharel Enterprise	$T \hookrightarrow i$
Name	: Mre Fazlur		THOUSE !
Designation	Cent:	Date : 16.01-12	Signature (50° :
	Coup.	Date   16'(7'1)	ime :
	W	ORK INSPECTION REPOR	T .
-			
Relenforcemen	u[√]OK	Formwork \( \sqrt{OK} \)	Proping/Supporting OK
Comments	3 /2 - L V	1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	
	6,000 4	Her Rectificat	tion
		S 10.55	****
Inspected By Company	: Cityscape Intern	optional Lieute d	
Name	Engl. Mr. Mc		- Bloom
Designation	Site Every		Signature Farm 51 Par
e engrinous	Direct Alber	T Date :12:01:12	Time : 19/6/12
		MEP CLEARANCE	
Not Applicable Clearannoed By	•□	Completed \	Not Completed
Company	: Cityscape Intern		
Name			
Designation		Date	Signature :
		1 0000	Time :
	APF	PROVAL FOR CONCRETIN	VG
Comments			
Section and the section and th			
Approve	d Approved	with Comments	Not Approved
Inspected By			not approved
Company	: Cityscape Intern	national Limited	1 00.
Name		O CONTRACTOR OF THE PARTY OF TH	- Classen
Designation	********		Signature
nesiduation	: (8)	Date : 16 -20	Time

## WEEEKLY CHECK-LIST FOR **SAFETY** AS ON: 18-01-12



Name of Sub-Contractor:	Sohel enterprise.				
List of Safety Materials iss	sued:				
Safety Shoe	85	pairs			
Helmet	193	nos.			
T-shirt	263	nos.			
Inducution:					
Total Labour:		Inducted:	113		
Tool Box Meeting (Weekly	/ Safety Meeting)	no.:			Date:
Safety Violation: (Attach F	Photograph)			•	·
Warning	No. of Persons				
1st Warning :	10				
2nd Warning with Fine:	3				
Termination:					
Safety Award: (Attach Pho	otograph)				
Induction ID:		Trade		Clean	er
Name:					
Accidents/ Injury:					
Accidents/ injury.					
House Keeping					
Trouse Recepting					
Remarks: to be filled by Pr	oject Incharge				
Sugggestion/ Advice:					
Re-bar and Shutter Lifting				d any acciden	t (see attached
picture). Safety Violation P	icture and Warnii	ng Letter are atta	ched.		
					Consultant
					Chief Engineer
Project Incharge	_	Chief Engineer		D	irector

Date: January 12, 2012

### **Health & Safety Requirement**

Findings: Rod & Shutter carrying rope has been torn out.





Date: January 12, 2012

### **Safety Violation Picture**

Name: Md. Shohel (Electrician)

**Induction ID:** 

**Safety Violation:** 



Project Safety Plan: PSP 01-P00 Rev.00

#### **ATTACHMENT 4**

#### **SAFETY VIOLATION NOTICE**

Date: January 12, 2012

To: Md. Shohel (Electrician) From: CIL – Ekushey Bhaban

Subject: First warning for "PPE"

A Safety and Health Survey of your operations has revealed non-compliance of CITISCAPE safety and health policies and laws. And applicable regulations you are required to maintain a safe work environment and to prevent unsafe actions of your employees. The violation(s) noted and the required corrective action(s) is/are as follows:

Reference:	Description of Violation	Corrective Action	Date of Action
5.2	He was found without	Immediately he forced to	January 12,
	Safety Shoe	wear safety shoe.	2012

Please conform in writing to our office as soon as the required corrective action has been completed.

Best Regards

Safety Engineer



## WEEEKLY CHECK-LIST FOR **MANPOWER** AS ON: 18-01-12



		T			
Name of Sub-Contractor:		Sohel Enterprise			
Shuttering Work:					
Manpower	Required No.	Present No.	Remarks		
Shutter Mistry		110			
Shutter Helper		106			
Re-bar Work:					
Manpower	Required No.	Present No.	Remarks		
Re-bar Fabricator		18			
Helper		14			
Concrete Work:					
Manpower	Required No.	Present No.	Remarks		
Mason		24			
Labour					
Housekeeping					
Manpower	Required No.	Present No.	Remarks		
Labour		14			
Over All Remarks b			ng comcrete volume = 16 m3		
5th floor C1A, C2A	& SW2, SW3 (firs	st lift) casting co	mcrete volume = 11.5 m3		
all 5th floor columr	n (2nd lift) & SW1	(2nd lift) castir	ng comcrete volume = 12 m3		
Suggestion/ Advice	<u> </u>				
Manpower decreas	sed but production	on increased. So	work-efficiency increased.		
				Consulta	
				 Chief Enginee	
Project Incharge	_	Chief Engineer	_	Director	
rioject incharge		Ciller Lingillieer		שוופכנטו	

#### MANPOWER HISTOGRAM

