



DAILY PROGRESS REPORT

Project:	Urban Resilience Unit Building	Project Code:	18	Date:	3-June-2022
Client:	Rajuk	Report	083	Day	Friday
Contractor:	Elevate Builders Ltd,			Climate	Sunny
					28-33C

Manpower

SN	Description	Nos.
01	Elevate-Staff	7
02	Civil Labor-Day Shift	18
03	Civil Labor-Night Shift	10
TOTAL		35


Progress This Day

WBS	Task	Total Qty	Today Done(%)	Total Done(%)	Schedule Start	Schedule Finish
3.2.6.1	Basement-1-Ramp-Form Work	1no.	10	100	11-03-22	14-03-22
3.2.6.2	Basement-1-Ramp-Re-bar Work	1no.	30	100	14-03-22	15-03-22
3.2.6.3	Basement-1-Ramp-Inspection	1no.	50	100	15-03-22	15-03-22
3.2.6.4	Basement-1-Ramp-Concreting	1no.	50	100	15-03-22	15-03-22

Site Photographs



Ready mix car

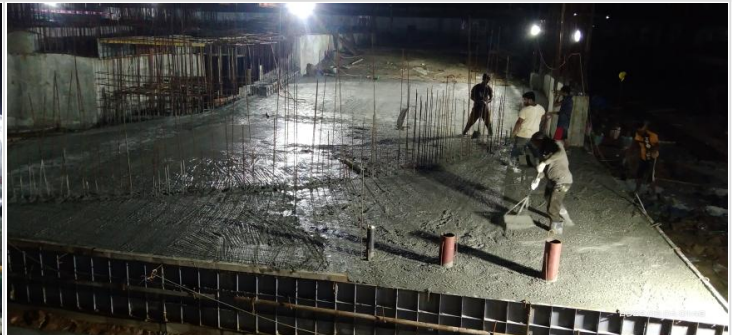

Ready mix concreting

Site Description

Site Instruction

Entry by:

Planning Engineer

Generated by:

www.bel3c.com, Developed by: Engr. Md. Sanaul Haque
