



## DAILY PROGRESS REPORT

|             |                            |               |     |         |                 |
|-------------|----------------------------|---------------|-----|---------|-----------------|
| Project:    | Shimanto Conference Center | Project Code: | 17  | Date:   | 31-January-2022 |
| Client:     | Border Guard Bangladesh    | Report        | 142 | Day     | Monday          |
| Contractor: | Sarker Steel Ltd.          |               |     | Climate | Sunny           |
|             |                            |               |     |         | 11-22C          |


### Manpower

| SN    | Description      | Nos. |
|-------|------------------|------|
| 01    | Sarker Staff     | 3    |
| 04    | AC-Newton-Staff  | 1    |
| 05    | AC-Newton-Worker | 10   |
| TOTAL |                  | 14   |

### Progress This Day

| WBS     | Task                             | Total Qty | Today Done(%) | Total Done(%) | Schedule Start | Schedule Finish |
|---------|----------------------------------|-----------|---------------|---------------|----------------|-----------------|
| 1.3.1.1 | Brick Work-Ground Floor          | 1340m2    | 5             | 100           | 01-05-21       | 18-08-21        |
| 1.3.1.3 | Brick Work-1st Floor             | 1210m2    | 5             | 100           | 28-05-21       | 04-09-21        |
| 1.3.2.2 | Plaster-Ground Floor             | 2680m2    | 5             | 100           | 09-05-21       | 20-08-21        |
| 1.3.2.4 | Plaster-1st Floor                | 2420m2    | 3             | 95            | 29-08-21       | 12-09-21        |
| 1.3.2.5 | Plaster-1st Floor Mezzanine      | 1560m2    | 3             | 95            | 10-09-21       | 16-09-21        |
| 1.3.3   | Tiles Work                       |           | 10            | 70            | 10-05-21       | 26-09-21        |
| 2.3.1.2 | Interior-False Ceiling-1st Floor | 0         | 70            | 70            | 16-09-21       | 15-10-21        |
| 2.5.2   | Generator                        |           | 20            | 80            | 15-09-21       | 27-10-21        |

### Site Photographs

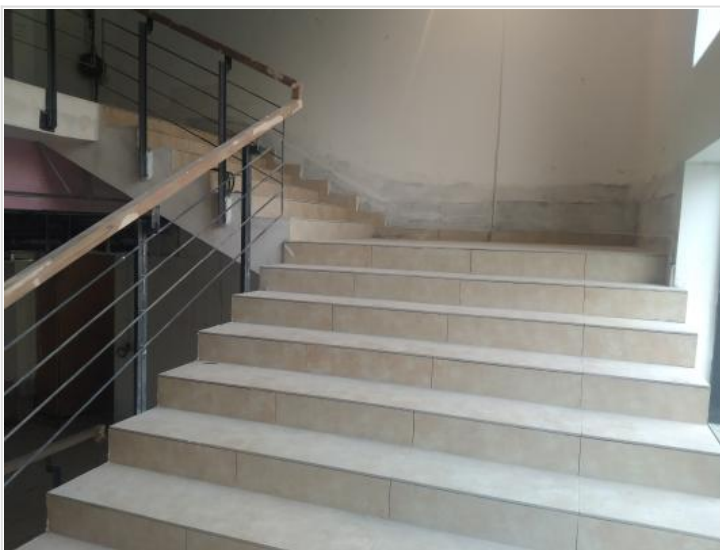

Tiles work



Interior work

Site Description

Site Instruction

Entry by:

Generated by:

