



MONTHLY PROGRESS REPORT

From 1-October-2024 to 17-October-2024

Project Code:	31	Name:	New Hope Agrotech-Munshiganj
Client:	New Hope Agrotech BD Ltd.	Contractor:	Sarker Steel Ltd.

Monthly Progress

WBS	Task	Total Qty	Upto Last Month(%)	This Month(%)	Total Done(%)	Schedule Start	Schedule Finish	Actual Finish
03.5.1	Pile Load Test-PDA-Pile Development	3nos	0	100	100	10-10-24	13-10-24	16-10-24
03.6	Wooden Shore Piling	135nos.	0	100	100	06-10-24	12-10-24	07-10-24
04.01	Excavation	1982m3	0	78	78	08-10-24	06-11-24	16-10-24
04.02	Pile head breaking	79nos	-6	88	82	10-10-24	08-11-24	17-10-24
04.03.1	Pile Cap-Lean Concrete	18nos	23	44	67	17-10-24	11-11-24	16-10-24
04.03.3	Pile Cap-Brick Shuttering	18nos	0	17	17	20-10-24	13-11-24	13-10-24
04.04.1	Tank Base-Lean Concrete	2Nos	-30	110	80	07-11-24	08-11-24	16-10-24
04.04.5	Tank Base-Side Brick Shutter	2nos	-50	135	85	12-11-24	13-11-24	17-10-24

Site Photographs



Earth excavation on 01-10-24

Re-bar straightening on 01-10-24

Site Description

Site Instruction



Earth excavation on 02-10-24

Old base-column found during excavation on 02-10-24

Site Description

During excavating old foundation with column found

Site Instruction

In Grid-1 in between C and D



Obstacle RCC dismantling on 03-10-24

Earth excavation on 03-10-24

Site Description

Dismantling RCC foundation found during excavation

Site Instruction

Money and Time wastage



Pile Head breaking on 04-10-24

Wooden pile driving on 04-10-24

Site Description

Due to rain work stopped

Site Instruction



Old base breaking on 05-10-24

Earth excavation on 05-10-24

Site Description

Site Instruction



Wooden shore pile driving on 06-10-24

Earth Excavation on 06-10-24

Site Description

Site Instruction



Earth excavation on 07-10-24

Site Description

Site Instruction



Pile head breaking on 07-10-24



Excavated earth dumping on 08-10-24

Site Description

Dismantling old foundation 17 m3

Site Instruction

By Hydraulic hammer



Dismantling by hydraulic breaker on 08-10-24



Earth excavation on 09-10-24


Site Description

Old base dismantling 11 m3 by hydraulic hammer

Site Instruction



Old base dismantling by hydraulic hammer on 09-10-24

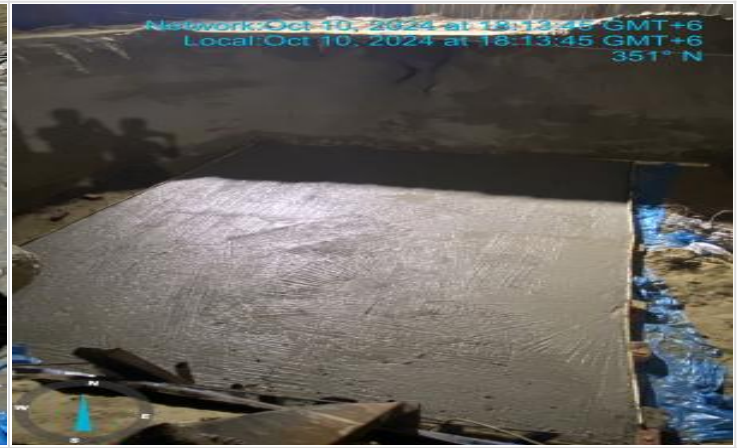

Pile Load Test-PDA-Pile Development on 10-10-24

Water Reservoir Base CC-Bottom on 10-10-24

Site Description

Old base dismantling 4 m3 by hydraulic hammer

Site Instruction



Dewatering on 11-10-24

Pile head breaking on 11-10-24

Site Description

Site Instruction



Checking before pile cap lean concreting on 12-10-24

Pile cap lean concreting on 12-10-24

Site Description

Due to rain work started late

Site Instruction



Pile cap side brick shuttering on 13-10-24

Site Description

Wooden shore piling 14 nos.

Site Instruction



Earth excavation manually on 13-10-24



Earth excavation on 14-10-24

Site Description

Wooden pile driving 41 nos.

Site Instruction



Shoring on 14-10-24



Inspection before CC at -5200 mm on 15-10-24

Site Description

Site Instruction



CC at level -5200 finished on 15-10-24



Excavation, brick-shuttering, steel shut on 16-10-24

Pile Cap Lean concreting on 16-10-24

Site Description

Site Instruction



Pile head breaking on 17-10-24

Water tank base brick wall shuttering on 17-10-24

Site Description

Site Instruction

Entry by:
Planning Engineer

Generated by:
www.bel3c.com, Developed by: Engr. Md. Sanaul Haque
