MOBILIZATION PLAN FOR MARRIOT-NILGIRI
AT BANDARBAN

Sl.	Task Name	Duration	Start	Finish	% Complete
1	**MARRIOT-NILGIRI-MOBILIZATION**	**98 d**	**31-10-20**	**05-02-21**	**47%**
1.1	TAKE-OVER SITE FOR CONSTRUCTION	1 d	31-10-20	31-10-20	100%
1.2	DEMARKATION	42 d	01-11-20	12-12-20	100%
1.3	**MOBILIZATION**	**90 d**	**08-11-20**	**05-02-21**	**38%**
1.3.1	Mobile Network Upgrading	7 d	08-11-20	14-11-20	100%
1.3.2	*Material Mobilization for Preliminaries*	*60 d*	*08-12-20*	*05-02-21*	*10%*
1.3.3	Water Resrvoir and Water Supply Line	31 d	16-11-20	16-12-20	100%
1.3.4	Labour Shed	25 d	07-12-20	31-12-20	100%
1.3.5	Store Shed	12 d	13-12-20	24-12-20	100%
1.3.6	Mechanics Shed	8 d	28-12-20	04-01-21	100%
1.3.7	Grass Cutting for Internal Road Network Development	30 d	28-12-20	26-01-21	10%
1.3.8	**Guest House**	**31 d**	**06-01-21**	**05-02-21**	**0%**
1.3.8.1	*Layout*	*1 d*	*06-01-21*	*06-01-21*	*0%*
1.3.8.2	*Excavation*	*4 d*	*07-01-21*	*10-01-21*	*0%*
1.3.8.3	*Footing*	*5 d*	*08-01-21*	*12-01-21*	*0%*
1.3.8.4	*Padestal*	*4 d*	*10-01-21*	*13-01-21*	*0%*
1.3.8.5	*Grade Beam*	*6 d*	*12-01-21*	*17-01-21*	*0%*
1.3.8.6	*Floor*	*3 d*	*18-01-21*	*20-01-21*	*0%*
1.3.8.7	*Column*	*4 d*	*21-01-21*	*24-01-21*	*0%*
1.3.8.8	*Brick-work*	*7 d*	*24-01-21*	*30-01-21*	*0%*
1.3.8.9	Tie Beam	5 d	28-01-21	01-02-21	0%
1.3.8.10	Truss	6 d	26-01-21	31-01-21	0%
1.3.8.11	Sanitary-Electrical Pipe work	3 d	30-01-21	01-02-21	0%
1.3.8.12	Grill-Door Frame	2 d	30-01-21	31-01-21	0%
1.3.8.13	*Plaster*	*4 d*	*31-01-21*	*03-02-21*	*0%*
1.3.8.14	*Roof Sheet*	*3 d*	*01-02-21*	*03-02-21*	*0%*
1.3.8.15	*Tile Work*	*4 d*	*31-01-21*	*03-02-21*	*0%*
1.3.8.16	*Painting*	*4 d*	*02-02-21*	*05-02-21*	*0%*
1.3.8.17	*Door-Window*	*2 d*	*04-02-21*	*05-02-21*	*0%*
1.3.8.18	*Sanitary-Electrical Fittings*	*4 d*	*02-02-21*	*05-02-21*	*0%*

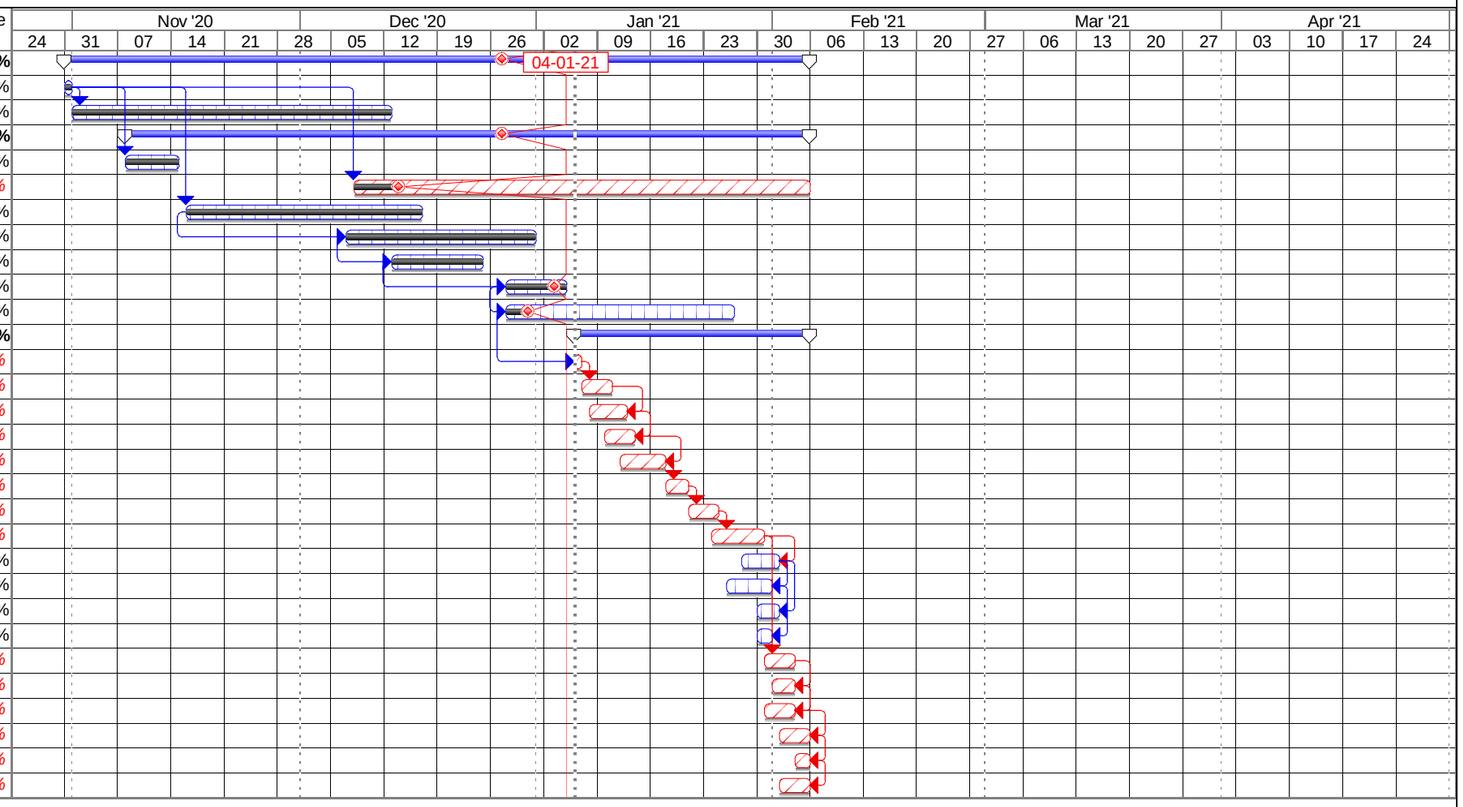

Date: 06-01-21 16.13
Sheet:1 /1

Task | Progress | Rolled Up Task | Rolled Up Progress | Group By Summary
Critical Task | Summary | Rolled Up Critical Task | Project Summary
