Work Plan(Rev-2.0) and Progress for Construction of 150,000 Tons Livestock and Poultry Feed Factory in Bogura, Rajshahi, Bangladesh

WBS	Task Name	Duration	Start	Finish	% Complete
1	**New Hope Animal Nutrition BD Co Ltd.**	**368 d**	**09/01/23**	**31/01/24**	**92%**
1.1	**Mobilization**	**35 d**	**09/01/23**	**12/02/23**	**100%**
1.1.1	Shed	12 d	09/01/23	20/01/23	100%
1.1.2	Labour	4 d	14/01/23	17/01/23	100%
1.1.3	Material	2 d	21/01/23	22/01/23	100%
1.1.4	Equipment	2 d	27/01/23	28/01/23	100%
1.1.5	Electricity Connection	7 d	31/01/23	06/02/23	100%
1.1.6	Tubewell Sinking	1 d	01/02/23	01/02/23	100%
1.1.7	Mud Tank Making	12 d	01/02/23	12/02/23	100%
1.2	Pile Layout and Survey	2 d	01/02/23	02/02/23	100%
1.3	**Living Area**	**337 d**	**09/02/23**	**31/01/24**	**96%**
1.3.1	**Comprehensive Building-2 Story**	**306 d**	**09/02/23**	**31/12/23**	**100%**
1.3.1.1	Pile Boring and Concreting-69 nos.	30 d	09/02/23	10/03/23	100%
1.3.1.2	Pile Load Test-Itegrity Test	3 d	11/04/23	13/04/23	100%
1.3.1.3	**Sub-structure**	**27 d**	**18/03/23**	**13/04/23**	**100%**
1.3.1.3.1	Pile Head Breaking	10 d	18/03/23	27/03/23	100%
1.3.1.3.2	Pile Cap	10 d	21/03/23	30/03/23	100%
1.3.1.3.3	Foundation Beam	14 d	31/03/23	13/04/23	100%
1.3.1.4	**Super Structure**	**39 d**	**24/05/23**	**11/07/23**	**100%**
1.3.1.4.1	**Ground Floor**	**18 d**	**24/05/23**	**10/06/23**	**100%**
1.3.1.4.1.1	Column	9 d	24/05/23	01/06/23	100%
1.3.1.4.1.2	**Stair Case**	**14 d**	**28/05/23**	**10/06/23**	**100%**
1.3.1.4.1.2.1	1st Flight	5 d	28/05/23	01/06/23	100%
1.3.1.4.1.2.2	2nd Flight	7 d	04/06/23	10/06/23	100%
1.3.1.4.1.3	**Roof Beam-Slab**	**10 d**	**01/06/23**	**10/06/23**	**100%**
1.3.1.4.1.3.1	Formwork	6 d	01/06/23	06/06/23	100%
1.3.1.4.1.3.2	Re-bar Work	3 d	07/06/23	09/06/23	100%
1.3.1.4.1.3.3	Electrical Pipe Fixing	2 d	08/06/23	09/06/23	100%
1.3.1.4.1.3.4	Concreting	1 d	10/06/23	10/06/23	100%
1.3.1.4.2	**1st Floor**	**15 d**	**12/06/23**	**26/06/23**	**100%**
1.3.1.4.2.1	Column	7 d	12/06/23	18/06/23	100%
1.3.1.4.2.2	**Stair Case**	**15 d**	**12/06/23**	**26/06/23**	**100%**
1.3.1.4.2.2.1	1st Flight	7 d	12/06/23	18/06/23	100%
1.3.1.4.2.2.2	2nd Flight	7 d	20/06/23	26/06/23	100%
1.3.1.4.2.3	**Roof Beam-Slab**	**8 d**	**19/06/23**	**26/06/23**	**100%**
1.3.1.4.2.3.1	Formwork	6 d	19/06/23	24/06/23	100%
1.3.1.4.2.3.2	Re-bar Work	2 d	25/06/23	26/06/23	100%
1.3.1.4.2.3.3	Electrical Pipe Fixing	2 d	25/06/23	26/06/23	100%
1.3.1.4.2.3.4	Concreting	1 d	26/06/23	26/06/23	100%
1.3.1.4.3	**Roof Top-Stair Room**	**4 d**	**08/07/23**	**11/07/23**	**100%**
1.3.1.4.3.1	Column	2 d	08/07/23	09/07/23	100%
1.3.1.4.3.2	Roof Slab	2 d	10/07/23	11/07/23	100%
1.3.1.4.3.3	Parapet-Brick Wall	3 d	08/07/23	10/07/23	100%
1.3.1.5	**Masonry and Finishing Work**	**180 d**	**25/06/23**	**31/12/23**	**100%**
1.3.1.5.1	**Ground Floor**	**168 d**	**25/06/23**	**19/12/23**	**100%**
1.3.1.5.1.1	Brick Work	7 d	25/06/23	11/07/23	100%
1.3.1.5.1.2	Window Grill Fixing	3 d	12/07/23	14/07/23	100%
1.3.1.5.1.3	Plaster Work	5 d	11/07/23	15/07/23	100%
1.3.1.5.1.4	Khoa-sand Cusion in Floor	5 d	11/07/23	15/07/23	100%
1.3.1.5.1.5	Floor Concreting	7 d	10/07/23	16/07/23	100%

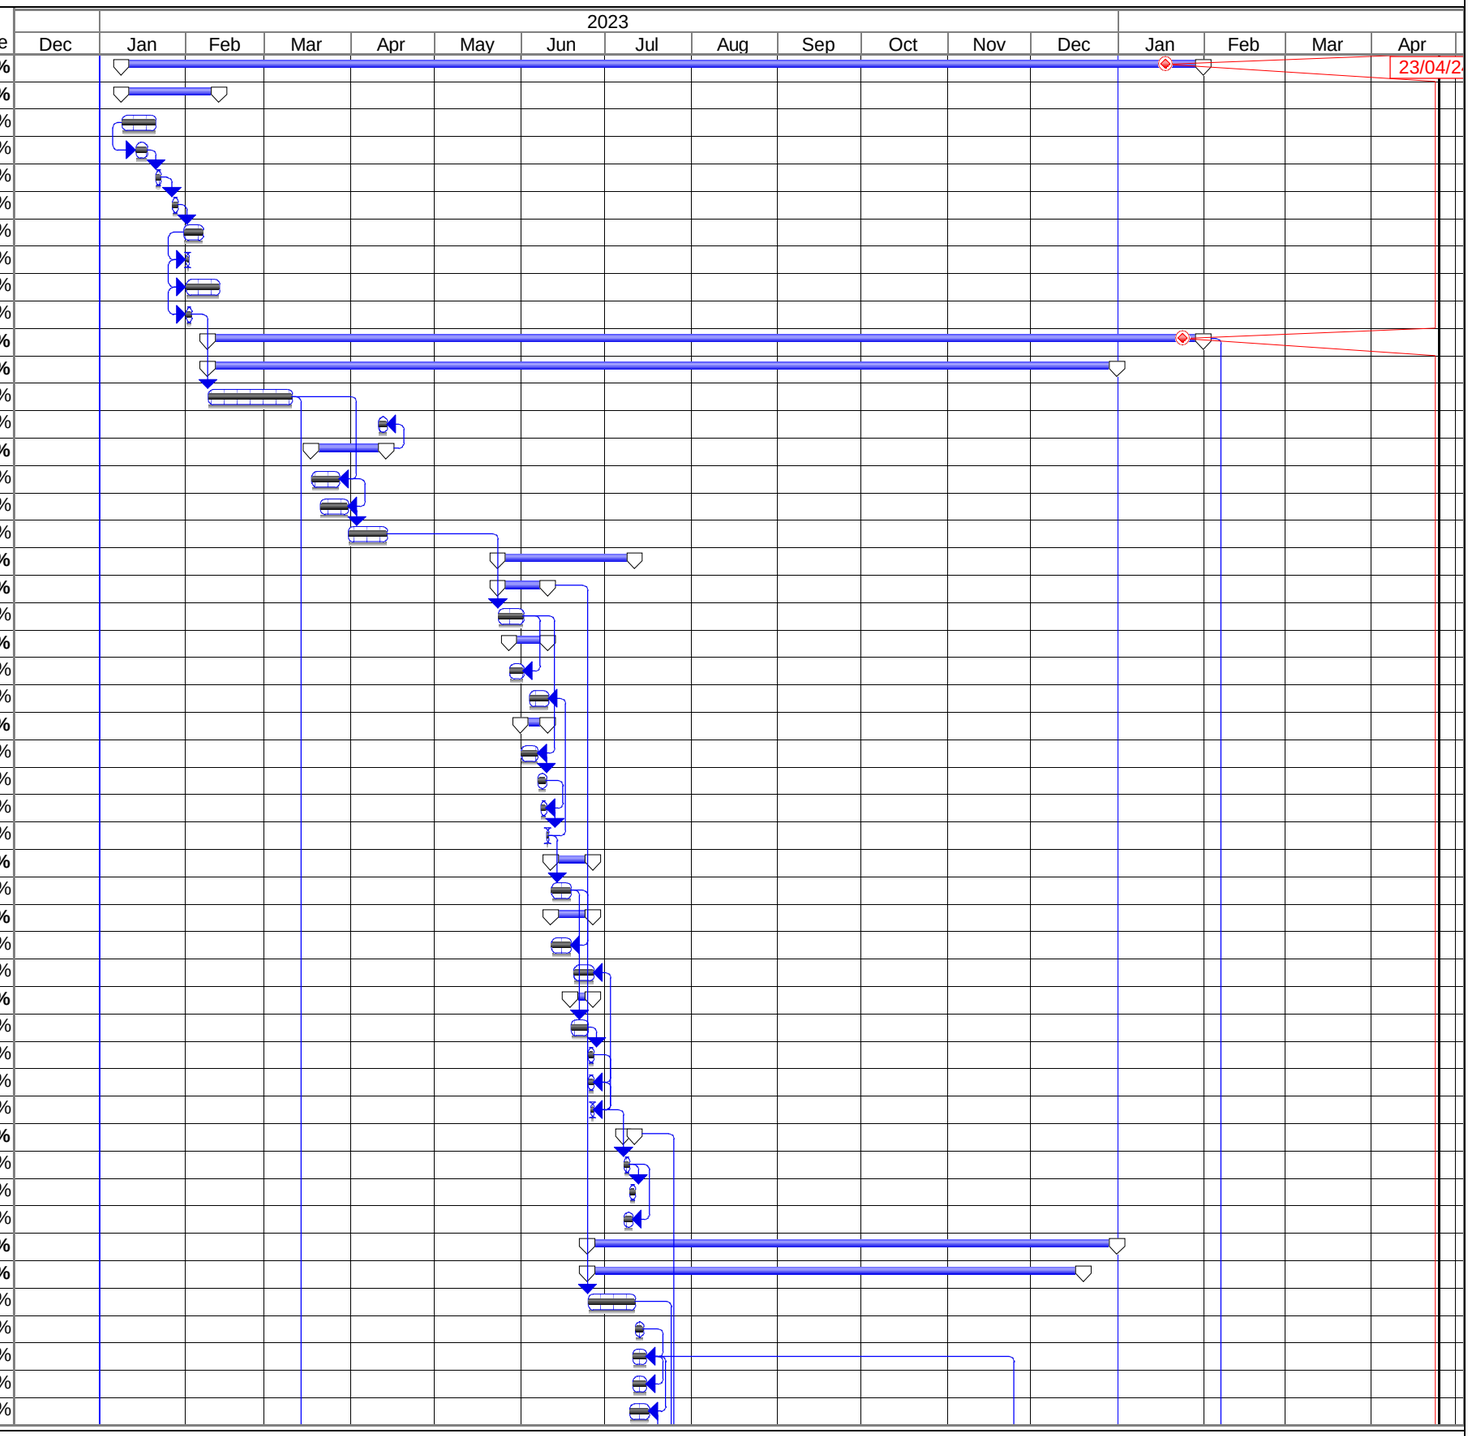

Date: 25/04/24 11:48
Sheet:1 /5

Task | Progress | Rolled Up Task | Rolled Up Progress | Group By Summary
Critical Task | Summary | Rolled Up Critical Task | Project Summary

Work Plan(Rev-2.0) and Progress for Construction of 150,000 Tons Livestock and Poultry Feed Factory in Bogura, Rajshahi, Bangladesh

WBS	Task Name	Duration	Start	Finish	% Complete
1.3.1.5.1.6	Tiles Fitting	7 d	17/07/23	23/07/23	100%
1.3.1.5.1.7	Door shiutter and Window fixing	3 d	22/07/23	24/07/23	100%
1.3.1.5.1.8	False Ceiling	15 d	10/07/23	24/07/23	100%
1.3.1.5.1.9	Inside Painting	25 d	25/11/23	19/12/23	100%
1.3.1.5.2	**1st Floor**	**154 d**	**26/07/23**	**26/12/23**	**100%**
1.3.1.5.2.1	Brick Work	7 d	26/07/23	01/08/23	100%
1.3.1.5.2.2	Plaster Work	5 d	01/08/23	05/08/23	100%
1.3.1.5.2.3	Tiles Fitting	7 d	04/08/23	10/08/23	100%
1.3.1.5.2.4	Door shiutter and Window fixing	3 d	09/08/23	11/08/23	100%
1.3.1.5.2.5	False Ceiling	15 d	28/07/23	11/08/23	100%
1.3.1.5.2.6	Inside Painting	25 d	02/12/23	26/12/23	100%
1.3.1.5.3	Outside Plastering	15 d	28/07/23	11/08/23	100%
1.3.1.5.4	Waterproofing on Roof	15 d	01/12/23	15/12/23	100%
1.3.1.5.5	Outside Painting	20 d	12/12/23	31/12/23	100%
1.3.1.6	**Water and Electrical**	**169 d**	**12/07/23**	**27/12/23**	**100%**
1.3.1.6.1	**Ground Floor**	**169 d**	**12/07/23**	**27/12/23**	**100%**
1.3.1.6.1.1	Sanitarty Pipe Work	7 d	12/07/23	18/07/23	100%
1.3.1.6.1.2	Plumbing Work	7 d	12/07/23	21/12/23	100%
1.3.1.6.1.3	Electrical Pipe Work	7 d	12/07/23	18/07/23	100%
1.3.1.6.1.4	Power Distribution Board	7 d	19/07/23	25/07/23	100%
1.3.1.6.1.5	Cable Tray	7 d	19/07/23	25/07/23	100%
1.3.1.6.1.6	Electrical Cable/ Wiring	7 d	13/07/23	19/07/23	100%
1.3.1.6.1.7	Sanitary Fixer installation	7 d	21/12/23	27/12/23	100%
1.3.1.6.1.8	Electrical Switch Socket Fixing	3 d	25/12/23	27/12/23	100%
1.3.1.6.2	**1st Floor**	**146 d**	**04/08/23**	**27/12/23**	**100%**
1.3.1.6.2.1	Sanitarty Pipe Work	5 d	04/08/23	08/08/23	100%
1.3.1.6.2.2	Plumbing Work	5 d	04/08/23	08/08/23	100%
1.3.1.6.2.3	Electrical Pipe Work	5 d	04/08/23	08/08/23	100%
1.3.1.6.2.4	Power Distribution Board	7 d	05/08/23	11/08/23	100%
1.3.1.6.2.5	Cable Tray	7 d	05/08/23	11/08/23	100%
1.3.1.6.2.6	Electrical Cable/ Wiring	3 d	07/08/23	09/08/23	100%
1.3.1.6.2.7	Sanitary Fixer installation	7 d	21/12/23	27/12/23	100%
1.3.1.6.2.8	Electrical Switch Socket Fixing	3 d	25/12/23	27/12/23	100%
1.3.2	**Staff Canteen Dormitor-2 Story**	**306 d**	**12/03/23**	**31/01/24**	**93%**
1.3.2.1	Pile Boring and Concreting-38 nos.	15 d	12/03/23	26/03/23	100%
1.3.2.2	Load Test-Intigrity Test	1 d	30/04/23	30/04/23	100%
1.3.2.3	**Sub-structure**	**39 d**	**01/05/23**	**08/06/23**	**100%**
1.3.2.3.1	Pile Head Breaking	10 d	01/05/23	10/05/23	100%
1.3.2.3.2	Pile Cap	10 d	20/05/23	29/05/23	100%
1.3.2.3.3	Short Column	3 d	30/05/23	01/06/23	100%
1.3.2.3.4	Grade Beam	7 d	02/06/23	08/06/23	100%
1.3.2.4	**Super Structure**	**166 d**	**18/06/23**	**10/12/23**	**100%**
1.3.2.4.1	**Ground Floor**	**29 d**	**18/06/23**	**26/07/23**	**100%**
1.3.2.4.1.1	Column	9 d	18/06/23	26/06/23	100%
1.3.2.4.1.2	**Stair Case**	**18 d**	**09/07/23**	**26/07/23**	**100%**
1.3.2.4.1.2.1	1st Flight	5 d	09/07/23	13/07/23	100%
1.3.2.4.1.2.2	2nd Flight	7 d	20/07/23	26/07/23	100%
1.3.2.4.1.3	**Roof Beam-Slab**	**15 d**	**12/07/23**	**26/07/23**	**100%**
1.3.2.4.1.3.1	Formwork	10 d	12/07/23	21/07/23	100%
1.3.2.4.1.3.2	Re-bar Work	4 d	22/07/23	25/07/23	100%

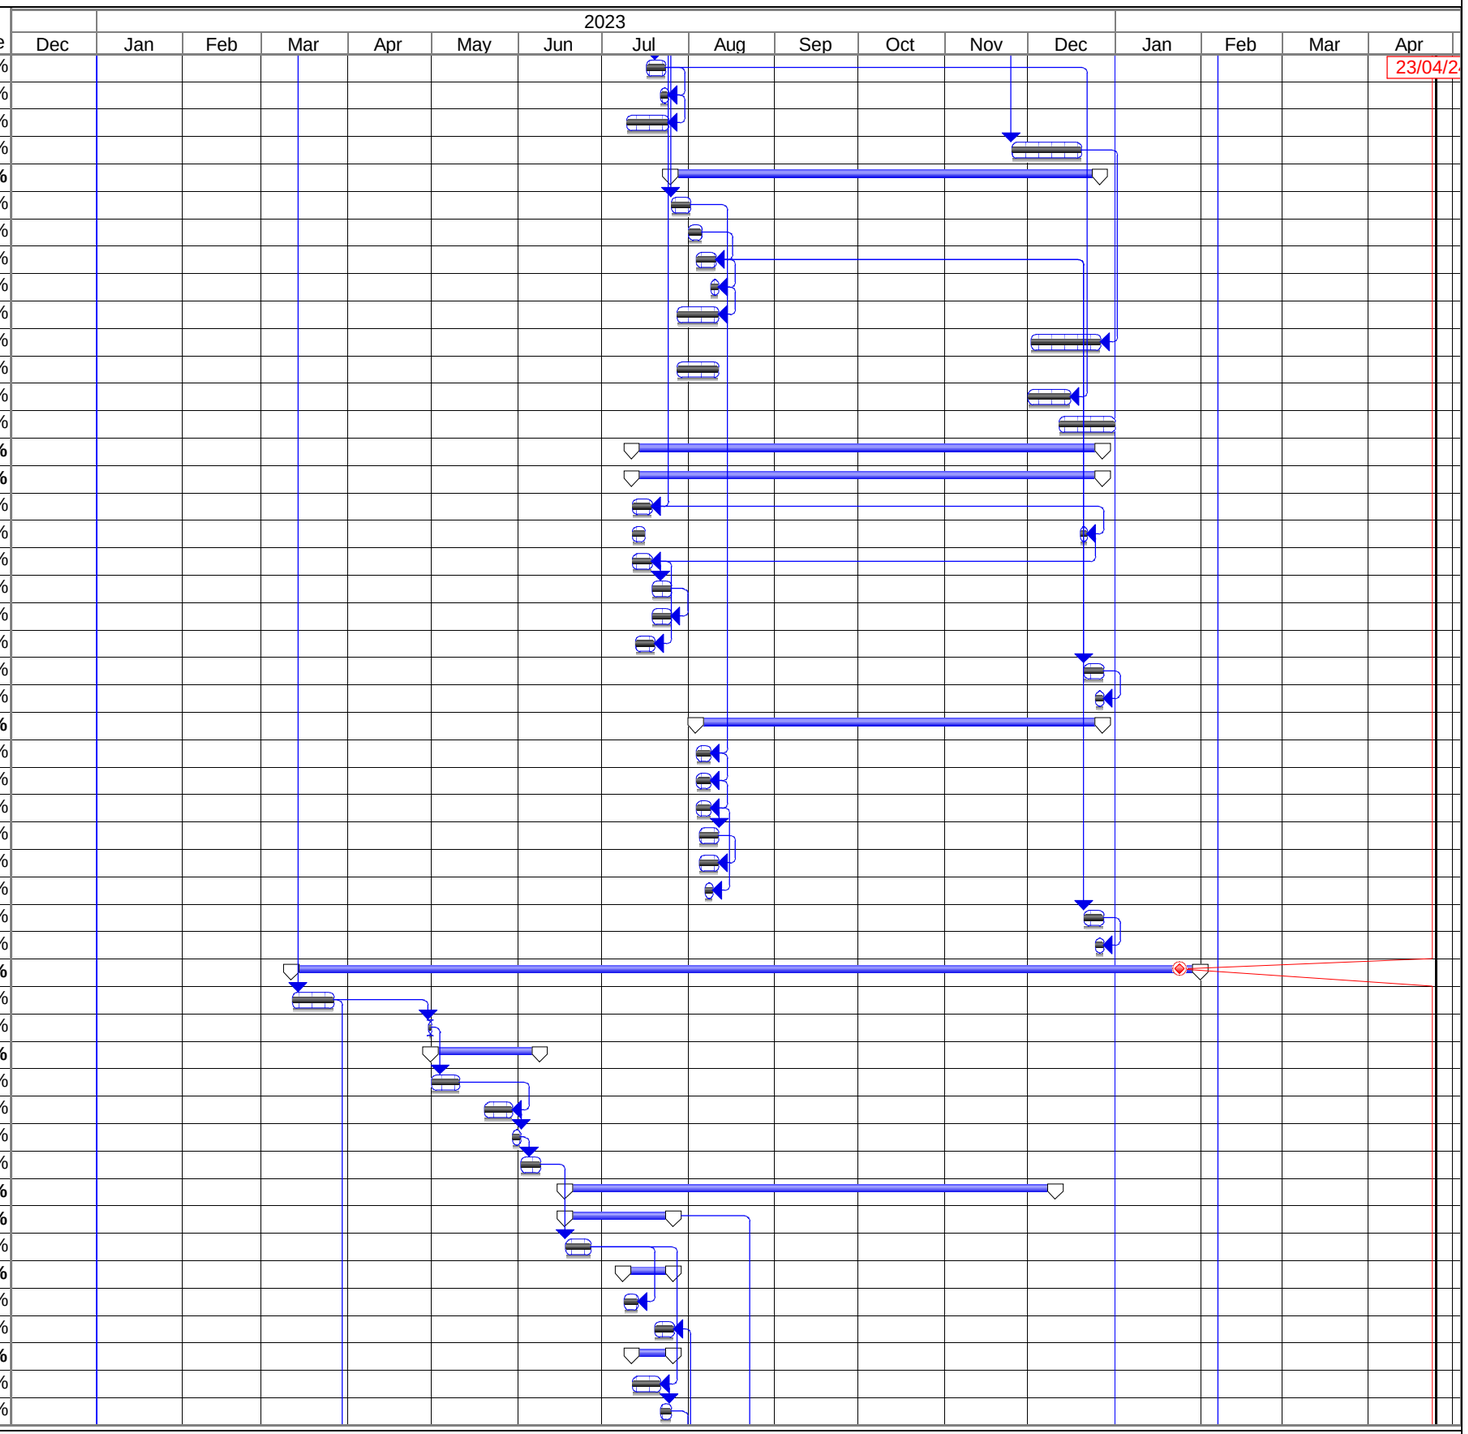

Date: 25/04/24 11:48
Sheet:2 /5

Task | Progress | Rolled Up Task | Rolled Up Progress | Group By Summary
Critical Task | Summary | Rolled Up Critical Task | Project Summary

Work Plan(Rev-2.0) and Progress for Construction of 150,000 Tons Livestock and Poultry Feed Factory in Bogura, Rajshahi, Bangladesh

WBS	Task Name	Duration	Start	Finish	% Complete
1.3.2.4.1.3.3	Electrical Pipe Fixing	3 d	23/07/23	25/07/23	100%
1.3.2.4.1.3.4	Concreting	1 d	26/07/23	26/07/23	100%
1.3.2.4.2	**1st Floor**	**20 d**	**13/08/23**	**01/09/23**	**100%**
1.3.2.4.2.1	Column	7 d	13/08/23	19/08/23	100%
1.3.2.4.2.2	**Stair Case**	**20 d**	**13/08/23**	**01/09/23**	**100%**
1.3.2.4.2.2.1	1st Flight	7 d	13/08/23	19/08/23	100%
1.3.2.4.2.2.2	2nd Flight	7 d	26/08/23	01/09/23	100%
1.3.2.4.2.3	**Roof Beam-Slab**	**13 d**	**20/08/23**	**01/09/23**	**100%**
1.3.2.4.2.3.1	Formwork	8 d	20/08/23	27/08/23	100%
1.3.2.4.2.3.2	Re-bar Work	5 d	28/08/23	01/09/23	100%
1.3.2.4.2.3.3	Electrical Pipe Fixing	2 d	31/08/23	01/09/23	100%
1.3.2.4.2.3.4	Concreting	1 d	01/09/23	01/09/23	100%
1.3.2.4.3	**2nd Floor**	**98 d**	**04/09/23**	**10/12/23**	**100%**
1.3.2.4.3.1	Column	60 d	04/09/23	02/11/23	100%
1.3.2.4.3.2	**Stair Case**	**45 d**	**27/10/23**	**10/12/23**	**100%**
1.3.2.4.3.2.1	1st Flight	7 d	27/10/23	02/11/23	100%
1.3.2.4.3.2.2	2nd Flight	7 d	04/12/23	10/12/23	100%
1.3.2.4.3.3	**Roof Beam-Slab**	**38 d**	**03/11/23**	**10/12/23**	**100%**
1.3.2.4.3.3.1	Formwork	8 d	03/11/23	10/11/23	100%
1.3.2.4.3.3.2	Re-bar Work	5 d	06/12/23	10/12/23	100%
1.3.2.4.3.3.3	Electrical Pipe Fixing	2 d	09/12/23	10/12/23	100%
1.3.2.4.3.3.4	Concreting	1 d	10/12/23	10/12/23	100%
1.3.2.5	**Masonry and Finishing Work**	**185 d**	**31/07/23**	**31/01/24**	**91%**
1.3.2.5.1	**Ground Floor**	**143 d**	**31/07/23**	**20/12/23**	**100%**
1.3.2.5.1.1	Brick Work	17 d	31/07/23	16/08/23	100%
1.3.2.5.1.2	Door Frame Fixing	7 d	11/12/23	17/12/23	100%
1.3.2.5.1.3	Window Grill Fixing	7 d	11/12/23	17/12/23	100%
1.3.2.5.1.4	Plaster Work	5 d	16/08/23	20/08/23	100%
1.3.2.5.1.5	Khoa-sand Cusion in Floor	5 d	16/08/23	20/08/23	100%
1.3.2.5.1.6	Floor Concreting	6 d	16/08/23	21/08/23	100%
1.3.2.5.1.7	Tiles Fitting	15 d	05/12/23	19/12/23	100%
1.3.2.5.1.8	Door shiutter and Window fixing	3 d	18/12/23	20/12/23	100%
1.3.2.5.1.9	Inside Painting	15 d	06/12/23	20/12/23	100%
1.3.2.5.2	**1st Floor**	**88 d**	**09/10/23**	**04/01/24**	**100%**
1.3.2.5.2.1	Brick Work	7 d	09/10/23	15/10/23	100%
1.3.2.5.2.2	Door Frame Fixing	3 d	18/12/23	20/12/23	100%
1.3.2.5.2.3	Window Grill Fixing	3 d	18/12/23	20/12/23	100%
1.3.2.5.2.4	Plaster Work	5 d	15/10/23	21/12/23	100%
1.3.2.5.2.5	Tiles Fitting	15 d	20/12/23	03/01/24	100%
1.3.2.5.2.6	Door shiutter and Window fixing	3 d	02/01/24	04/01/24	100%
1.3.2.5.2.7	Inside Painting	15 d	21/12/23	04/01/24	100%
1.3.2.5.2.8	False Ceiling and Toilet Partition	7 d	29/12/23	04/01/24	100%
1.3.2.5.3	**2nd Floor**	**24 d**	**08/01/24**	**31/01/24**	**81%**
1.3.2.5.3.1	Brick Work	10 d	08/01/24	17/01/24	100%
1.3.2.5.3.2	Door Frame Fixing	3 d	18/01/24	20/01/24	100%
1.3.2.5.3.3	Window Grill Fixing	3 d	18/01/24	20/01/24	100%
1.3.2.5.3.4	Inside Plaster Work	10 d	12/01/24	21/01/24	100%
1.3.2.5.3.5	Tiles Fitting	9 d	20/01/24	28/01/24	100%
1.3.2.5.3.6	*Door shiutter and Window fixing*	*3 d*	*27/01/24*	*29/01/24*	*95%*
1.3.2.5.3.7	*Inside Painting*	*14 d*	*18/01/24*	*31/01/24*	*30%*

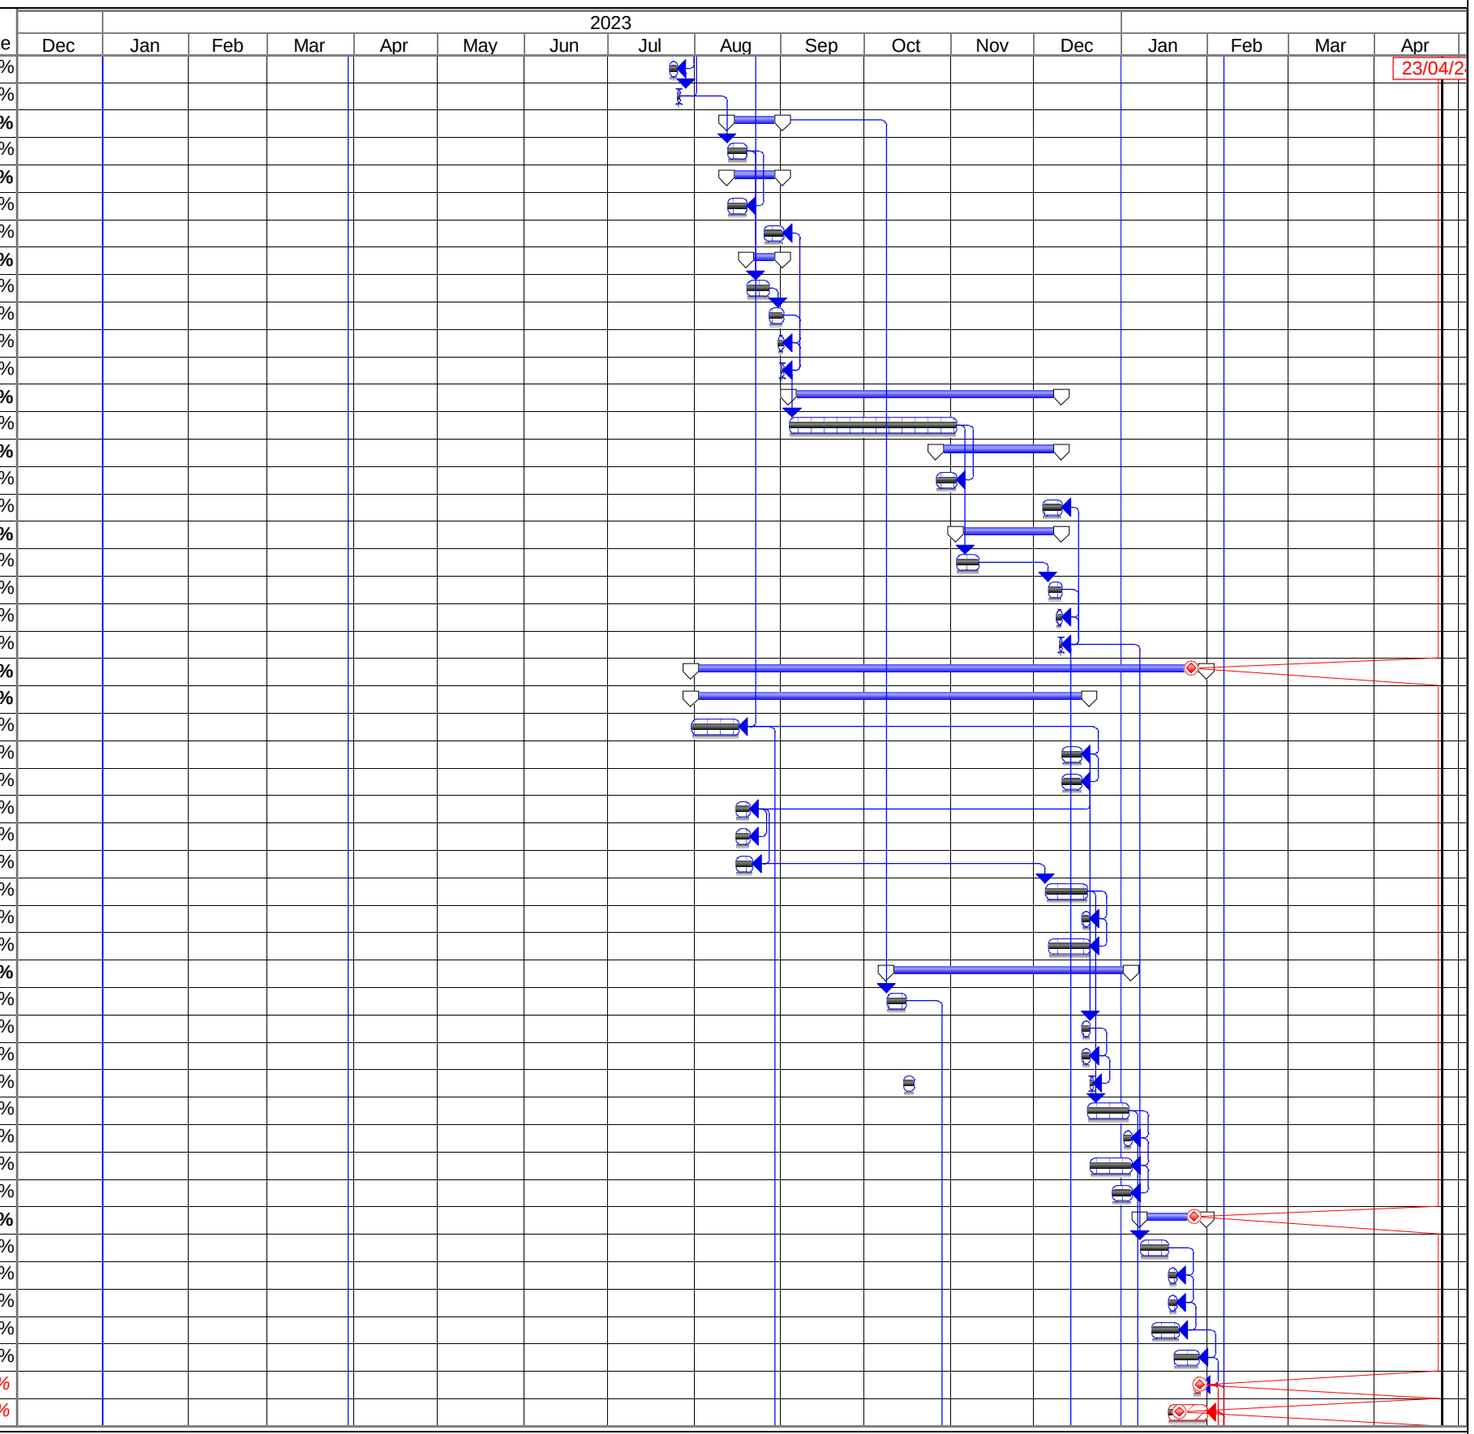

Date: 25/04/24 11:48
Sheet:3 /5

Task | Critical Task | Progress | Summary | Rolled Up Task | Rolled Up Critical Task | Rolled Up Progress | Project Summary | Group By Summary

Work Plan(Rev-2.0) and Progress for Construction of 150,000 Tons Livestock and Poultry Feed Factory in Bogura, Rajshahi, Bangladesh

WBS	Task Name	Duration	Start	Finish	% Complete
1.3.2.5.3.8	*Toilet Patition and False Ceiling*	*7 d*	*25/01/24*	*31/01/24*	*80%*
1.3.2.5.4	Roof Top Parapet Brick-wall	15 d	14/12/23	28/12/23	100%
1.3.2.5.5	Outside Plastering	25 d	29/12/23	22/01/24	100%
1.3.2.5.6	Water Proofing on Rooftop	15 d	08/01/24	22/01/24	100%
1.3.2.5.7	*Outside Painting*	*20 d*	*12/01/24*	*31/01/24*	*30%*
1.3.2.5.8	Stair Railing	7 d	25/01/24	31/01/24	100%
1.3.2.6	**Water and Electrical**	**166 d**	**17/08/23**	**29/01/24**	**86%**
1.3.2.6.1	**Ground Floor**	**147 d**	**17/08/23**	**10/01/24**	**100%**
1.3.2.6.1.1	Sanitarty Pipe Work	7 d	17/08/23	23/08/23	100%
1.3.2.6.1.2	Plumbing Work	7 d	22/12/23	28/12/23	100%
1.3.2.6.1.3	Electrical Pipe Work	7 d	17/08/23	23/08/23	100%
1.3.2.6.1.4	Power Distribution Board	7 d	22/12/23	28/12/23	100%
1.3.2.6.1.5	Cable Tray	7 d	20/08/23	26/08/23	100%
1.3.2.6.1.6	Electrical Cable/ Wiring	7 d	22/12/23	28/12/23	100%
1.3.2.6.1.7	Sanitary Fixer installation	7 d	04/01/24	10/01/24	100%
1.3.2.6.1.8	Electrical Switch Socket Fixing	3 d	08/01/24	10/01/24	100%
1.3.2.6.2	**1st Floor**	**91 d**	**16/10/23**	**14/01/24**	**100%**
1.3.2.6.2.1	Sanitarty Pipe Work	7 d	16/10/23	22/10/23	100%
1.3.2.6.2.2	Plumbing Work	7 d	29/12/23	04/01/24	100%
1.3.2.6.2.3	Electrical Pipe Work	7 d	29/12/23	04/01/24	100%
1.3.2.6.2.4	Power Distribution Board	3 d	05/01/24	07/01/24	100%
1.3.2.6.2.5	Cable Tray	7 d	01/01/24	07/01/24	100%
1.3.2.6.2.6	Electrical Cable/ Wiring	7 d	08/01/24	14/01/24	100%
1.3.2.6.2.7	Sanitary Fixer installation	1 d	05/01/24	05/01/24	100%
1.3.2.6.2.8	Electrical Switch Socket Fixing	2 d	04/01/24	05/01/24	100%
1.3.2.6.3	2nd Floor	15 d	15/01/24	29/01/24	0%
1.3.3	**Gate House**	**182 d**	**28/03/23**	**15/10/23**	**100%**
1.3.3.1	Pile Boring and Concreting-6 nos.	2 d	28/03/23	29/03/23	100%
1.3.3.2	Pile Integrity Test- 1 nos	3 d	17/04/23	19/04/23	100%
1.3.3.3	**Sub-structure**	**15 d**	**03/05/23**	**17/05/23**	**100%**
1.3.3.3.1	Pile Cap-6 nos	5 d	03/05/23	07/05/23	100%
1.3.3.3.2	Foundation Beam	10 d	08/05/23	17/05/23	100%
1.3.3.4	Brick Work	14 d	28/05/23	10/06/23	100%
1.3.3.5	Column	7 d	11/06/23	17/06/23	100%
1.3.3.6	Roof Slab	8 d	18/06/23	25/06/23	100%
1.3.3.7	**Plaster and Finishing Work**	**66 d**	**11/08/23**	**15/10/23**	**100%**
1.3.3.7.1	Door Frame Fixing	3 d	12/08/23	14/08/23	100%
1.3.3.7.2	Plaster Work	5 d	11/08/23	15/08/23	100%
1.3.3.7.3	Khoa-sand Cusion in Floor	3 d	14/08/23	16/08/23	100%
1.3.3.7.4	Floor Concreting	3 d	17/08/23	19/08/23	100%
1.3.3.7.5	Tiles Fitting	5 d	20/08/23	24/08/23	100%
1.3.3.7.6	Door shiutter and Window fixing	2 d	25/08/23	26/08/23	100%
1.3.3.7.7	Painting	7 d	09/10/23	15/10/23	100%
1.3.3.8	**Water and Electrical**	**15 d**	**12/08/23**	**26/08/23**	**100%**
1.3.3.8.1	Electrical Pipe Work	5 d	12/08/23	16/08/23	100%
1.3.3.8.2	Electrical Cable/wiring	2 d	23/08/23	24/08/23	100%
1.3.3.8.3	Electrical Switch Socket Fixing	2 d	25/08/23	26/08/23	100%
1.4	**General Leveling and Road Works**	**216 d**	**20/06/23**	**31/01/24**	**87%**
1.4.1	Sub-grade Compaction	120 d	20/06/23	03/01/24	100%
1.4.2	Sub-base-Car Road-400mm	90 d	06/08/23	10/01/24	100%

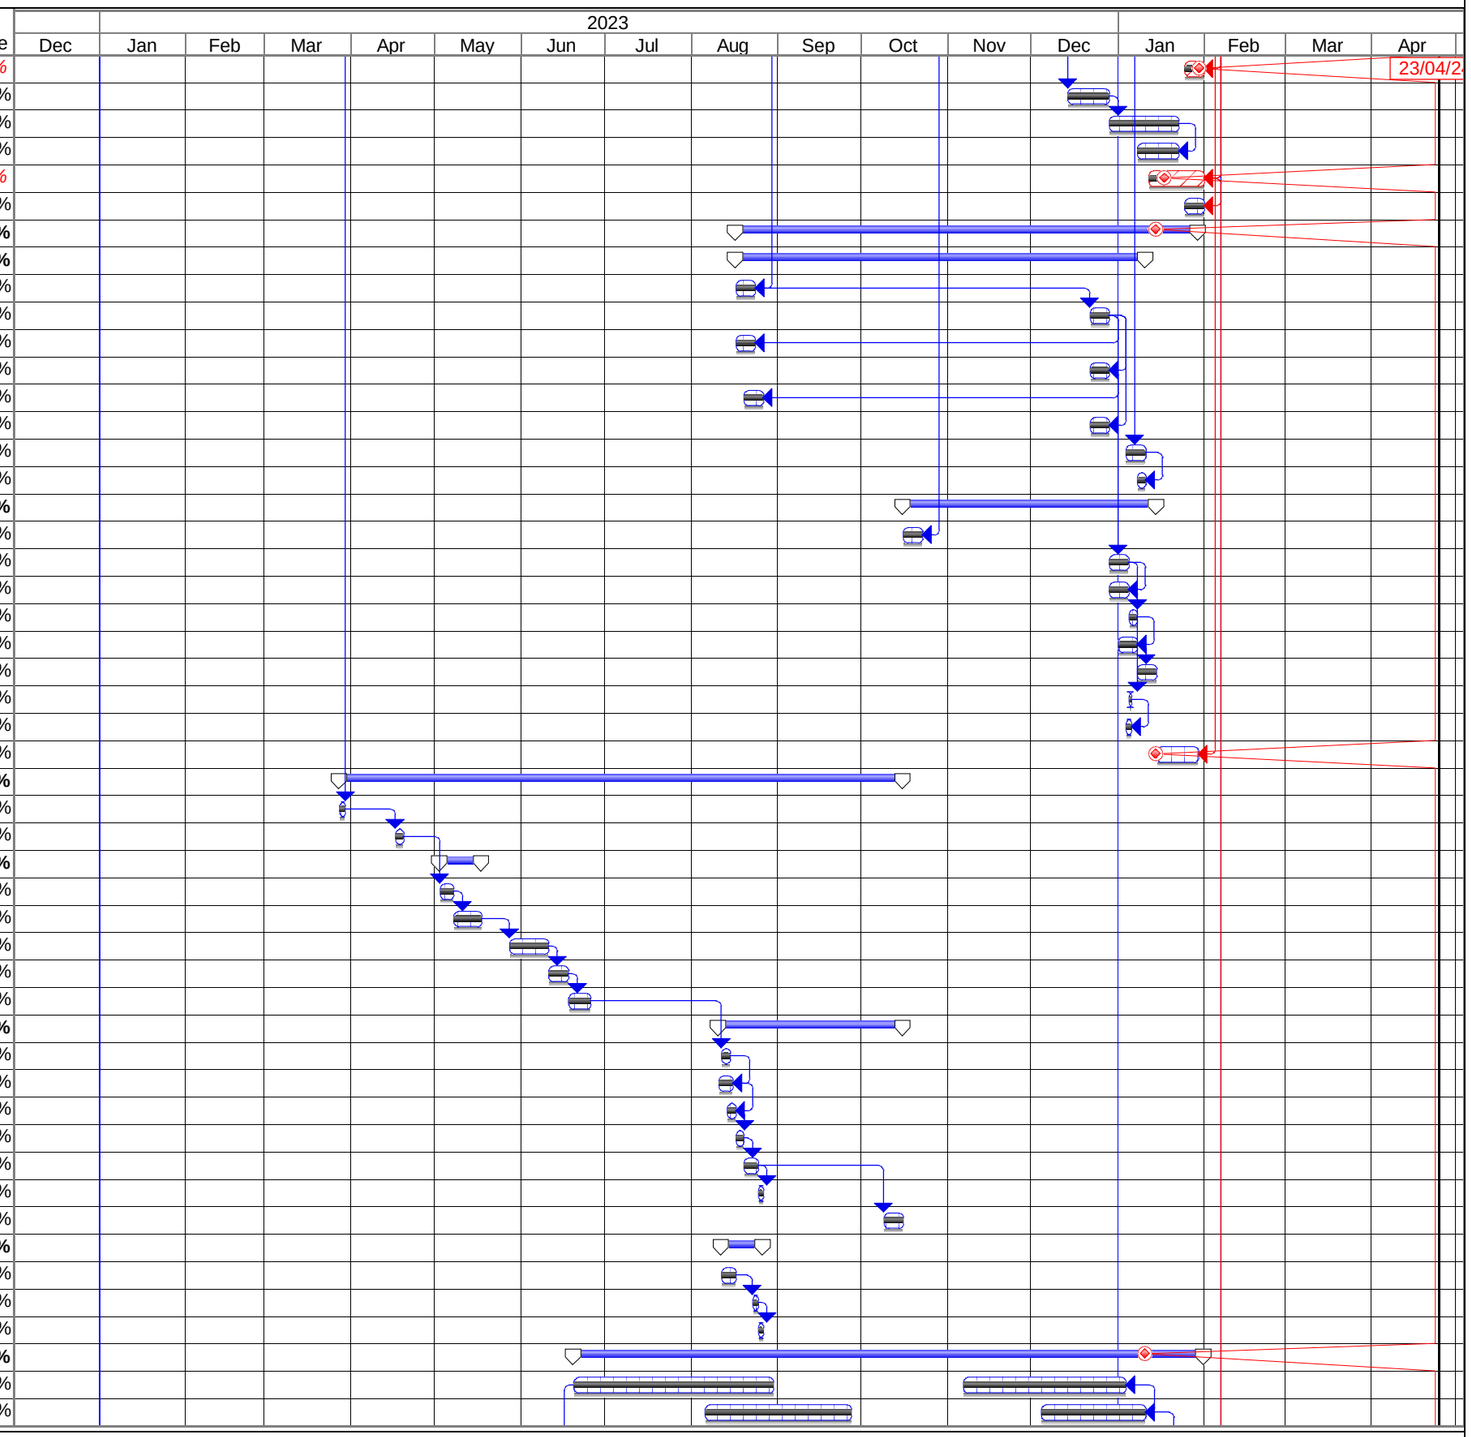

Date: 25/04/24 11:48
Sheet:4 /5

Task | Progress | Rolled Up Task | Rolled Up Progress | Group By Summary
Critical Task | Summary | Rolled Up Critical Task | Project Summary

Work Plan(Rev-2.0) and Progress for Construction of 150,000 Tons Livestock and Poultry Feed Factory in Bogura, Rajshahi, Bangladesh

WBS	Task Name	Duration	Start	Finish	% Complete
1.4.3	Sub-base Pedstrain	60 d	19/11/23	17/01/24	80%
1.4.4	RCC-Car Road	30 d	26/12/23	24/01/24	100%
1.4.5	*RCC-Pedstrain*	*30 d*	*02/01/24*	*31/01/24*	*0%*
1.5	**Water-Electricity-Outdoor Enigineering**	**188 d**	**11/07/23**	**14/01/24**	**100%**
1.5.1	Electrical-Power Cable	158 d	11/07/23	15/12/23	100%
1.5.2	Water Supply-PE Pipe	30 d	16/12/23	14/01/24	100%
1.5.3	Sewerage	30 d	16/12/23	14/01/24	100%
1.6	**Hydropower Installation-Production Area**	**110 d**	**11/10/23**	**28/01/24**	**64%**
1.6.1	Main Workshop	52 d	08/12/23	28/01/24	90%
1.6.2	Finished Product Ware House	42 d	18/12/23	28/01/24	90%
1.6.3	Boiler Room	52 d	08/12/23	28/01/24	0%
1.6.4	**Power Ditstribution Room (Sub-station)**	**110 d**	**11/10/23**	**28/01/24**	**85%**
1.6.4.1	Roof Slab-Elecrical Pipe work	2 d	11/10/23	13/10/23	100%
1.6.4.2	Wall-Electrical Pipe Work	7 d	16/12/23	23/12/23	100%
1.6.4.3	Electrical Cable/ Wiring	30 d	23/12/23	22/01/24	100%
1.6.4.4	Electrical Socket/ Switch Fixing	7 d	22/01/24	28/01/24	0%
1.7	*Handover*	*1 d*	*31/01/24*	*31/01/24*	*0%*

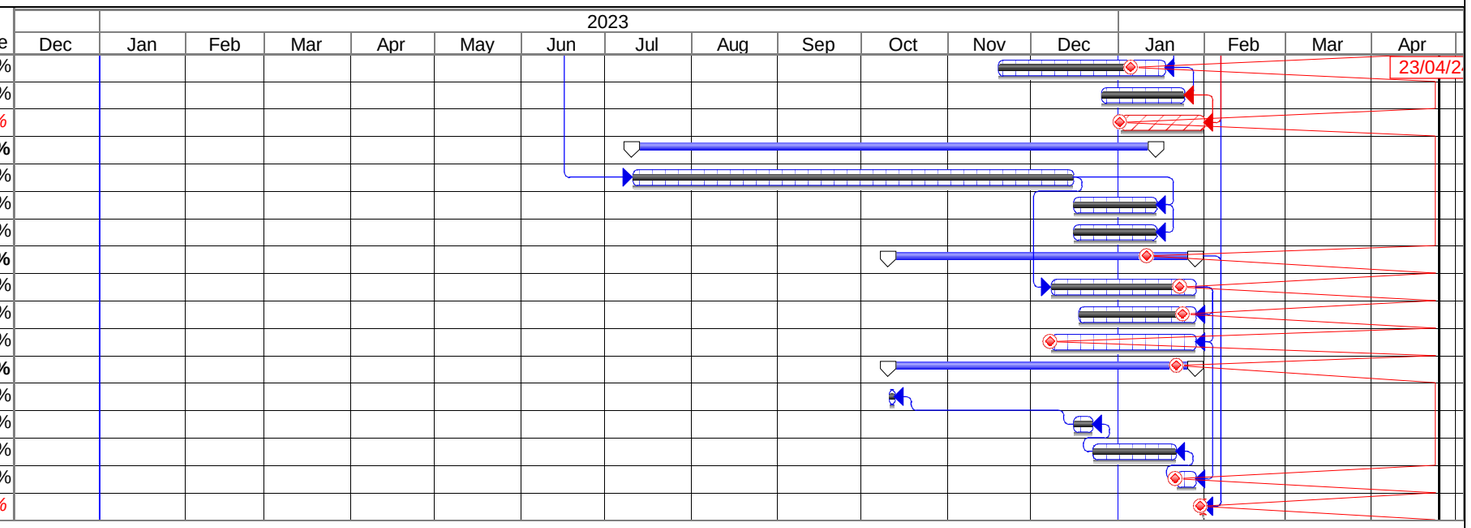

Date: 25/04/24 11:48
Sheet:5 /5

Task | Progress | Rolled Up Task | Rolled Up Progress | Group By Summary
Critical Task | Summary | Rolled Up Critical Task | Project Summary
